



IG PETROCHEMICALS LIMITED

Date: 1st Dec 2023

The Director
Ministry of Environment, Forest & Climate Change,
Indira Paryavaran Bhavan, Aliganj, Jorbagh Road,
New Delhi -110 003

Sub: Submission of Six Monthly Environmental Clearance Compliance Status Report.

Ref.: Environmental clearances granted for expansion of petrochemical unit, by
MoEF & CC vides clearance no.

- 1) PA-I EXPANSION EC NO-I-11013/14/2007-IA 11 (I) dated: 12th June, 2007.
- 2) PA-II EC NO -)-11012/78/96-IA dated 20thTune 1997.
- 3) PA-III & BENZOIC ACID EC NO-I-11011/994/2007/I A (11) I, Dated: 03.12.2009.
- 4) MA-III EC NO -I-11011/986/2007-IA -11(I) dated 2nd April 2008.
- 5) PA-IV,MA-IV,BENZOIC ACID EXPANSION-PLASTICIZER EC NO-I-1011/73/
2016- IA-II (I), Dated : 18th July, 2017 & amendment in same is received on 20th
February 2018.

Dear Sir,

With reference to the above we are submitting herewith our half yearly compliance status report as per condition stipulated in Environmental Clearance for period of Apr 2023 – Sept 2023. We hope the above is to your satisfaction.

Thanking You,
Yours faithfully


(Sagar Jadhav)

Chief - Manufacturing Operations



CC to:

1. The CCF, Regional Office, Western Region, Ministry of Environment, Forests & Climate Regional Office (WCZ), Ground Floor, East Wing, New Secretariat Building, Civil Lines, Nagpur-440001
2. The Member Secretary, Maharashtra Pollution Control Board, 3rd floor, Kalpataru Point, Sion, Mumbai -400 022.
3. Central Pollution Control Board, Parivesh Bhavan, Opp. VNC Ward office No. 10, Subhanpura, Vadodara-390023.

Ref	PA-I EXPANSION EC COMPLIANCE REPORT APR 2023 – SEPT 2023 EC No. J-11013/14/2007-IAII (I) dated 12.06.2007.
To	I G Petrochemicals Ltd, T-2, MIDC Talaja
Status	PLANT EXPANSION COMPLETED IN THE YEAR 2008

It is noted that the proposal is for capacity addition of 26,110 MTA of Phthalic Anhydride to the existing 90,000 TPA by change in catalyst on 'No- Increase in Pollution Load' basis. The technology for the plant has been supplied by Lurgi of Germany. The unit PA – I was installed in 1992 with a capacity of 45,000 MTA and PA – II was set up in 1997 with the same capacity. PA – II was undertaken after the Environmental Clearance from the ministry. The expansion capacity is due the proposed use of a new generation catalyst supplied by BASF of Germany which will increase the yield of product. For this purpose, PA- I will need de-bottlenecking while PA- II will be in a position to handle the extra load. The Maharashtra Pollution Control Board has issued Consent to Establish for the project on 16.09.2006. The cost of the project is Rs. 04.68 Crores.

This Environmental Clearance was obtained for debottlenecking of plant for capacity 26110 TPA. Consolidated Consent to Operate for existing Plant PA –I, PA – II and PA – III plant and PA – IV is obtained which is commissioned. Actual production details as per listed below:

Product	As per Environmental Clearances	As per Consent to Operate (2020)	Actual Production		Remarks
			APRIL 2022- MARCH 2023 full year	APRIL 2023- SEPTEMBER 2023 6 months	
Phthalic Anhydride	PAI+PAII90000 MTPA PAI EXP 26110 MTPA PAIII 53000	222110 MT/A	204554.350 MT	97756.400 MT	<ul style="list-style-type: none"> We are well within the prescribed limit of EC & Consent

	MTPA PA IV 53000 MTPA				
Benzoic Acid	1500 MT/A	1500 MT/A	816.830 MT	341.000 MT	
Maleic Anhydride	7660 MT/A	7660 MT/A	6904.225 MT	3322.300 MT	
Di Ethyl Phthalate	12600 MT/A	12600 MT/A	4678 MT	3251.671 MT	
Power (Exported to Grid)	2.5 MW	2.5 MW	NIL	NIL	

Compliance to the conditions stipulated under Environmental Clearance granted by the Ministry of Environment & Forest, Government of India vide letter No. J-11013/14/2007-IAII (I) dated 12.06.2007 is complied.

The project activity is listed at 5 (f) in the Schedule of the EIA Notification, 2006 and is of 'B' Category being in the industrial area and shall not require Public Hearing. Based on the information provided by you, the Ministry of Environment and Forest hereby accords environmental clearance to the above project under the provisions of EIA Notification dated 14th September 2006, subject to the compliance of the following Specific and Generation condition

OK. Above condition is noted.

A. Specific Conditions:	
i. Due to this proposed de-bottlenecking, there will be a reduction in the generation of pollutants. The air pollution load will be reducing from 375.6 kg/hr to 366.50 kg/hr for PA-I and from 398.3 kg/hr to 336.40 kg/hr for PA-II. This will reduce the TOC in the scrubber outlet as inlet load will be reduced. Total DM water usage will be reduced from 3816 m³/hr to 3600 m³/hr	We are regularly monitoring Air pollution through MoEF recognized laboratory. TOC monitoring reports for Apr 2023 – Sept 2023 are enclosed under ANNEXURE -II . We have also provided online monitoring system for stack emissions and effluent which is linked directly with CPCB /MPCB servers. REFER ANNEXURE XVI FOR OCEMS DASHBOARD.

	due to reduced organics levels in the off gases.	
ii.	The DM makeup water will further be reduced to 2348 m ³ /month from 2434 m ³ /month. The total effluent generation from both the plants will reduce from 2304 m ³ /month to 2088 m ³ /month.	Yes, Agreed. The total water consumption and effluent generation are under the consented quantities. Data on Actual Water Consumption & Waste Water Generation for Apr 2023 - Sept 2023 period is enclosed as ANNEXURE - III.
iii.	There will be no change in the quantity of distillate residue generated. It will be disposed off as per the authorization from MPCB.	Yes, Agreed. Data on Residue Generation Apr 2023 - Sept 2023 period is enclosed as ANNEXURE -IV.
iv.	There will be no increase in Storage tanks.	There was no additional storage tank installed for this project. Subsequently, new storage tanks have been installed with due permission from MoEF by getting subsequent EC's. Fix roof tanks are converted to Internal Floating Roof. EC No.J.11012/78/96-IA-II Dated 20th June 1997 of PA - II Plant expansion. EC No. J-11011/994/2007/I A (II) I dated: 03.12.2009 of PA -III plant expansion.
v.	All other conditions prescribed by Ministry at the time of expansion of PA- II will be prevail.	Yes six monthly reports for all ECs are being submitted regularly ANNEXURE -V.
vi.	Fugitive emissions, especially in the work zone shall be regularly monitored and records be maintained	Yes, Noted. Work zone monitoring reports for Apr 2023 - Sept 2023 period are enclosed under ANNEXURE - II
vii.	Raw material will be stored in covered	Major Raw Material is o-Xylene which is liquid

	yards. Water sprinkling arrangement should be made in the raw material stock yard to control fugitive emissions.	in nature. Stored in Storage tanks with sprinklers arrangement. The installation is CCoE approved. Fix roof tanks are converted to Internal Floating Roof tanks. Photographs showing designated storage area for storage of raw material: O-xylene are enclosed as ANNEXURE - VI.
viii.	Acoustic enclosure will be installed to limit the noise levels below 85 dBA.	Yes, Enclosures have been provided at various Noise Generating locations. Maximum Noise Level measured is 69.8 dBA in the month of Aug 2023. Monitoring Reports for the period Apr 2023 - Sept 2023 are enclosed as ANNEXURE - II
ix.	The company shall strictly follow all the relevant guidelines of CPCB given from time to time.	Complied.
x.	25% of the total land area will developed as green belt.	Adequate green belt has been developed .
xi.	The company shall harvest surface as well as rainwater from the rooftops of the building proposed in the expansion project and storm water drains to recharge the ground water and use the same water for the various activities of the project to conserve fresh water.	Yes, we have installed rainwater harvesting system and recover 20354 m3 of rain water during Apr 2023 to Sept 2023.
xii.	Occupational health surveillance program shall be undertaken as regular exercise for all the employees. The first aid facilities in the occupational health centre shall be strengthened and the medical records of	Regular medical check-ups of all the employees are conducted. Trained Male nurse is provided in all three shifts. We have appointed fulltime Doctor and have tie up with local hospitals to attend to

	<p>each employee shall be maintained separately.</p>	<p>medical emergencies. Please refer ANNEXURE - VIII.</p> <p>Company has well equipped Occupational Health center (OHC) with two beds located in its admin building.</p> <p>Company has a program of pre and post (periodic) medical checkups whereby all workers in hazardous operations are tested twice a year. The records are maintained in Form-7. ANNEXURE - VIII.</p>

B.	General Conditions:	
i.	<p>The project authority must strictly adhere to the stipulations made by the concerned State Pollution Control Board (SPCB) and State Government.</p>	<p>Yes agreed. We have received Consent to Operate from Maharashtra Pollution Control Board vide no. Format 1.0/CAC/UAN No. MPCB CONSENT - 0000115836/CR/2207000116 Dated: 02/07/2022, valid upto 31/08/2026. Copy of same is enclosed as ANNEXURE - XV.</p>
ii.	<p>No further expansion or modifications in the plant shall be carried out without prior approval of the Ministry of Environment and Forests.</p>	<p>Agreed. All subsequent expansions were carried out after obtaining Environmental Clearances from MOEF & CC.</p>
iii.	<p>Regular Ambient Air Quality Monitoring shall be carried out. The monitoring stations will be set up in consultation with the SPCB. At least four Ambient air quality monitoring stations shall be established in the downward direction as well as where maximum ground level concentration of</p>	<p>We are regularly monitoring Ambient Air Quality through MoEF & CC recognized laboratory. Ambient Air Quality monitoring stations are set up as per guidelines of SPCB. Same are undertaken at industry premises. Ambient Air Monitoring Reports for Apr 2023 - Sept 2023 period are enclosed as</p>

	SPM, SO ₂ and NO _x are anticipated in consultation with the SPCB. It will be ensured that at least one monitoring station is set up in up-wind & down-wind direction along with those in other directions. On-line data for air emissions shall be transferred to the CPCB and SPCB once in six months. The instruments used for ambient air quality monitoring shall be calibrated regularly.	ANNEXURE - II .
iv.	Adequate number of influent and effluent quality monitoring stations shall be set up in consultation with the SPCB. Regular monitoring shall be carried out for relevant parameters.	We are regularly monitoring effluent quality through MoEF recognized laboratory. Effluent monitored at intermediate stages of ETP. Inlet / Outlet of ETP monitoring Reports for the period Apr 2023 - Sept 2023 are enclosed under ANNEXURE - II We have also provided online monitoring system for effluent which is linked directly with CPCB /MPCB server for effluent. REFER ANNEXURE - XVI FOR OCEMS DASHBOARD.
v.	Industrial waste water shall be properly collected and treated so as to conform to the standards prescribed under GSR 422 (E) dated 19 th May 1993 and 31 st December, 1993 or as amended from time to time. The treated wastewater shall be utilized for plantation purpose.	Analysis being done as per MPCB consent norms and has been extended to cover all parameters as per GSR 422 (E). Reports for the period Apr 2023 - Sept 2023 are enclosed under ANNEXURE - II
vi.	The overall noise levels in and around the plant area shall be limited within the prescribed standards (85 dBA) by providing noise control measures including acoustic hoods, silencers, enclosures etc. on	Yes, above condition is complied with. We have provided enclosures, hood etc. to ensure noise level is under control. Regular ambient Noise monitoring is carried out within the unit and at fence level. All high noise generating

	all sources of noise generation.	sources are enclosed. Regular Noise Level monitoring undertaken. Maximum Noise Level measured is 69.8 dBA in the month of Aug 2023. Reports for the period Apr 2023 – Sept 2023 are enclosed as ANNEXURE - II showing compliance.
vii.	Proper House Keeping and adequate occupational health programs shall be taken up. Regular Occupational Health Surveillance Programme for the employees and contract workers shall be carried as per the Factories Act and records shall be maintained properly for at least 30-40 years.	Trained Male nurse is provided in all three shifts. We have appointed fulltime Doctor and have tie up with local hospitals to attend to medical emergencies. Please refer Company has well equipped Occupational Health center (OHC) with two beds located in its admin building. Company has a program of pre and post (periodic) medical checkups whereby all workers in hazardous operations are tested twice a year. The records are maintained in Form-7. ANNEXURE - VIII.
viii.	A separate environment management cell with full fledge laboratory facilities to carry out various management and monitoring functions shall be set up under the control of a Senior Executive.	Separate Environment Management Team under HoD – Health, Safety & Environment (Master in Environment Management -M.E.M from SIBER Institute, ADIS, CDM) has been formed. Separate Environment Laboratory for monitoring ETP performance has been established. Technical guidance shall be provided by President (Production & Technical Services). Necessary sampling & analysis is conducted by MoEF & CC approved laboratories.
ix.	Separate funds will be earmarked for the environmental protection measures and shall be used judiciously used to implement	Yes, we have provided separate funds for Environmental Protection Measures and we affirm that same will not be diverted for any

	the conditions stipulated by the Ministry of Environment and Forests as well as the State Government. The funds so provided shall not be diverted for any other purpose.	other purpose, Budget for Environment Protection is enclosed as ANNEXURE - IX
x.	Concerned Regional Office of this Ministry / SPCB / Central Pollution Control Board shall monitor the implementation of the stipulated conditions. Six monthly compliance status report and monitoring data along with statistical interpretation shall be submitted to them regularly.	Yes, we are regularly submitting six monthly compliance report to the ministry / SPCB / CPCB. Please refer ANNEXURE - V for last submitted six monthly compliance report.
xi.	The project proponent should advertise in at least two local newspapers widely circulated in the region around the project, one of which shall be in the vernacular language of the locality concerned informing that the project has been accorded environmental clearance by the Ministry and copies of the clearance letter are available with the State Pollution Control Board / Committee and may also be seen at Website of the Ministry and Forests at http://envfor.nic.in. The advertisement should be made within 7 days from the date of issue of the clearance letter and copy of the same should be forwarded to the Ministry's Regional Office at Bhopal.	Yes, we had advertised in two local newspapers in vernacular language's such as Marathi at Navshakti & in English at Free Press Journal. Copy of advertisement is enclosed as ANNEXURE - X .
xii.	The project authority shall inform the Regional Office as well as the Ministry the date of financial closure and final approval of the project by the concerned authorities	Yes, complied. MPCB CTO No. BO/RO-NM/PCI-I/1208-08/0/CC-193 dated 22 nd Dec 2008 is available. This was expansion project.

	and the date of start of land development work.	
	The Ministry may revoke or suspend the clearance, if implementation of any of the above conditions is not satisfactory.	Yes, Agreed.
	The Ministry reserves the right to stipulate additional conditions if found necessary. The company will implement these conditions in a time bound manner.	Yes. Noted.

Ref	PA-II EC COMPLIANCE REPORT APR 2023 – SEPT 2023 EC No.J.11012/78/96-IA-II Dated 20 th June 1997
To	IG Petrochemicals Ltd, T-2, MIDC Talaja
For	Manufacture of Products like Phthalic Anhydride, Benzoic Acid and Power.
Status	PA-II PROJECT WAS COMPLETED AND COMISSIONED IN YEAR 1998.

	EC Condition	status
i.	The project authorities must strictly adhere to the stipulations made by Maharashtra State Pollution Control Board and the state Government.	Consent to Operate /Authorization from MPCB has been obtained. Format 1.0/CAC/UAN No. MPCB CONSENT - 0000115836/CR/2207000116 Dated: 02/07/2022, valid upto 31/08/2026. Copy of same is enclosed as ANNEXURE – XV .
ii.	No further expansion or modifications in the plant shall be carried out without prior approval of the Ministry of Environment and Forests.	Yes, agreed. For further expansion (installation of new plants of Phthalic Anhydride/Maleic Anhydride/benzoic acid) we have received EC No J-11011/73/2016-IA-II(I) dated 14 th Mar 2022.
iii.	The gaseous emission from the various process units should adhere to the air emission standards specified in Part D, Schedule VI of Environmental (Protection) Second amendment and Rules, 1993. For boiler stack the EPA norms as per Notification dated 27 th February, 1996 should be complied. In case the standards stipulated	Regular stack / vent monitoring is being carried out through MoEF recognized lab. Refer Annexure – II . We have also provided online monitoring system which is linked directly with CPCB /MPCB server for stack emissions as well as effluent. REFER ANNEXURE XVI FOR OCEMS DASHBOARD

	<p>by SPCB are more stringent than the EPA norms, the industry should follow the above. At no time the emission should go beyond the prescribed standards. In the event of failure of any pollution control system adopted by the unit the respective unit should <i>be</i> immediately put out of operation and should not be restarted until the control measures are rectified to achieve the desired efficiency.</p>	
<p>iv.</p>	<p>Ambient- Air quality monitoring stations should be set up in the downwind direction as well as at location- where maximum ground level concentrations are anticipated. These locations should be fixed in consultation with the State Pollution Control Board. The number of air quality monitoring stations and frequency of monitoring should be selected on the basis of mathematical modelling to represent short term ground level concentrations, - human settlements, sensitive targets etc.</p> <p>Stack emissions from the process and boilers and incinerator should be monitored for SO₂, NO_x and SPM and record maintained. It is observed that SO₂ concentration in the ambient air is 64 micrograms per cubic meters. This along with emission from the plant is expected to exceed ambient air quality standards.</p> <p>In view of the above, project proponent should provide necessary enhancement/changes in stack design to ensure that SO₂ level in the ambient air. is maintained within the stipulated norms.</p> <p>Data on ambient air quality and stack emission from boiler should be submitted to this Ministry once in six months along with the statistical analysis and interpretation.</p>	<p>Yes, the ambient air quality monitoring is carried out regularly in existing plants and same practice will be continued in future.</p> <p>REFER ANNEXURE II</p> <p>Regular stack / vent monitoring is being carried out through MoEF recognized laboratory. REFER ANNEXURE II We have also provided online monitoring system which is linked directly with CPCB /MPCB server for stack emissions as well as effluent.</p> <p>REFER ANNEXURE XVI FOR OCEMS DASHBOARD</p> <p>The ambient air quality data is submitted along with 6 monthly EC compliance report.</p> <p>REFER ANNEXURE II</p>

v.	Storage of solvents should be in accordance with the prescribed safety norms. Fugitive emissions should be prescribed safety norms. Fugitive emissions should be controlled, regularly monitored and data recorded. The monitored data should be submitted to this Ministry once in 6 months for review	Major Raw Material is o-Xylene which is liquid in nature. Stored in Storage Tanks with sprinklers arrangement. Fix roof tanks are converted to Internal Floating Roof. The installation is approved by CCOE. Photographs showing designated storage area for storage of raw material o-Xylene are enclosed as ANNEXURE - VI. There was no additional storage tank installed for this project. Subsequently, new storage tanks have been installed with due permission from MoEF by getting subsequent EC's. EC No. J-11011/994/2007/I A (II) I dated: 03.12.2009 of PA -III plant expansion. Refer ANNEXURE - II - Fugitive emission monitoring.
vi.	The existing ETP facilities should be upgraded by providing tertiary treatment facilities to ensure that the existing discharges meet the norms stipulated by the SPCB/MINAS. Further, as indicated in the BMP, a new ETP should be provided to treat the additional effluent load after the expansion. The treated effluent should meet the norms prescribed norms under Gazette Notification dated 2.4.96 Specifically BOD (3 days at 27 C) shall be 30 mg/l if discharged directly to a freshwater body. Bioassay test must be carried out to meet 90% survival after 96 hrs. in 100% effluent. Test shall be carried out as per ist6582-197i. in case the treated effluent is proposed to be disposed into the CETP proposed at MIDC, adequate treatment facility should be provided to meet the CETP norms notified under the Environment (Protection) Rules, 1986.	The ETP plant was revamped in the years 1998 (incorporating tertiary treatment) and also subsequently in the year 2013 to treat the additional load from the expansion before commissioning the Phase III plant. Bioassay test is already carried out on our effluent through MOEF recognized third party. Company is already a Member of CETP. Effluent after treatment is disposed to CETP as per MPCB norms as specified in CTO. The note on revamping of ETP is enclosed as ANNEXURE - XI. Upgradation of ETP has been completed incorporating RO & MEE to recycle total effluent which will be generated from expansion. In addition, part of the effluent from existing plant will also be recycled. We have reduced effluent discharge from 686

		m ³ /day to 220 m ³ /day as stipulated in expansion CTO. Attached are few photographs ETP, RO & MEE. ANNEXURE - XXV
vii.	Regular effluent quality monitoring should be carried out on a 24-hour log and record instrumentation system and the monitored data along with the statistical analysis and interpretation should be submitted to this Ministry once in six months and to the State Pollution Control Board once in 3 months.	We have online emission and effluent monitoring system connected to CPCB and MPCB servers .Ref ANNEXURE XVI .
viii	Guard ponds of sufficient holding capacity should be provided to cope with the effluent discharge -during the process disturbances. In the event of 'failure or nonfunctioning of the ETP, the respective units should be immediately put out of operation and should not be restarted until the control measures are rectified to achieve the desired efficiency.	Holding tanks with total capacity 880 m ³ for incoming effluent and 400 m ³ treated effluent are provided as buffer for any upstream/downstream disturbances. These tanks are RCC tanks(with lining of Acid/alkali proof tile for acidic effluents)
ix	The guard pond should be provided with impervious. lining and stability of the ponds with respect to leakages/cracks and other factors should be ensured	These tanks are RCC tanks with lining of Acid/alkali proof tile lining. The lining is checked and pointing & other repairs if required is done as preventive maintenance.
x	Adequate number of influent and effluent. Quality monitoring stations should be set up in consultation with the State Pollution Control Board	We have online effluent monitoring system connected to CPCB and MPCB servers. Ref ANNEXURE XVI . Regular in plant analysis of various streams of ETP are done in the laboratory.
xii	The hazardous wastes should be handled as per the Hazardous Wastes (Management and Handling) rules of	We are complying the hazardous waste management rules .

	the environment (Protection) Act, 1989	
xiii	Handling, manufacturing storage and transport of hazardous chemicals should be in accordance with the Manufacture, Storage and Import of Hazardous Chemicals Rules, 1989	Complied
xiv	On-site and off-site Emergency Plan as required under the Rules 13 and 14 of the Manufacture, Storage and Import of the Hazardous Chemicals Rules, 1989 should be prepared and approval from the competent authority should be obtained.	We have the onsite and off-site emergency plan which is submitted to DISH (factory inspectorate) .
xvi	A green belt of adequate width and density should be raised all around the proposed unit and township. Native plant species should be selected for this purpose in consultation with the local DFO. A norm of about 1500-2000 plants per ha. may be followed.	Adequate green belt has been developed within the plot.
xvii	Periodical medical checkup of the workers should be done and records maintained as a measure to provide occupational health service to the workers.	Regular medical check-ups of all the employees are conducted. Trained Male nurse is provided in all three shifts. We have appointed fulltime Doctor and have tie up with local hospitals to attend to medical emergencies. Please refer Company has well equipped Occupational Health center (OHC) with two beds located in its admin building. Company has a program of pre and post (periodic) medical checkups whereby all workers in hazardous operations are tested twice a year. The records are maintained in Form-7. ANNEXURE - VIII.
xviii	The project authorities should set up laboratory facilities for collection, analysis of samples under the supervision of competent technical	Separate Environment Laboratory for monitoring ETP performance has been established. Technical guidance shall be

	personnel who will report to the Chief Executive.	provided by President (Production & Technical Services). Necessary sampling & analysis is conducted by MoEF & CC approved laboratories.
xix	A separate environment management cell with suitably qualified people to carry out various functions should be set up under the control of senior executive who will report directly to the Head of the Organization.	Separate Environment Management Team under HoD – Health, Safety & Environment (Master in Environment Management -M.E.M from SIBER Institute, ADIS, CDM) has been formed. Separate Environment Laboratory for monitoring ETP performance has been established. Technical guidance shall be provided by President (Production & Technical Services). Necessary sampling & analysis is conducted by MoEF & CC approved laboratories.
xx	The funds earmarked for the environmental protection measures should not be diverted for any other purpose and year wise expenditure should be reported to this Ministry and to the State Pollution Control Board under the Rules prescribed for environmental audit.	Yes, we have provided separate funds for Environmental Protection Measures and we affirm that same will not be diverted for any other purpose, Budget for Environment Protection is enclosed as ANNEXURE – IX.

Ref	PA III EC COMPLIANCE REPORT APR 2023 - SEPT 2023 EC No. J-11011/994/2007/I A (II) I dated: 03.12.2009
To	I.G. Petrochemicals Ltd, T-2, MIDC Talaja
Status	Project completed in the year 2013.

It is noted that M/s. IG Petrochemicals Limited have proposed to increase the manufacturing capacity of existing petrochemicals complex. The unit is located at MIDC, Talaja in District Raigad in Maharashtra. It is proposed to set up Phthalic Anhydride plant with capacity of 53,000 TPA, recovery of 1000 TPA of benzoic acid and generation of 2.5 MW power for its own use and export to state Electricity Board Grid. The phthalic anhydride will be recovered in switch condensers. The existing area of the plant is 20,491 m² and additional area of 2522 m² is proposed for the expansion project. Cost of the project is Rs. 148 crores.

The project has been completed in the year 2013.

Compliance to the conditions stipulated under Environmental Clearance granted by the Ministry of Environment & Forest, Government of India vide letter No. J-11011/994/2007/I A dated 03.12.2009.

It is noted that water requirement will increase from 2615 m³/day to 4117 m³/day which will be met from the MIDC supply. About 651 m³/day of effluent will be generated. The effluent after primary, secondary and tertiary treatment will be discharged to CETP, Talaja. Process emissions in the form of HCL and TOC will be controlled through scrubbers. Stack height of 55m is provided for boilers for dispersion of gaseous emissions. Stack height of 31m is provided for heaters and 30m for the DG sets.

The water requirements and effluent generation are within stipulated limits. **REFER ANNEX III** for water consumption and effluent generated during period Oct 2022 – Mar 2023. The effluent after primary, secondary & tertiary treatment is discharged to CETP, Talaja. Scrubbers have been provided for process emissions. The stack emissions are being monitored through OCEMS which is connected to CPCB/MPCB servers. Requisite stack heights have been provided.

A. SPECIFIC CONDITIONS:	
i)	The Company shall install full-fledged ETP to treat the process effluent and treated effluent after primary, secondary and tertiary treatment and confirming to the prescribed standards shall be sent to CETP for further treatment. The company shall construct a guard pond for treated effluent and shall carry out the bioassay test by collecting the treated effluent into guard pond before discharging into CETP. The reports shall be submitted to CPCB and Ministry's Regional Office at Bhopal.
	The existing ETP plant was revamped in 2013 to treat the additional load from the expansion before commissioning the Phase III plant. Holding tanks with total capacity 880 m ³ for incoming effluent and 400 m ³ treated effluent are provided in ETP. Bioassay test is already carried out on our effluent through MoEF recognized third party. Company is already a Member of CETP and all effluents shall be disposed to CETP. The note on revamping of ETP is enclosed as ANNEXURE - XI . We have continuous online effluent monitoring system (BOD, COD, pH, TSS) connected to CPCB

		and MPCB servers. Ref ANNEXURE XVI . We have further upgraded ETP by incorporating RO and MEE to recycle total effluent generated from ongoing expansion and also recycling part of the existing effluent, thus bringing consented effluent discharge from 686 m ³ /day to 220 m ³ /day. Ref ANNEXURE-XXV for details of upgradation.
ii)	Process emissions in the form of HCl and TOC shall be controlled by installation of scrubbers. The company shall provide the monitoring arrangements with stack and regular monitoring shall be carried out and reports submitted to the SPCB, CPCB and Ministry's Regional Office at Bhopal. The gaseous emissions from the DG sets shall be dispersed through stack of adequate height as per CPCB / state pollution Control Board standards.	Process emissions are controlled by three stage scrubbers. Provision for sampling port hole and monitoring is being done. Scrubber is installed for scrubbing HCL vapors from storage tanks and day tanks. DG sets are provided with stack height of 15 & 30 m above roof, which is as per the Consent granted to our unit. Regular monitoring is carried out through MoEF & CC recognized laboratory. All stacks emission parameters are connected via OCEMS to CPCB and MPCB servers. Refer ANNEXURE XVI for snapshots of OCEMS Dashboards.
iii)	The proponent shall upload the status of compliance of the stipulated environmental clearance conditions, including results of monitored data on their Website and shall update the same periodically. It shall simultaneously be sent to the Regional Office of MoEF, the respective Zonal office of CPCB and State Pollution Control Board. The Pollutant levels namely, SPM, RSPM, SO₂, NO_x & CO (ambient levels as well as stack emissions) shall be monitored and displayed at a convenient location near the main gate of the company in the public domain.	We are uploading compliance reports on our company web site (http://www.igpetro.com/quality#main-content). We are submitting 6 monthly compliances to various authorities as stipulated. We are regularly monitoring ambient air quality and stack emissions from various stacks. Display Board as specified by Honorable Supreme Court is put up at our Gate. Please refer ANNEXURE - XII & ANNEXURE XXII .
iv)	Fugitive emission in the work zone environment, product, raw material storage area shall be regularly monitored. The emissions shall conform to the limits imposed by SPCB.	We monitor the fugitive emissions at work place/shop floor as desired. The monitoring of work zone is carried out regularly. Please refer ANNEXURE - II .
v)	The company shall explore the possibility of sending the spent carbon	Spent carbon is generated from ETP tertiary treatment process & DEP Plant, thus unsuitable

	and bio sludge to the cement plants or spent carbon should be incinerated.	for burning in cement plants. There is no Cement plant in 500 km distance from our unit. Hence, we shall dispose this in CHWTSDF Taloja (As per CTO) which is located in 2 km distance from our unit. Copy of MWML Membership Certificate is enclosed as ANNEXURE - XIII & Copy of Hazardous Waste Return submitted in form - IV for 2021 - 2022 is enclosed as ANNEXURE - XIV .
vi)	The project authorities shall strictly comply with the rules and guidelines under Manufacture, Storage and Import of Hazardous Chemicals, 1989 as amended in October, 1994 and January, 2000 and Hazardous Waste (Management, Handling & Transboundary Movement) Rules, 2008, as amended from time to time. Authorization from the SPCB shall be obtained for collection, treatment, storage and disposal of hazardous wastes. All Transportation of Hazardous Chemicals shall be as per the MVA, 1989.	We shall abide by this strictly. The site details are submitted to the DISH as they are the prescribed authority under the MSIHC Rules. Consent To Operate / Authorization from MPCB for PA -I, PA - II, PA - III and PA - IV plant is obtained with vide No. Format 1.0/CAC/UAN No. MPCB CONSENT - 0000115836/CR/2207000116 Dated: 02/07/2022, valid upto 31/08/2026. (ANNEXURE - XV) . We shall abide by the conditions of the Authorization. All hazardous chemicals/wastes are transported as per MVA, 1989 and through approved transporters of MPCB.
vii)	The project authority shall obtain the membership of TSDF for disposal of solid and hazardous waste and copy of the same shall be submitted to the Ministry and Ministry's Regional Office at Bhopal. The company shall maintain the valid membership.	Yes, complied. We have membership with CHWTSDF at Taloja and regularly disposing off our hazardous waste. . Copy of the membership certificate enclosed as ANNEXURE - XIII .
viii)	The company shall develop in land area of 35685 sq. ft, as per the CPCB guidelines to mitigate the effect of fugitive emissions.	Adequate green belt has been developed.
ix)	Occupational health surveillance of the workers shall be done on a regular basis and records maintained as per the Factories Act.	Regular medical check-ups of all the employees are conducted. Trained Male nurse is provided in all three shifts. We have appointed fulltime Doctor and have tie up with local hospitals to attend to medical emergencies.

		<p>Company has well equipped Occupational Health center (OHC) with two beds located in its admin building.</p> <p>Company has a program of pre and post (periodic) medical checkups whereby all workers in hazardous operations are tested twice a year. The records are maintained in Form-7.</p> <p>Please refer ANNEXURE - VIII.</p>
x)	The company shall make the arrangement for protection of possible fire hazards during manufacturing process in material handling.	Complied- entire plant is covered by a hydrant system, which is provided with separate fire water reservoir and emergency pumps (diesel operated). Fire extinguishers are kept in various parts of the plant depending upon type of fire hazard likely.
xi)	The company shall comply with the recommendations made in the EIA/EMP and Risk Assessment Report	We are abiding by the recommendations in the EIA/EMP and Risk assessment study.
	B. GENERAL CONDITIONS:	
i)	The project authorities shall strictly adhere to the stipulations made by the State Pollution Control Board.	Amalgamated Consent to Operate /Authorization from MPCB is obtained has been obtained with vide No. Format 1.0/CAC/UAN No. MPCB CONSENT - 0000115836/CR/2207000116 Dated: 02/07/2022, valid upto 31/08/2026. (ANNEXURE - XV) . We shall abide by the conditions of the Consent /Authorization and other stipulations.
ii)	No further expansion or modifications in the plant shall be carried out without prior approval of the Ministry of Environment & Forests. In case of deviations or alternations in the project proposal from those submitted to this \Ministry for clearance, a fresh reference shall be made to the Ministry to assess the adequacy of conditions imposed and to add additional environmental protection measures required, if any.	Yes, agreed.
iii)	At no time, the emissions shall exceed the prescribed limits. In the event of failure of pollution control system(s)	Yes, agreed.

	adopted by the unit, the respective unit shall not be restarted until the control measures are rectified to achieve the desired efficiency.	
iv)	The gaseous emissions (NO _x , SO ₂ and SPM) and Particulate matter along with RSPM levels from various process units shall conform to the standards prescribed by the concerned authorities from time to time. At no time, the emissions level shall go beyond the stipulated standards. In the event of failure of pollution control system(s) adopted by the unit, the respective unit shall not be restarted until the control measures are rectified to achieve the desired efficiency. Stack monitoring for SO ₂ , NO _x and SPM shall be carried.	Regular stack / vent monitoring is being carried out through MoEF recognized laboratory. We have also installed Online Continuous Environment Monitoring System which is linked directly with CPCB /MPCB servers for stack emissions as well as effluent. REFER ANNEXURE XVI FOR OCEMS DASHBOARD.
iv)	The locations of ambient air quality monitoring stations shall be decided in consultation with the State Pollution Control Board (SPCB) and it shall be ensured that at least one station is installed in the up wind and down wind directions as well as where maximum ground level concentrations are anticipated.	Yes, the ambient air quality monitoring is carried out regularly & will be continued. REFER ANNEXURE II
v)	The overall noise levels in and around the plant area shall kept well within the standards by providing noise control measures including acoustic hoods, silencers, enclosures etc. on all sources of noise generation. The ambient noise levels shall conform to the standards prescribed under Environment (Protection) Act, 1986 Rules 1989 viz. 75 dBA (day Time) and 70 dBA (night time).	Ambient and work place Noise level monitoring is carried out regularly in plants and same practice will be continued in future. We have taken all control measures as stipulated to control noise. Maximum Noise Level measured is 69.8 dBA in the month of Aug 2023. REFER ANNEXURE II
vii)	The project proponent shall also comply with all the environmental protection measures and safeguards proposed in the project report submitted to the Ministry. All the recommendations made	Yes agreed.

	in respect of environmental management & risk mitigation measures relating to the project shall be implemented.	
viii)	The company will undertake all relevant measures for improving the Socio-economic conditions of the surrounding area. CSR activities will be undertaken by involving local villages and administration.	Company is undertaking various community welfare measure for improvement of the environment as under: Refer ANNEX XVIII for details
ix)	The company shall undertake eco-development measures including community welfare measures in the project area for the overall improvement of the environment.	Company is undertaking various community welfare measure for improvement of the environment as under: Refer ANNEX XVII & XXVI for details
x)	A separate Environmental Management Cell equipped with full fledged laboratory facilities shall be set up to carry out the Environmental Management and Monitoring functions.	Separate Environment Management Team under HoD – Health, Safety & Environment (Master in Environment Management -M.E.M from SIBER Institute. ADIS, CDM) has been formed. Separate Environment Laboratory for monitoring ETP performance has been established. Technical guidance shall be provided by President (Production & Technical Services). Necessary sampling & analysis is conducted by MoEF & CC approved laboratories.
xi)	The project authorities shall earmark adequate funds to implement the conditions stipulated by the Ministry of Environment & Forests as well as the State Government along with the implementation schedule for all the conditions stipulated herein. The funds so provided shall not be diverted for any other purpose.	Budget for Environment Protection as stipulated in the EIA has been used for environmental protection in expansion project.
xii)	The implementation of the project vis-vis environmental action plans shall be monitored by the concerned Regional Office of the Ministry / SPCB / CPCB. A six monthly compliance status report shall be submitted to monitoring agencies and shall be posted on the website of the	Yes- being done regularly. Refer Annexure – V.

	company.	
xiii)	A copy of the clearance letter shall be sent by the proponent to concerned Panchyat, Zila Parishad / Municipal Corporation, Urban Local body and local NGO, if any from whom suggestions / representations, if any were received while processing the proposal.	Yes -submitted to Ghot Grampanchayat & Municipal Corporation. Refer Annexure - XXIII.
xiv)	The project proponent shall also submit six monthly reports on the status of compliance of conditions stipulated E C conditions including results of monitored data (both in hard copies as well as by email) to the respective Regional Office of MoEF, the respective Zonal Office of CPCB and State Pollution Control Board.	Yes, six monthly reports are being submitted regularly. For Last submitted report refer ANNEXURE V
xv)	The project proponent shall inform the public that the project has been accorded environmental clearance by the Ministry and copies of the clearance letter are available with State Pollution Control Board / Committee and may also be seen at Website of the Ministry and Forests at http://envfor.nic.in . This shall be advertise within seven days from the date of issue of the clearance letter, at least two local Newspapers widely circulated in the region around the project, one of which shall be in the vernacular language of the locality concerned and copy of the same should be forwarded to the Ministry's Regional Office of the Ministry.	Complied- advertisement was placed in media on obtaining the Environmental clearance. Refers ANNEXURE X
xvi)	The project authorities shall inform the Regional Office as well as the Ministry, the date of financial closure and final approval of the project by the concerned authorities and the date of start of construction.	The implementation of Phase IV PA, MA & Benzoic plants are done. Benzoic acid recovery project which envisages recovery of benzoic acid from residue and waste water is installed and commissioned - Consent to Operate copy attached. Format 1.0/CAC/UAN No. MPCB CONSENT - 0000115836/CR/2207000116 Dated: 02/07/2022, valid upto 31/08/2026.

		(ANNEXURE - XV).
7)	The Ministry may revoke or suspend the clearance, if implementation of any of the above conditions is not satisfactory	Yes, above condition is noted.
8)	The Ministry reserves the right to stipulate additional conditions. If found necessary. The company is a time bound manner implements these conditions.	Yes, above condition is noted.
9)	Any appeal against this environmental clearance shall lie with the National Appellate Authority, if proffered within a period of 30 days as prescribed under section 11 of the National Environment Appellate Authority Act, 1997.	Yes, Noted.
10)	The above conditions will be enforced, inter-alia under the provisions of the water (Prevention & Control of Pollution) Act, 1974, Air (Prevention & Control of pollution) Act, 1981, The Environment Protection Act 1986, Hazardous Waste (Management & Handling) Rules, 2003/2008 and Public Liability Insurance Act, 1991 along with their amendments and rules.	Yes, Noted.

Ref	EC COMPLIANCE FOR THE PERIOD APR 2023 - SEPT 2023 Maleic Anhydride (REVAMPING OF EXISTING MA-I AND MA-II PLANTS) EC No. J-11011/986/2007-IAII (I) dated 02/04/2008
	EC No. J-11011/986/2007-IA II (I) dated 02/04/2008 was obtained by Mysore Petrochemicals Ltd, T-1, MIDC Taloja for expansion of Maleic Anhydride plant capacity from 5400 TPA to 6500TPA. This unit of Mysore Petrochemicals was sold to sister company IG Petrochemicals Ltd ,T-2, MIDC ,Taloja with effect from April 2017 and is amalgamated with I G Petrochemicals .
Status	PLANT EXPANSION COMPLETED IN THE YEAR 2013.

This Environmental Clearance was obtained for enhancing of plant for capacity of Maleic Anhydride from 5400 TPA to 6500TPA. Consolidated Consent to Operate for the amalgamated unit (IG Petrochemicals Ltd has been obtained on 16/03/2020

Product	As per Environmental Clearances	As per Consent to Operate (2020)	Actual Production		Remarks
			APRIL 2022- MARCH 2023 full year	APR 2023 - SEPT 2023 6 months	
Maleic Anhydride	7660 TPA	7660 TPA	6904.225	3322.300	We are well within the prescribed limit of EC & Consent

Compliance to the conditions stipulated under Environmental Clearance granted by the Ministry of Environment & Forest, Government of India vide letter No. J-11011/986/2007-IAII (I) dated 02.04.2008 is complied.

A.	Specific Conditions:	
i.	Ambient air quality monitoring stations, SPM, SO ₂ and NO _x) shall be set up in the petrochemical unit in consultation with SPCB, based on occurrence of maximum ground level concentration and down-wind direction of wind. The monitoring network must be decided based on modeling exercise to represent short term GLCs. Data on VOC shall be monitored and submitted to the SPCB / Ministry's Regional Office. Monitoring of VOC shall be undertaken.	Yes, the ambient air quality monitoring is carried out regularly & will be continued. REFER ANNEXURE II
ii.	The effluent generated after recovery of Maleic Anhydride from Scrubber effluent of M/s IG Petrochemicals Limited (IGPL) shall be sent back to ETP of IGPL for further Treatment.	Complied. The effluent generated in Maleic Anhydride plant is sent to ETP for further treatment. After amalgamation of Mysore Petrochemicals MA plant with IGPL, this effluent transfer is internal transfer to ETP.
iii.	The hazardous waste generated in the form of distillation residues shall be used as a fuel in heater of M/s IG Petrochemical Limited.	Complied. Refer ANNEXURE IV for the quantities generated and used as fuel in thermic fluid heaters.
iv.	All the standards /Norms stipulated under Environment (Protection) Act, 1986/CPCB should be met. In addition all new standards/norms that would be notified in future for petrochemical units shall be applicable for the proposed expansion unit.	Agreed
v.	Project authority shall undertake rainwater harvesting measures to recharge water and also to minimize the water drawl from the reservoir and ground water.	Yes, we have installed rainwater harvesting system and recover 20354 m ³ of rain water during Apr 2023 to Sept 2023.
vi.	Green belt shall be raised in 33% of the plant area to mitigate the fugitive emissions the plant. Selection of plant species shall	Adequate green belt has been developed.

	be as per the Central Pollution Control Board guidelines.	
vii.	Occupational Health Surveillance of the workers should be done on a regular basis and records maintained as per the Factories Act.	Trained Male nurse is provided in all three shifts. We have appointed fulltime Doctor and have tie up with local hospitals to attend to medical emergencies. Please refer Company has well equipped Occupational Health center (OHC) with two beds located in its admin building. Company has a program of pre and post (periodic) medical checkups whereby all workers in hazardous operations are tested twice a year. The records are maintained in Form-7. ANNEXURE – VIII.

B.	General Conditions:	
i.	The project authorities must strictly adhere to the stipulations made by the Pollution Control Board and the State Government.	Agreed and complied
ii.	No further expansion or modernization in the plant shall-be carried out without prior approval of the Ministry of Environment and Forests.	Agreed .
iii.	At no time, the emissions shall go beyond the prescribed standards. In the event of failure of any pollution control system adopted by the units, the respective unit should be immediately put out of operation and should not be restarted until the desired efficiency has been achieved.	Agreed
iv.	The overall noise levels in and around the plant area shall be kept well within the standards (85 dBA) by providing noise control measures including acoustic hoods,	Yes, Enclosures have been provided at various Noise Generating locations.

	silencers, enclosures etc. on all sources of noise generation. The ambient noise levels should conform to the standards prescribed under EPA Rules, 1989 viz. 75 dBA (day time) and 70 dBA (night time).	Maximum Noise Level measured is 69.8 dBA in the month of Aug 2023. Monitoring Reports for the period Apr 2023 – Sept 2023 are enclosed as ANNEXURE – II.
v.	The project authorities must strictly comply with the provisions made in Manufacture, Storage and Import of Hazardous Chemicals Rules 1989 as amended in 2000 for handling of hazardous chemicals etc. Necessary approvals from Chief Controller of Explosives must be obtained before commission of the project.	We shall abide by this strictly. The site details are submitted to the DISH as they are the prescribed authority under the MSIHC Rules. Consent To Operate / Authorization from MPCB has been obtained. Format 1.0/CAC/UAN No. MPCB CONSENT - 0000115836/CR/2207000116 Dated: 02/07/2022, valid upto 31/08/2026. Copy of same is enclosed as ANNEXURE – XV.
vi.	The project authorities must strictly comply with the rules and regulations with regard to handling and disposal of hazardous wastes in accordance with the Hazardous Wastes (Management and Handling) Rules, 2003. Authorization from the State Pollution Control Board must be obtained for collections/treatment/storage/disposal of hazardous wastes.	Yes, complied. We have membership with CHWTSDF at Taloja and regularly disposing off our hazardous waste to CHWTSDF. Copy of the membership certificate & hazardous waste return are enclosed as ANNEXURE – XIII & XIV.
vii.	The project authorities will provide adequate funds both recurring and non-recurring to implement the conditions stipulated by the Ministry of Environment and Forests as well as the State Government along with the implementation schedule for all the conditions stipulated herein. The funds so provided should not be diverted for any other purposes.	Agreed and complied ANNEXURE IX.
viii.	The stipulated conditions will be monitored by the Regional Office of this Ministry at Bhopai/Central Pollution Control Board/State Pollution Control Board. A six monthly compliance report and the monitored data should be submitted to them regularly.	Complied.

ix.	The Project Proponent shall inform the public that the project has been accorded environmental clearance by the Ministry and copies of the clearance letter are available with the State Pollution Control Board/ Committee and may also be seen at Website of the Ministry of Environment and Forests at http://www.envfor.nic.in . This should be advertised within seven days from the date of issue of the clearance letter at least in two local newspapers that are widely circulated in the region of which one shall be in the vernacular language of the locality concerned and a copy of the same should be forwarded to the Regional office.	Complied
x.	The Project Authorities shall inform the Regional Office as well as the Ministry, the date of financial closure and final approval of the project by the concerned authorities and the date of commencing the land development work.	Complied.

I. G. Petrochemicals Ltd.

PAIV-MAIV-BENZOIC ACID –DEP/DMP-ETP UPGRADATION Compliance Report

Ref	PA-IV EC COMPLIANCE REPORT APR 2023 – SEPT 2023 EC No. J-11011/73/2016-IA-II (I), Dated : 18th July, 2017 & amendment in same dated 20th February 2018.
To	IG Petrochemicals Ltd, T-2, MIDC Talaja
For	Expansion of Petrochemical and synthetic organic chemicals manufacturing facility.
Status	Phthalic Anhydride & Maleic Anhydride Plants are commissioned, Di Ethyl / Di Methyl Phthalic Plant is under erection.

Proposal is for expansion of petrochemical and synthetic organic chemicals manufacturing facility at Plot No. T-2, MIDC Talaja, Tehsil Panvel, District Raigad, Maharashtra by M/s I G Petrochemicals Ltd. (IGPL). Total land area is 1,13,282 m². Industry has already developed Green belt in an area of 10% i.e. 11,327.6 m² out of 1,13,282 m² of area of the project.

This Environmental Clearance were obtained for expansion of petrochemical and synthetic organic chemicals manufacturing facility with total proposed capacity of 72210 TPA.

Consolidated Consent to Operate for existing Plant PA –I, PA – II ,PA – III, Benzoic Acid & Maleic Anhydride plants is obtained.

Production details of existing unit as per listed below:

Product	As per Environmental Clearances	As per Consent to Operate (2021)
Phthalic Anhydride	PAI+PAII90000 MTPA PAI+PA IIEXP 26110 MTPA PAIII 53000 MTPA PA IV 53000 MTPA	222110 MT/A
Benzoic Acid	1750 MTPA	1500 MT/A
*Maleic Anhydride	7660 MTPA	7660 MTPA
Di Ethyl Phthalate / Di Methyl Phthalate	12600 MTPA	12600 MTPA

I. G. Petrochemicals Ltd.

PAIV-MAIV-BENZOIC ACID –DEP/DMP-ETP UPGRADATION Compliance Report

Power (Exported to Grid)	2.5 MW	2.5 MW
--------------------------	--------	--------

* Maleic Anhydride manufacturing facility of Mysore Petro Chemicals Ltd located at plot T-1 was bought over by I G Petro Chemicals Ltd w. e.f. 1st April 2017.

Proposed Additional capacities of Products as per EC No. J-11011/73/2016-IA-II (I), Dated: 18th July, 2017 & amendment of the same was received on 20th February 2018

Product	As per Environmental Clearance (MT/A)
Phthalic anhydride (PAN)(PA4 plant)	53,000
Benzoic acid (capacity increase of existing plant)	750
Maleic Anhydride (MA4 plant)	1160
Power (Export to grid)	--
Di ethyl phthalate (DEP)	12600
Di methyl phthalate (DMP)	
By Products	
Sodium sulphate	900
Phthalic acid	800
Monoester salts	3000

Compliance to the conditions stipulated under Environmental Clearance granted by the Ministry of Environment & Forest, Government of India vide letter No. J-11011/73/2016-IA-II (I), Dated: 18th July, 2017 & amendment in same is received on 20th February 2018 is as given below.

The project activity is listed at 5 (f) in the Schedule of the EIA Notification, 2006 and is of 'B' Category being in the industrial area and shall not require Public Hearing. Based on the information provided by you, the Ministry of Environment and Forest hereby accords environmental clearance to the above project under the provisions of EIA Notification dated 14th September 2006, subject to the compliance of the following Specific and Generation condition.

OK. Above condition is noted.

A.	Specific Conditions:	
i.	<p>5000 trees shall be planted in five years in nearby villages. Survival rate of plants shall be reported to RO, MoEF & CC in 6 monthly compliance report.</p>	<p>We have planted 2000 nos of trees at Ghot Camp located 1.0 km away from IGPL Plant in the year - 2019 monsoon. Also, we have planted 3000 no.s of trees near Nitlas village in Aug 2021. Total 5000 number of trees are planted. Survival report enclosed. Refer ANNEXURE-XXVI.</p> <p>59 numbers of trees were replanted against non-living & damaged tress. Survival rate is 98.82 %.</p> <p>MIDC has been allocated Plot No. OS – 44 to M/s I G Petrochemicals Ltd. For tree plantation & beautification where 2134 no.s of trees are planted.</p>
ii.	<p>At least 1.5 % of the total cost of the project shall be earmarked towards the Enterprise Social Commitment (ESC)based on local needs and action plan with financial and physical breakup/details shall be prepared and submitted to the Ministry's Regional Office at Nagpur. Implementation of such program shall be ensured accordingly in a time bound manner.</p>	<p>Yes, 0.75 % (fig revised as per MoEF & CC office memorandum F.No.22-65/2017-IA.III dated 1st May 2018) of the total cost of the project will be earmarked towards Enterprise Social Commitment. Sufficient budgetary provision will be made for health improvement, education, water and electricity supply etc. at nearby villages. Budgetary allocation made towards ESC /CER are enclosed as ANNEXURE – XVIII.</p>
iii.	<p>A regular environment manager having post graduate qualification in environmental sciences/ environmental engineering to be appointed for looking after the environmental management activities of the proposed plant.</p>	<p>Appointed qualified staff with post-graduation in Environmental Science (Master in Environment Management -M.E.M from SIBER Institute.) Engineering is appointed for environmental management activities.</p>

iv.	<p>The unit shall adhere to zero liquid discharge (ZLD) . As per EC amendment dated 20th Feb 2018(ANNEXURE XIX) effluent discharge to CETP should be 220 m3/day.</p>	<p>Yes, Agreed. Effluent generated from existing unit and expansion is being treated and recycled within the plant & remaining treated effluent is restricted to 220 m³/day for final discharge to CETP. REFER. ANNEXURE-XXV for few photos of ETP upgradation.</p>
v.	<p>Continuous online (24 x7) monitoring to be installed for flow measurement and measurement of pollutants within the treatment unit. Data to be uploaded on company's website and provided to the respective RO of MoEF & CC, CPCB and SPCB.</p>	<p>Yes, we have installed continuous online (24*7) monitoring system measurement for stacks emission & effluent. We have connected online continuous emission monitoring system to CPCB / MPCB Server and data is uploaded on company's website regularly. Refer Annexure – XVI for OCEMS dashboard. Same system has extended for expanded plants. We have provided link of OCEMS on our company web site (http://www.igpetro.com/quality#main-content) Refer ANNEXURE XXII</p>
vi.	<p>The unit shall make the arrangement for protection of possible fire hazards during manufacturing process in material handling. Firefighting system shall be as per the norms.</p>	<p>Yes, entire plant is covered by a hydrant system, which has provided with separate fire water pump and emergency pumps (diesel operated). Fire extinguishers are kept in various parts of the plant depending upon type of fire hazard likely. Total 7600 m³ hydrant tank is available along with 2 numbers of jockey pumps, one main pump (electrical driven) and 4 diesel driven pump.</p>
vii.	<p>Occupational health surveillance of the workers shall be done on a regular basis and records maintained as per the Factories Act.</p>	<p>Regular medical check-ups of all the employees are conducted. Trained Male nurse is provided in all three shifts. We have appointed fulltime Doctor and have tie up with local hospitals to attend to medical emergencies. Please refer</p>

I. G. Petrochemicals Ltd.

PAIV-MAIV-BENZOIC ACID –DEP/DMP-ETP UPGRADATION Compliance Report

		<p>Company has well equipped Occupational Health center (OHC) with two beds located in its admin building.</p> <p>Company has a program of pre and post (periodic) medical checkups whereby all workers in hazardous operations are tested twice a year. The records are maintained in Form-7. ANNEXURE – VIII</p>
viii.	<p>The by-products which fall under the purview of the Hazardous Waste Rules, be handled as per the provisions of the said Rules and necessary permissions shall be obtained under the said rules.</p>	<p>We have already received amalgamated Consent to Operate from MPCB (REF ANNEXURE-XV) for the additional requirement from the expansion plants. We are member of CHW-TSDF REF ANNEXURE XIII.</p>

B.	General Conditions:	
i.	<p>The project authorities must strictly adhere to the stipulations made by the state Pollution Control Board (SPCB), State Government and any other statutory authority.</p>	<p>Amalgamated Consent to Operate /Authorization from MPCB is obtained. Format 1.0/CAC/UAN No. MPCB CONSENT - 0000115836/CR/2207000116 Dated: 02/07/2022, valid upto 31/08/2026. Copy of same is enclosed as ANNEXURE – XV.</p>
ii.	<p>No further expansion or modifications in the plant shall be carried out without prior approval of the Ministry of Environment and Forests. In case of deviations or alterations in the project proposal from those submitted to this Ministry for clearance, a fresh reference shall be made to the Ministry to assess the adequacy of conditions imposed and to add additional environmental protection measures required, if any.</p>	<p>Yes, agreed. No further expansion or modification in the plant will be carried out without prior approval from MoEF & CC</p>

iii.	The locations of ambient air quality monitoring stations shall be decided consultation with the State Pollution Control Board (SPCB) and it shall be ensured that at least one stations is installed in the upwind and downwind direction as well as where maximum ground level concentrations are anticipated.	We are regularly monitoring Ambient Air Quality Monitoring through MoEF & CC recognized laboratory. Ambient Air Quality monitoring stations are set up as per guidelines of SPCB. Ambient Air Monitoring Reports for last six months are enclosed as ANNEXURE - II.
iv.	The National Ambient Air Quality Emission Standards issued by the Ministry vide G.S.R. No. 826(E) dated 16 th November, 2009 shall be followed	Yes, Agreed. Refer ANNEXURE - II.
v.	The overall noise levels in and around the plant area shall be kept well within the standards by providing noise control measures including acoustic hoods, silencers, enclosures etc. on all sources of noise generation. The ambient noise levels shall conform to the standards prescribed under Environment (Protection) Act, 1986 Rules, 1989 viz. 75 dBA (day time) and 70 dBA (night time).	Yes, we have provided enclosures, hood etc. to ensure noise level is under control. Regular ambient Noise monitoring is carried out within the unit and at fence level. All high noise generating sources are enclosed. Regular Noise Level monitoring undertaken. Maximum Noise Level measured is 69.2 dBA in the month of Feb 2023. Reports for Apr 2023 - Sept 2023 period are enclosed under ANNEXURE - II showing compliance.
vi.	The Company shall harvest rainwater from the roof tops of the buildings and storm water drains to recharge the ground water and use the same water for the process activities of the project to conserve fresh water.	Yes, we have installed rainwater harvesting system and recover 20354 m ³ of rain water during Apr 2023 to Sept 2023.
vii.	Training shall be imparted to all employees on safety and health aspects of chemicals handling. Pre-employment and routine periodical medical examinations for all employees shall be undertaken on regular basis. Training to all employees on handling of chemicals shall be imparted.	Yes, periodical Training is carried out of all employees on safety and health aspects of chemicals handling. Pre-employment and routine periodical medical examinations for regular basis. Refer ANNEXURE - XX.

viii.	The company shall also comply with all the environmental protection measures and safeguards proposed in the documents submitted to the Ministry. All the recommendations made in the EIA & EMP in respect of environmental management, risk mitigation measures and public hearing relating to the project shall be implemented.	Yes agreed. Complied.
ix.	The company shall undertake all relevant measures for improving the socio-economic conditions of the surrounding area. CSR activities shall be undertaken by involving local villages and administration.	Yes, the company contributes to nearby Ashram / local village Gram panchayat. Refer Annexure – XVIII.
x.	The company shall undertake eco-developmental measures including community welfare measures in the project area for the overall improvement of the environment.	Company is undertaking various community welfare measures for improvement of the environment. refer ANNEXURE XXVI & ANNEXURE – XVIII.
xi.	A separate Environmental Management Cell equipped with full-fledged laboratory facilities shall be set up to carry out the Environmental Management and Monitoring functions.	Separate Environment Management Team under HoD – Health, Safety & Environment (Master in Environment Management -M.E.M from SIBER Institute.) has been formed. Separate Environment Laboratory for monitoring ETP performance has been established. Technical guidance shall be provided by President (Production & Technical Services). Necessary sampling & analysis is conducted by MoEF & CC approved laboratories.
xii.	The company shall earmark sufficient funds towards capital cost and recurring cost per annum to implement the conditions stipulated by the Ministry of Environment and Forests as well as the State Government along with the implementation schedule for all the conditions stipulated herein. The funds so earmarked for environment management/ pollution control measures	Yes, Budget for Environment Protection as stipulated in the EIA has been used for environmental protection in proposed expansion project.

I. G. Petrochemicals Ltd.

PAIV-MAIV-BENZOIC ACID –DEP/DMP-ETP UPGRADATION Compliance Report

	shall not be diverted for any other purpose.	
xiii.	A copy of the clearance letter shall be sent by the project proponent to concerned Panchayat, Zila Parisad/Municipal Corporation, Urban local Body and the local NGO, if any, from whom suggestions/representations, if any, were received while processing the proposal.	Yes, We have submitted EC copy to Panvel Municipal Corporation which is local body. REF ANNEXURE XXIII
xiv.	The project proponent shall also submit six monthly reports on the status of compliance of the stipulated Environmental Clearance conditions including results of monitored data (both in hard copies as well as by e-mail) to the respective Regional Office of MoEF, the respective Zonal Office of CPCB and SPCB. A copy of Environmental Clearance and six monthly compliance status report shall be posted on the website of the company.	Yes, it is carried out regularly for all EC s. Refer ANNEXURE V for Ack. Copy of last six monthly compliance report submitted
xv.	The environmental statement for each financial year ending 31 st March in Form-V as is mandated shall be submitted to the concerned State Pollution Control Board as prescribed under the Environment (Protection) Rules, 1986, as amended subsequently, shall also be put on the website of the company along with the status of compliance of environmental clearance conditions and shall also be sent to the respective Regional Offices of MoEF by email.	Yes, it is carried out regularly in existing plants and same practice will be adopted in expansion plant. REFER ANNEXURE -XXI.
xvi.	The project proponent shall inform the public that the project has been accorded environmental clearance by the Ministry and copies of the clearance letter are available with the SPCB/ Committee and may also be seen at Website of the Ministry at http://moef.nic.in . This shall be advertised within seven days from the date of issue of the clearance letter, at least in two local	Complied- advertisement was placed in media on obtaining the Environmental clearance. Copy of Advertisement published in local newspaper is enclosed herewith as ANNEXURE- X.

	newspapers that are widely circulated in the region of which one shall be in the vernacular language of the locality concerned and a copy of the same shall be forwarded to the concerned Regional Office of the Ministry.	
xvii.	The project authorities shall inform the Regional Office as well as the Ministry, the date of financial closure and final approval of the project by the concerned authorities and the date of start of the project.	Yes, Agreed. Project is completed Phthalic, Maleic Anhydride and DEP/DMP. Consent to Operate /Authorization from MPCB is obtained. Format 1.0/CAC/UAN No. MPCB CONSENT - 0000115836/CR/2207000116 Dated: 02/07/2022, valid upto 31/08/2026. Copy of same is enclosed as ANNEXURE – XV.
xviii	The Ministry may revoke or suspend the clearance, if implementation of any of the above conditions is not satisfactory	Yes, Noted.
xix	The Ministry reserves the right to stipulate additional conditions, if found necessary. The company in a time bound manner will implement these conditions.	Yes, Agreed.
xx.	The above conditions will be enforced, inter-alia under the provisions of the Water (Prevention & Control of Pollution) Act, 1974, Air (Prevention & Control of Pollution) Act, 1981, the Environment (Protection) Act, 1986, Hazardous Waste (Management, Handling and Trans-boundary Movement) Rules, 2016 and the Public Liability Insurance Act, 1991 along with their amendments and rules.	Yes, Noted.

INDEX

ANNEXURE NO.	DESCRIPTION
ANNEXURE-I	: CER guidelines from MOEF & CC
ANNEXURE-II	: <ul style="list-style-type: none"> - Environmental Monitoring Reports for: - Ambient Air Quality, - Ambient Noise Level, - Stack Emission Monitoring, - Work Room Air Quality Monitoring, - ETP Inlet / Outlet Monitoring Reports
ANNEXURE – III	: Data on Water Consumption & Waste Water Generation.
ANNEXURE – IV	: Data on Residue Generation.
ANNEXURE – V	: Ack. Copy of last six monthly compliance report submitted.
ANNEXURE – VI	: Photograph Showing Designated Area for Raw Material Storage
ANNEXURE – VII	: Plot Plan
ANNEXURE - VIII	: Details of Occupational Health Surveillance Program.
ANNEXURE - IX	: Budget for Environmental Protection.
ANNEXURE - X	: Copy of Advertisements.
ANNEXURE – XI	: Note on revamped ETP.
ANNEXURE – XII	: Photograph of MPCB display board.
ANNEXURE – XIII	: Copy of MWML Membership Certificate.
ANNEXURE – XIV	: Copy Hazardous Waste Returns for year 2021 - 2022.

ANNEXURE – XV	:	Copy of existing Consent to Operate
ANNEXURE-XVI	:	OCEMS Dashboard
ANNEXURE-XVII	:	CSR Details
ANNEXURE-XVIII	:	CER Budget & Expenditure
ANNEXURE-IXX	:	EC Amendment
ANNEXURE-XX	:	Chemical Handling
ANNEXURE-XXI	:	Environmental Statement 2023 – 2024
ANNEXURE-XXII	:	IGPL web site snapshot
ANNEXURE-XXIII	:	EC copy submission to Panvel Municipal Corporation.
ANNEXURE-XXIV	:	Photos of ongoing expansion project
ANNEXURE-XXV	:	ETP Upgradation Photos
ANNEXURE-XXVI	:	Tree Plantation Survival Report

F.No.22-65/2017-IA.III

Government of India

Ministry of Environment, Forest and Climate Change
Impact Assessment Division

Indira Paryavaran Bhawan
Jor Bagh Road, Aliganj
New Delhi - 110003

Dated: 1st May, 2018

Office Memorandum

Sub: Corporate Environment Responsibility (CER) – reg.

The Environment Impact Assessment (EIA) Notification, 2006, issued under the Environment (Protection) Act, 1986, as amended from time to time, prescribes the process for granting prior environment clearance (EC) in respect of certain development projects/activities listed out in the Schedule to the Notification.

2. Sustainable development has many important facets/components like social, economic, environmental, etc. All these components are closely inter-related and mutually re-enforcing. Therefore, the general structure of EIA document, under Appendix-III to the notification, prescribes inter-alia public consultation, social impact assessment and R&R action plan besides environment management plan (EMP).

3. Section 135 of the Companies Act, 2013 deals with Corporate Social Responsibility (CSR) and Schedule-VII of the Act lists out the activities which may be included by companies in their CSR Policies. The concept of CSR as provided for in the Companies Act, 2013 and covered under the Companies (Corporate Social Responsibility Policy) Rules, 2014 comes into effect only in case of companies having operating projects and making net profit as also subject to other stipulations contained in the aforesaid Act and Rules. The environment clearance given to a project may involve a situation where the concerned company is yet to make any net profit and/or is not covered under the purview of the aforesaid Act and Rules. In such cases, the provisions of aforesaid act and Rules will not apply.

4. In the past, it has been observed that different Expert Appraisal Committees / State Expert Appraisal Committees (EACs/SEACs) have been prescribing different formulation of the Corporate Environment Responsibility (CER) and no common principles are followed. Several suggestions have also been received in this regard which inter-alia states that Greenfield projects and Brownfield projects should be treated differently; no CER should be prescribed whereas there is no increase in air pollution load, R&R, etc., besides streamlining percentage of CER.

5. The Ministry has carried out a detailed stakeholder consultation which inter-alia included meeting with Ministry of Petroleum & Natural Gas, Ministry of Power, Chairmen EACs, FICCI, ASSOCHAM, Gujarat Chamber of Commerce and Industry amongst others.

6. In order to have transparency and uniformity while recommending CER by Expert Appraisal Committee (EAC) / State level Expert Appraisal Committee (SEAC) / District level Expert Appraisal Committee (DEAC), the following guidelines are issued:

- (I) The cost of CER is to be in addition to the cost envisaged for the implementation of the EIA/EMP which includes the measures for the pollution control, environmental protection and conservation, R&R, wildlife and forest conservation/protection measures including the NPV and Compensatory Aforestation, required, if any, and any other activities, to be derived as part of the EIA process.
- (II) The fund allocation for the CER shall be deliberated in the EAC or SEAC or DEAC, as the case may be, with a due diligence subject to **maximum percentage** as prescribed below for different cases:

S.No	Capital Investment / Additional Capital Investment (in Rs)	Greenfield Project - % of Capital Investment	Brownfield Project - % of Additional Capital Investment
I	II	III	IV
1.	≤ 100 crores	2.0%	1.0%
2.	> 100 crores to ≤ 500 crores	1.5%	0.75%
3.	> 500 crores to ≤ 1000 crores	1.0%	0.50%
4.	> From 1000 crores to ≤10000 crores	0.5%	0.25%
5.	> 10000 crores	0.25%	0.125%

- visal
- (III) The activities proposed under CER shall be worked out based on the issues raised during the public hearing, social need assessment, R&R plan, EMP, etc.
 - (IV) The proposed activities shall be restricted to the affected area around the project.
 - (V) Some of the activities which can be carried out in CER, are infrastructure creation for drinking water supply, sanitation, health, education, skill development, roads, cross drains, electrification including solar power, solid waste management facilities, scientific support and awareness to local farmers to increase yield of crop and fodder, rain water harvesting, soil moisture conservation works, avenue plantation, plantation in community areas, etc.
 - (VI) The entire activities proposed under the CER shall be treated as project and shall be monitored. The monitoring report shall be submitted to the regional office as a part of half-yearly compliance report, and to the District Collector. It should be posted on the website of the project proponent.
 - (VII) The District Collector may add or delete the activities as per the requirement of the District.
 - (VIII) The EAC can vary the above percentage of CER subject to proper diligence, quantification and justification. The EAC based on appraisal, should clearly suggest the activities to be carried out under CER.
 - (IX) This CER is not applicable in name change, transfer and amendment involving no additional project investment. In case of amendment in EC involving additional expenditure, CER will be applicable only on the additional expenditure as per column-IV of the table given in para 6(II) above.

7. This issues in supersession of all earlier OMs and guidelines issued in this regard.

8. This issues with the approval of competent authority.


(Sharath Kumar Palleria)
Director (IA-III-Policy)

1. Chairman, CPCB
2. Chairmen of all the Expert Appraisal Committees
3. Chairperson/Member Secretaries of all the SEIAA/SEACs
4. Chairpersons/Member Secretaries of all SPCBs/UTPCCs
5. All the officers of IA Division

Copy for information to:

- 1 PS to Minister for Environment, Forest and Climate Change
- 2 PS to Min (EP&CC)
- 3 PPS to Secretary (EP&CC)
- 4 PPS to AS(A&J) / AS(A&M)
- 5 PPS to JS(GB) / JS(JF)
- 6 Website: MUEP&CC
- 7 Guided File

ANNEXURE II

DRINKING WATER ANALYSIS

Drinking Water Analysis Report										
Sr. No	Location	Apr-23			May-23			June-23		
		Coliform Count/ 100 ml	E.coli (Limit: Absent)	Remark	Coliform Count/ 100 ml	E.coli (Limit: Absent)	Remark	Coliform Count/ 100 ml	E.coli (Limit: Absent)	Remark
		1	Canteen-1 (Main Canteen)	Absent	Absent	Potable	Absent	Absent	Potable	Absent
2	Canteen-2 (Contract Canteen)	Absent	Absent	Potable	Absent	Absent	Potable	Absent	Absent	Potable
3	PA Control room	Absent	Absent	Potable	Absent	Absent	Potable	Absent	Absent	Potable
4	Workshop	Absent	Absent	Potable	Absent	Absent	Potable	Absent	Absent	Potable
5	Instrumentation	Absent	Absent	Potable	Absent	Absent	Potable	Absent	Absent	Potable
6	Admin	Absent	Absent	Potable	Absent	Absent	Potable	Absent	Absent	Potable
7	Laboratory	Absent	Absent	Potable	Absent	Absent	Potable	Absent	Absent	Potable
8	MA Control Room	Absent	Absent	Potable	Absent	Absent	Potable	Absent	Absent	Potable
9	PA Bagging Section	Absent	Absent	Potable	Absent	Absent	Potable	Absent	Absent	Potable

Drinking Water Analysis Report										
Sr. No	Location	July-23			Aug-23			Sept-23		
		Coliform Count/ 100 ml	E.coli (Limit: Absent)	Remark	Coliform Count/ 100 ml	E.coli (Limit: Absent)	Remark	Coliform Count/ 100 ml	E.coli (Limit: Absent)	Remark
		1	Canteen-1 (Main Canteen)	Absent	Absent	Potable	Absent	Absent	Potable	Absent
2	Canteen-2 (Contract Canteen)	Absent	Absent	Potable	Absent	Absent	Potable	Absent	Absent	Potable
3	PA Control room	Absent	Absent	Potable	Absent	Absent	Potable	Absent	Absent	Potable
4	Workshop	Absent	Absent	Potable	Absent	Absent	Potable	Absent	Absent	Potable
5	Instrumentation	Absent	Absent	Potable	Absent	Absent	Potable	Absent	Absent	Potable
6	Admin	Absent	Absent	Potable	Absent	Absent	Potable	Absent	Absent	Potable
7	Laboratory	Absent	Absent	Potable	Absent	Absent	Potable	Absent	Absent	Potable
8	MA Control Room	Absent	Absent	Potable	Absent	Absent	Potable	Absent	Absent	Potable
9	PA Bagging Section	Absent	Absent	Potable	Absent	Absent	Potable	Absent	Absent	Potable

Monitoring & Analysis by M/s. Aditya Environmental Services Pvt. Ltd.

ANNEXURE II

WORK PLACE FUGATIVE EMISSION MONITORING REPORT

<u>WORK PLACE FUGATIVE EMISSION MONITORING REPORT</u>					
Sr. No.	Parameter	Analysis Result			Limiting Standard
		April - 2023			
		14-04-2023			
		Ortho Xylene (Unloading)	Ortho Xylene (Tank Farm)	DEP Plant	
1	Maleic Anhydride	<0.5	<0.5	-	25 mg/Nm ³
2	Phthalic Anhydride	<0.5	<0.5	-	25 mg/Nm ³
3	Ortho Xylene	<0.5	<0.5	-	25 mg/Nm ³
4	Benzoic Acid	<0.5	<0.5	-	25 mg/Nm ³
5	Ethyl Alcohol	-	-	<0.1	1900 mg/m ³
6	Phthalic Anhydride	-	-	<0.5	20 mg/Nm ³
7	Benzene	-	-	<0.5	1 ppm

<u>WORK PLACE FUGATIVE EMISSION MONITORING REPORT</u>					
Sr. No.	Parameter	Analysis Result			Limiting Standard
		May – 2023			
		23-05-2023			
		Ortho Xylene (Unloading)	Ortho Xylene (Tank Farm)	DEP Plant	
1	Maleic Anhydride	<0.5	<0.5	-	25 mg/Nm ³
2	Phthalic Anhydride	<0.5	<0.5	-	25 mg/Nm ³
3	Ortho Xylene	<1.0	<1.0	-	25 mg/Nm ³
4	Benzoic Acid	<0.5	<0.5	-	25 mg/Nm ³
5	Ethyl Alcohol	-	-	<0.1	1900 mg/m ³
6	Phthalic Anhydride	-	-	<0.5	20 mg/Nm ³
7	Benzene	-	-	<0.5	1 ppm

WORK PLACE FUGATIVE EMISSION MONITORING REPORT

Sr. No.	Parameter	Analysis Result			Limiting Standard
		June – 2023			
		20-06-2023			
		Ortho Xylene (Unloading)	Ortho Xylene (Tank Farm)	DEP Plant	
1	Maleic Anhydride	<0.5	<0.5	-	25 mg/Nm ³
2	Phthalic Anhydride	<0.5	<0.5	-	25 mg/Nm ³
3	Ortho Xylene	<1.0	<1.0	-	25 mg/Nm ³
4	Benzoic Acid	<0.5	<0.5	-	25 mg/Nm ³
5	Ethyl Alcohol	-	-	<0.1	1900 mg/m ³
6	Phthalic Anhydride	-	-	<0.5	20 mg/Nm ³
7	Benzene	-	-	<0.5	1 ppm

WORK PLACE FUGATIVE EMISSION MONITORING REPORT

Sr. No.	Parameter	Analysis Result			Limiting Standard
		July -2023			
		28-07-2023			
		Ortho Xylene (Unloading)	Ortho Xylene (Tank Farm)	DEP Plant	
1	Maleic Anhydride	<0.5	<0.5	-	25 mg/Nm ³
2	Phthalic Anhydride	<0.5	<0.5	-	25 mg/Nm ³
3	Ortho Xylene	<1.0	<1.0	-	25 mg/Nm ³
4	Benzoic Acid	<0.5	<0.5	-	25 mg/Nm ³
5	Ethyl Alcohol	-	-	<0.1	1900 mg/m ³
6	Phthalic Anhydride	-	-	<0.5	20 mg/Nm ³
7	Benzene	-	-	<0.5	1 ppm

WORK PLACE FUGATIVE EMISSION MONITORING REPORT

Sr. No.	Parameter	Analysis Result			Limiting Standard
		August – 2023			
		22-08-2023			
		Ortho Xylene (Unloading)	Ortho Xylene (Tank Farm)	DEP Plant	
1	Maleic Anhydride	<0.5	<0.5	-	25 mg/Nm ³
2	Phthalic Anhydride	<0.5	<0.5	-	25 mg/Nm ³
3	Ortho Xylene	<1.0	<1.0	-	25 mg/Nm ³
4	Benzoic Acid	<0.5	<0.5	-	25 mg/Nm ³
5	Ethyl Alcohol	-	-	<0.1	1900 mg/m ³
6	Phthalic Anhydride	-	-	<0.5	20 mg/Nm ³
7	Benzene	-	-	<0.5	1 ppm

WORK PLACE FUGATIVE EMISSION MONITORING REPORT

Sr. No.	Parameter	Analysis Result			Limiting Standard
		September – 2023			
		16-09-2023			
		Ortho Xylene (Unloading)	Ortho Xylene (Tank Farm)	DEP Plant	
1	Maleic Anhydride	<0.5	<0.5	-	25 mg/Nm ³
2	Phthalic Anhydride	<0.5	<0.5	-	25 mg/Nm ³
3	Ortho Xylene	<1.0	<1.0	-	25 mg/Nm ³
4	Benzoic Acid	<0.5	<0.5	-	25 mg/Nm ³
5	Ethyl Alcohol	-	-	<0.1	1900 mg/m ³
6	Phthalic Anhydride	-	-	<0.5	20 mg/Nm ³
7	Benzene	-	-	<0.5	1 ppm

Monitoring & Analysis by M/s Aditya Environmental Services Pvt. Ltd.

ANNEXURE II

WORK ROOM AIR MONITORING REPORTS

Work Room Air Monitoring				
Location	April – 2023			
	16-04-2023			
	PA	SO2	NOx	SPM
	ppm	mg/m ³	mg/m ³	mg/m ³
Phthalic Anhydride Ware House	<0.5	0.028	0.038	0.346
Limiting Standards	1	13	9	15
NIOSH				
TLV(TWA)	--	2	--	--
STEL	--	5	1	--
ACGIH				
TLV(TWA)	--	2	3	10
STEL	--	5	5	--

Work Room Air Monitoring				
Location	May-2023			
	24-05-2023			
	PA	SO2	NOx	SPM
	ppm	mg/m ³	mg/m ³	mg/m ³
Phthalic Anhydride Ware House	<0.5	0.032	0.048	0.362
Limiting Standards	1	13	9	15
NIOSH				
TLV(TWA)	--	2	--	--
STEL	--	5	1	--
ACGIH				
TLV(TWA)	--	2	3	10
STEL	--	5	5	--

Work Room Air Monitoring				
	June – 2023			
	20-06-2023			
Location	PA	SO2	NOx	SPM
	ppm	mg/m ³	mg/m ³	mg/m ³
Phthalic Anhydride Ware House	<0.5	0.030	0.040	0.356
Limiting Standards	1	13	9	15
NIOSH				
TLV(TWA)	--	2	--	--
STEL	--	5	1	--
ACGIH				
TLV(TWA)	--	2	3	10
STEL	--	5	5	--

Work Room Air Monitoring				
	July – 2023			
	28-07-2023			
Location	PA	SO2	NOx	SPM
	ppm	mg/m ³	mg/m ³	mg/m ³
Phthalic Anhydride Ware House	<0.5	0.028	0.042	0.340
Limiting Standards	1	13	9	15
NIOSH				
TLV(TWA)	--	2	--	--
STEL	--	5	1	--
ACGIH				
TLV(TWA)	--	2	3	10
STEL	--	5	5	--

Work Room Air Monitoring				
	August - 2023			
	22-08-2023			
Location	PA	SO2	NOx	SPM
	ppm	mg/m ³	mg/m ³	mg/m ³
Phthalic Anhydride Ware House	<0.5	0.026	0.042	0.348
Limiting Standards	1	13	9	15
NIOSH				
TLV(TWA)	--	2	--	--
STEL	--	5	1	--
ACGIH				
TLV(TWA)	--	2	3	10
STEL	--	5	5	--

Work Room Air Monitoring				
	September – 2023			
	15-09-2023			
Location	PA	SO2	NOx	SPM
	ppm	mg/m ³	mg/m ³	mg/m ³
Phthalic Anhydride Ware House	<0.5	0.024	0.035	0.324
Limiting Standards	1	13	9	15
NIOSH				
TLV(TWA)	--	2	--	--
STEL	--	5	1	--
ACGIH				
TLV(TWA)	--	2	3	10
STEL	--	5	5	--

Monitoring & Analysis by M/s Aditya Environmental Services Pvt. Ltd.

ANNEXURE II

WORK ROOM EMISSION MONITORING REPORT

<u>WORK ROOM EMISSION MONITORING REPORT</u>						
Sr. No.	Parameter	Analysis Result				Limiting Standard
		April – 2023				
		14-04-2023				
		Phthalic Anhydride Plant -I	Phthalic Anhydride Plant -II	Phthalic Anhydride Plant –III	Phthalic Anhydride Plant - IV	
1	Ortho Xylene	<0.5	<0.5	<0.5	<0.5	100 ppm
2	Phthalic Anhydride	<0.5	<0.5	<0.5	<0.5	1 ppm
3	Benzene	-	-	-	<0.5	1 ppm

<u>WORK ROOM EMISSION MONITORING REPORT</u>						
Sr. No.	Parameter	Analysis Result				Limiting Standard
		May – 2023				
		22-11-2022				
		Phthalic Anhydride Plant -I	Phthalic Anhydride Plant -II	Phthalic Anhydride Plant –III	Phthalic Anhydride Plant - IV	
1	Ortho Xylene	<1.0	<1.0	<1.0	<1.0	100 ppm
2	Phthalic Anhydride	<0.5	<0.5	<0.5	<0.5	1 ppm
3	Benzene	-	-	-	<0.5	1 ppm

WORK ROOM EMISSION MONITORING REPORT

Sr. No.	Parameter	Analysis Result				Limiting Standard
		Dec - 22				
		19-12-2022				
		Phthalic Anhydride Plant -I	Phthalic Anhydride Plant -II	Phthalic Anhydride Plant -III	Phthalic Anhydride Plant - IV	
1	Ortho Xylene	<0.5	<0.5	<0.5	<0.5	100 ppm
2	Phthalic Anhydride	<0.5	<0.5	<0.5	<0.5	1 ppm
3	Benzene	-	-	-	<0.5	1 ppm

WORK ROOM EMISSION MONITORING REPORT

Sr. No.	Parameter	Analysis Result				Limiting Standard
		Jan - 23				
		11-01-2023				
		Phthalic Anhydride Plant -I	Phthalic Anhydride Plant -II	Phthalic Anhydride Plant -III	Phthalic Anhydride Plant - IV	
1	Ortho Xylene	<0.5	<0.5	<0.5	<0.5	100 ppm
2	Phthalic Anhydride	<0.5	<0.5	<0.5	<0.5	1 ppm
3	Benzene	-	-	-	<0.5	1 ppm

WORK ROOM EMISSION MONITORING REPORT

Sr. No.	Parameter	Analysis Result				Limiting Standard
		Feb - 23				
		06-02-2023				
		Phthalic Anhydride Plant -I	Phthalic Anhydride Plant -II	Phthalic Anhydride Plant -III	Phthalic Anhydride Plant - IV	
1	Ortho Xylene	<0.5	<0.5	<0.5	<0.5	100 ppm
2	Phthalic Anhydride	<0.5	<0.5	<0.5	<0.5	1 ppm
3	Benzene	-	-	-	<0.5	1 ppm

WORK ROOM EMISSION MONITORING REPORT

Sr. No.	Parameter	Analysis Result				Limiting Standard
		Mar - 23				
		16-03-2023				
		Phthalic Anhydride Plant -I	Phthalic Anhydride Plant -II	Phthalic Anhydride Plant -III	Phthalic Anhydride Plant - IV	
1	Ortho Xylene	<0.5	<0.5	<0.5	<0.5	100 ppm
2	Phthalic Anhydride	<0.5	<0.5	<0.5	<0.5	1 ppm
3	Benzene	-	-	-	<0.5	1 ppm

Monitoring & Analysis by M/s Aditya Environmental Services Pvt. Ltd.

ANNEXURE II

AMBIENT AIR MONITORING

Ambient air monitoring- ETP							
Parameters	Standard	April 2023	May 2023	June 2023	July 2023	August 2023	September 2023
SO ₂	80 ug/m ³	30.13	30.3	25.9	22.46	24.36	27.10
Nox	80 ug/m ³	39.37	40.0	35.3	30.35	33.46	37.83
PM 10	100 ug/m ³	85.27	87.1	84.4	48.34	66.64	69.44
PM 2.5	60 ug/m ³	34.06	36.0	33.8	21.74	25.97	28.08
OZONE	180 ug/m ³	10.84	12.5	13.1	11.07	12.58	16.09
Lead	1 ug/m ³	0.6	0.6	1.0	0.11	0.13	0.11
CO	4 mg/m ³	0.5	0.2	0.1	0.77	0.92	1.00
Benzene	5 ug/m ³	<0.6	< 0.84	<0.7	<0.7	<0.7	<0.7
Benzopyrene	1 ug/m ³	<0.3	<0.2	<0.2	<0.2	<0.2	<0.2
Arsenic	6 ug/m ³	<0.3	<1.32	<1.9	<1.9	<1.9	<0.4
Nickel	20 ug/m ³	1.01	4.2	8.5	7.60	11.64	9.90
NH ₃	400 ug/m ³	34.39	26.2	26.8	15.94	19.91	18.33

Ambient air monitoring- Near PA 4							
Parameters	Standard	April 2023	May 2023	June 2023	July 2023	August 2023	September 2023
SO2	80 ug/m3	29.085	31.7	26.2	21.36	23.55	28.44
Nox	80 ug/m3	37.745	42.6	38.5	28.11	29.51	36.09
PM 10	100 ug/m3	86.845	91.8	84.1	50.22	65.38	77.54
PM 2.5	60 ug/m3	35.925	37.5	37.0	19.56	22.88	32.40
OZONE	180 ug/m3	10.28	12.8	13.6	11.15	15.63	16.27
Lead	1 ug/m3	0.09	0.2	0.3	0.11	0.16	0.14
CO	4 mg/m3	0.71	0.6	0.87	0.77	0.79	1.05
Benzene	5 ug/m3	<0.6	<0.7	<0.8	<0.7	<0.7	<0.7
Benzopyrene	1 ug/m3	<0.3	<0.2	<0.2	<0.2	<0.2	<0.2
Arsenic	6 ug/m3	<0.3	<1.9	< 1.56	<1.9	<1.9	<0.4
Nickel	20 ug/m3	0.73	3.1	9.94	8.42	11.83	10.60
NH3	400 ug/m3	36.125	30.9	27.91	16.37	22.31	22.35

Ambient air monitoring- Main Gate							
Parameters	Standard	April 2023	May 2023	June 2023	July 2023	August 2023	September 2023
SO ₂	80 ug/m ³	29.8	29.385	27.9	22.55	26.37	29.05
Nox	80 ug/m ³	38.2	41.735	39.8	30.51	33.64	36.59
PM 10	100 ug/m ³	93.5	82.88	83.5	48.04	68.89	77.00
PM 2.5	60 ug/m ³	35.4	33.645	34.3	22.70	27.18	30.79
OZONE	180 ug/m ³	8	11.635	12.3	10.28	12.77	14.53
Lead	1 ug/m ³	<0.8	0.5	0.6	0.10	0.14	0.12
CO	4 mg/m ³	0.58	1.15	1.0	0.81	1.04	1.10
Benzene	5 ug/m ³	<0.2	< 0.6	<0.7	<0.7	<0.8	<0.7
Benzopyrene	1 ug/m ³	<0.5	<0.3	<0.2	<0.2	<0.2	<0.2
Arsenic	6 ug/m ³	<0.2	< 2.7	<1.9	<1.9	<1.9	<0.4
Nickel	20 ug/m ³	<0.2	5.24	10.9	8.50	9.15	12.70
NH ₃	400 ug/m ³	41	28.56	77.0	16.12	17.35	22.92
Monitoring & Analysis by Aditya Environmental Services Pvt. Ltd.							

ANNEXURE II

EFFLUENT ANALYSIS REPORT

TREATED EFFLUENT ANALYSIS REPORT							
Month	April 2023	May 2023	June 2023	July 2023	August 2023	September 2023	Limiting Standard (*)
Date	13.04.23	24.05.23	19.06.23	29.07.23	23.08.23	15.09.23	
pH	7.85	7.65	7.55	7.5	7.48	7.65	5.5-9.0
COD	20	40	60	30	90	10	250 mg/l
BOD	6.9	14	22	12	35	3.9	100 mg/l
TDS	920	1010	1100	1180	1230	1120	2100 mg/l
Chloride	130	157	150	146	152	260	600 mg/l
TSS	20	28	32	38	52	44	100 mg/l
Sulphates	140	145	138	124	130	210	1000 mg/l
TAN	<0.56	<0.56	<0.56	<0.56	<0.56	<0.56	50 mg/l
O & G	<2.0	<2.0	<2.0	<2.0	<2.0	<2.0	10 mg/l
Bio-assay	90%	90%	90%	100% survival	100% survival	100% survival	90% survival
(*) Standard for discharge in Public Sewers							
All parameters and limits except pH are in mg / lit.							
BOD is expressed in the terms of 3 days and @ 27°C.							
Monitoring & Analysis by M/s Aditya Environmental Services Pvt. Ltd.							

ANNEXURE II

AMBIENT NOISE LEVEL MONITORING REPORT

Ambient Noise Level Monitoring Report												
Month	April 2023		May 2023		June 2023		July 2023		August 2023		September 2023	
Date												
Location	Leq (Day)	Leq (Night)	Leq (Day)	Leq (Night)	Leq (Day)	Leq (Night)	Leq (Day)	Leq (Night)	Leq (Day)	Leq (Night)	Leq (Day)	Leq (Night)
At Factory Boundary :												
L1	66.3	63.1	64.0	61.3	64.2	61.2	63.6	60.3	65.2	61.3	63.2	60.2
L2	63.2	60.6	62.3	59.6	63.8	60.6	62.2	59.8	61.2	57.5	62.1	59.6
L3	56.4	53.8	59.6	55.8	64.9	61.4	61.5	58.0	59.6	55.2	58.9	54.3
L4	58.7	52.9	57.2	54.2	65.3	62.3	64.3	60.3	58.2	56.1	57.6	53.2
L5	64.3	60.7	66.8	61.8	64.1	62.9	66.5	62.4	69.8	65.8	65.2	60.1
L6	61.6	67.8	61.3	58.0	65.2	61.8	59.8	56.1	62.6	58.3	61.8	58.1
L7	65.6	64.3	67.3	62.3	66.1	61.6	66.1	61.3	69.3	64.9	67.9	62.8
Standard	75 (*)	70 (*)	75 (*)	70 (*)	75 (*)	70 (*)	75 (*)	70 (*)	75 (*)	70 (*)	75 (*)	70 (*)

Monitoring & Analysis by M/s Aditya Environmental Services Pvt. Ltd.

ANNEXURE II

STACK EMISSION MONITORING

A Heater Stack Emission Monitoring - PA I							
Physical Data:		April 2023	May 2023	June 2023	July 2023	August 2023	September 2023
Stack Height (m)		31 m					
Inside Diameter (m)		0.5 m					
Stack Area (m²)		0.196 m ²					
Flue Gas Temperature (°C)		165 °C	67 °C	68 °C	75 °C	68 °C	62 °C
Velocity m/sec		8.98 m/sec	8.74 m/sec	3.88 m/sec	2.23 m/sec	7.45 m/sec	7.12 m/sec
Flow m³/hr.		3889 m ³ /hr.	4977 m ³ /hr.	2273 m ³ /hr.	2910 m ³ /hr.	4162 m ³ /hr.	4114 m ³ /hr.
Fuel Quantity		4 MTPD + 7 MTPD					
Fuel Used		LSHS + Residue					
PA I Heater	Limiting Standard	April 2023	May 2023	June 2023	July 2023	August 2023	September 2023
		13-04-2023	23-05-2023	23-06-2023	28-07-2023	22-08-2023	13-09-2023
TPM (mg/Nm³)	150	43.85	50.71	55.56	26.81	31.53	40.48
SO₂ (Kg/Day)	1700	7.58	4.33	1.64	21.31	3.40	2.78
Nox (mg/Nm³)	450	39.74	72.02	57.11	71.60	67.69	74.75
CO (ppm)	200	18.20	16.31	12.63	13.54	9.14	10.51
Acid Mist (mg/Nm³)	35	10.74	8.68	7.67	12.51	10.74	6.84

B

Heater Stack Emission Monitoring - PA II							
Physical Data:		April 2023	May 2023	June 2023	July 2023	August 2023	September 2023
Stack Height (m)		31 m					
Inside Diameter (m)		0.59 m					
Stack Area (m²)		0.274 m ²					
Flue Gas Temperature (°C)		154 °C	165 °C	57 °C	66 °C	67 °C	76 °C
Velocity m/sec		7.75 m/sec	6.87 m/sec	4.91 m/sec	5.10 m/sec	6.40 m/sec	7.00 m/sec
Flow m³/hr.		6108 m ³ /hr.	4430 m ³ /hr.	4195 m ³ /hr.	4136 m ³ /hr.	5087 m ³ /hr.	5583 m ³ /hr.
Fuel Used		LSHS + Residue					
Fuel Quantity		4 MTPD + 7 MTPD					
PA II Heater	Limiting Standard	April 2023	May 2023	June 2023	July 2023	August 2023	September 2023
		13-04-2023	24-05-2023	19-06-2023	28-07-2023	21-08-2023	14-09-2023
TPM (mg/Nm³)	150	46.56	55.12	52.34	36.51	38.08	44.22
SO₂ (Kg/day)	360	6.16	4.10	3.31	2.61	3.71	4.65
Nox (mg/Nm³)	450	27.67	59.22	52.29	60.35	63.74	70.58
CO ppm	200	16.43	18.52	14.08	10.51	11.50	10.88
Acid mist (mg/Nm³)	35	7.66	8.33	9.87	8.60	12.76	8.40

C

Heater Stack Emission Monitoring - PA IV							
Physical Data:		April 2023	May 2023	June 2023	July 2023	August 2023	September 2023
Stack Height (m)		31 m	31 m	31 m	31 m	31 m	31 m
Inside Diameter (m)		0.8 m	0.59 m	0.59 m	0.59 m	0.8 m	0.8 m
Stack Area (m²)		0.502 m ²	0.274 m ²	0.274 m ²	0.274 m ²	0.502 m ²	0.274 m ²
Flue Gas Temperature (°C)		-	165 °C	132°C	97°C	-	149 °C
Velocity m/sec		-	9.09 m/sec	5.79 m/sec	4.92 m/sec	-	11.60 m/sec
Flow m³/hr.		-	10950 m ³ /hr.	6534 m ³ /hr.	6495 m ³ /hr.	-	14526 m ³ /hr.
Fuel Used		HSD + Residue	HSD + Residue	HSD + Residue	HSD + Residue	HSD + Residue	HSD + Residue
Fuel Quantity		4 MTPD + 7 MTPD	4 MTPD + 7 MTPD	4 MTPD + 7 MTPD	4 MTPD + 7 MTPD	4 MTPD + 7 MTPD	4 MTPD + 7 MTPD
PA IV Heater	Limiting Standard	April 2023	May 2023	June 2023	July 2023	August 2023	September 2023
		-	23-05-2023	19-06-2023	28-07-2023	-	14-09-2023
TPM (mg/Nm³)	100	-	54.35	48.88	38.50	-	41.71
SO₂ (Kg/day)	360	-	8.78	4.87	4.46	-	10.96
Nox (mg/Nm³)	450	-	65.76	56.85	73.61	-	62.15
CO ppm	200	-	14.30	12.0	14.30	-	13.40
Acid mist (mg/Nm³)	35	-	7.94	8.77	9.83	-	14.23

D

Boiler Stack Emission Monitoring							
Physical Data:		April 2023	May 2023	June 2023	July 2023	August 2023	September 2023
Stack Height (m)		55 m					
Inside Diameter (m)		2.6 m					
Stack Area (m²)		5.31 m ²					
Flue Gas Temperature (°C)		175 °C	172 °C	147 °C	154 °C	174 °C	176 °C
Velocity m/sec		4.97 m/sec	5.45 m/sec	2.10 m/sec	2.23 m/sec	6.05 m/sec	2.18 m/sec
Flow m³/hr.		54787 m ³ /hr.	67886 m ³ /hr.	29312 m ³ /hr.	29102 m ³ /hr.	75046 m ³ /hr.	26630 m ³ /hr.
Fuel Used		Furnace Oil					
Fuel Quantity		27 MTPD (maximum)					
Boiler	Limiting standard	April 2023	May 2023	June 2023	July 2023	August 2023	September 2023
		13-04-2023	24-05-2023	20-06-2023	28-07-2023	21-08-2023	13-09-2023
TPM(mg/Nm³)	100	54.02	64.49	55.87	36.21	40.44	74.20
Nox Conc (mg/Nm³)	450	39.76	34.28	45.27	80.61	75.85	67.69
SO₂ (Kg/Day)	2430	93.03	54.92	36.03	36.77	80.19	55.10
CO mg/Nm³	200	21.31	20.68	14.35	12.41	10.06	10.06

E

Scrubber Stack Emission Monitoring - PA I							
Physical Data:		April 2023	May 2023	June 2023	July 2023	August 2023	September 2023
Stack Height (m)		50 m					
Inside Diameter (m)		1.99 m					
Stack Area (m²)		3.11 m ²					
Flue Gas Temperature (°C)		47 °C	50 °C	44 °C	45 °C	42 °C	48 °C
Velocity m/sec		8.37 m/sec	9.04 m/sec	6.68 m/sec	7.77 m/sec	6.97 m/sec	7.26 m/sec
Flow m³/hr.		85647 m ³ /hr	79513 m ³ /hr	67633 m ³ /hr	73780 m ³ /hr	68066 m ³ /hr	72319 m ³ /hr
PA I Scrubber	Limiting Standard	April 2023	May 2023	June 2023	July 2023	August 2023	September 2023
		13-04-2023	23-05-2023	19-06-2023	28-07-2023	22-08-2023	13-09-2023
TOC (mg/Nm³)	150	ND	ND	ND	ND	ND	ND
SO₂ (mg/Nm³)	850	<0.5	<5.0	<0.5	<0.5	<0.5	<5.0
TPM (mg/Nm³)	50	33.12	44.69	39.29	34.60	30.75	26.79
NO_x (mg/Nm³)	350	12.5	19.74	19.74	18.60	14.65	11.63
Acid mist (mg/Nm³)	35	<1.0	<1.0	<1.0	14.67	7.76	9.25
ND - NOT DETECTED							

F

Scrubber Stack Emission Monitoring - PA II							
Physical Data:		April 2023	May 2023	June 2023	July 2023	August 2023	September 2023
Stack Height (m)		50 m					
Inside Diameter (m)		1.69 m					
Stack Area (m²)		2.24 m ³	2.24 m ²				
Flue Gas Temperature (°C)		46 °C	42 °C	46 °C	42 °C	45 °C	47 °C
Velocity m/sec		7.99 m/sec	8.82 m/sec	6.85 m/sec	6.80 m/sec	7.16 m/sec	7.61 m/sec
Flow m³/hr.		58967 m ³ /hr	59313 m ³ /hr	49911 m ³ /hr	46873 m ³ /hr	48317 m ³ /hr	55502 m ³ /hr
PA - II Scrubber	Limiting Standard	April 2023	May 2023	June 2023	July 2023	August 2023	September 2023
		13-04-2023	24-05-2023	24-06-2023	28-07-2023	21-08-2023	14-09-2023
TOC (mg/Nm³)	150	ND	ND	ND	ND	ND	ND
SO₂ (ppm)	1700	<0.5	<0.5	<0.5	<0.5	<0.5	<5.0
TPM (mg/Nm³)	100	35.61	48.55	42.36	6.80	36.54	29.86
Nox (mg/Nm³)	450	11.4	48.55	40.01	25.61	20.10	17.90
Acid mist (mg/Nm³)		7.51	<0.1	<0.1	12.36	15.47	13.90
ND - NOT DETECTED							

G

Scrubber Stack Emission Monitoring - PA III							
Physical Data:		April 2023	May 2023	June 2023	July 2023	August 2023	September 2023
Stack Height (m)		51 m	50 m				
Inside Diameter (m)		1.69 m					
Stack Area (m²)		2.24 m ³	2.24 m ²				
Flue Gas Temperature (°C)		41 °C	445 °C	41 °C	49 °C	42 °C	42 °C
Velocity m/sec		7.47m/sec	7.70 m/sec	6.83 m/sec	7.44 m/sec	7.14 m/sec	6.88 m/sec
Flow m³/hr.		55187 m ³ /hr	52526 m ³ /hr	51932 m ³ /hr	50602 m ³ /hr	50028 m ³ /hr	50054 m ³ /hr
PA III Scrubber	Limiting standard	April 2023	May 2023	June 2023	July 2023	August 2023	September 2023
		14-04-2023	24-05-2023	19-06-2023	28-07-2023	21-08-2023	13-09-23
TOC (mg/Nm³)	150	ND	ND	ND	ND	ND	ND
SO₂ (ppm)	1700	<0.5	<0.5	<0.5	<0.5	<0.5	<5.0
TPM (mg/Nm³)	100	30.40	38.11	32.37	31.70	39.36	33.44
Nox (mg/Nm³)	450	10.5	17.66	22.11	20.35	25.97	21.82
Acid mist (mg/Nm³)	35	<0.1	<0.1	<1.0	13.51	9.85	11.82
ND - NOT DETECTED							

H

Scrubber Stack Emission Monitoring - PA IV							
Physical Data:		April 2023	May 2023	June 2023	July 2023	August 2023	September 2023
Stack Height (m)		50 m	50 m	50 m	50 m	50 m	50 m
Inside Diameter (m)		1.69 m	1.69 m	1.69 m	1.69 m	1.69 m	1.69 m
Stack Area (m²)		2.24 m ²	2.24 m ²	2.24 m ²	2.24 m ²	2.24 m ²	2.24 m ²
Flue Gas Temperature (°C)		°C	44 °C	44 °C	43 °C	°C	43 °C
Velocity m/sec		m/sec	8.50 m/sec	6.53 m/sec	6.84 m/sec	m/sec	6.72 m/sec
Flow m³/hr.		m ³ /hr	57737 m ³ /hr	47895 m ³ /hr	46652 m ³ /hr	m ³ /hr	48190 m ³ /hr
PA IV Scrubber	Limiting standard	April 2023	May 2023	June 2023	July 2023	August 2023	September 2023
		-	24-05-2022	19-06-2023	29-07-2023	-	14-09-2023
TOC (mg/Nm³)	150	ND	ND	ND	ND	-	ND
SO₂ (ppm)	850	-	<0.5	<0.5	<0.5	-	<5.0
TPM	50	-	42.15	37.19	30.86	-	27.52
Nox	350	-	29.09	26.44	23.67	-	20.87
Acid mist (mg/Nm³)	35	-	<1.0	<1.0	10.86	-	15.50
ND- Not Detected							

Stack Emission Monitoring - PA Dedusting 1

Physical Data:		April 2023	May 2023	June 2023	July 2023	August 2023	September 2023
Stack Height (m)		12 m					
Inside Diameter (m)		0.35 m	0.35 m	0.35 m	0.4 m	0.35 m	0.35 m
Stack Area (m²)		0.1 m ²					
Flue Gas Temperature (°C)		46 °C	47 °C	42 °C	38 °C	42 °C	46 °C
Velocity m/sec		8.59 m/sec	9.07 m/sec	8.14 m/sec	8.32 m/sec	5.80 m/sec	7.93 m/sec
Flow m³/hr.		2927 m ³ /hr	2878 m ³ /hr	2592 m ³ /hr	2695 m ³ /hr	1871 m ³ /hr	2327 m ³ /hr
PA Dedusting 1	Limiting standard	April 2023	May 2023	June 2023	July 2023	August 2023	September 2023
		14-04-2022	22-05-2023	20-06-2023	29-07-2023	22-08-2023	18-09-2023
TOC (mg/Nm³)	150	ND	ND	ND	ND	ND	ND
TPM (mg/Nm³)	150	34.30	40.84	30.21	8.69	10.05	10.11
Acid mist (mg/Nm³)	35	<1.0	<1.0	<0.1	<1.0	<1.0	<1.0
ND- Not Detected							

Stack Emission Monitoring - PA Dedusting 2

Physical Data:		April 2023	May 2023	June 2023	July 2023	August 2023	September 2023
Stack Height (m)		12 m					
Inside Diameter (m)		0.35 m					
Stack Area (m²)		0.1 m ²					
Flue Gas Temperature (°C)		45 °C	46 °C	43 °C	36 °C	46 °C	48 °C
Velocity m/sec		10.02 m/sec	12.0 m/sec	10.73 m/sec	10.72 m/sec	11.81 m/sec	11.35 m/sec
Flow m³/hr.		3200 m ³ /hr	3819 m ³ /hr	3468 m ³ /hr	3483 m ³ /hr	3753 m ³ /hr	3578 m ³ /hr
PA Dedusting 2	Limiting standard	April 2023	May 2023	June 2023	July 2023	August 2023	September 2023
		14-04-2022	22-05-2023	20-06-2023	29-07-2023	22-08-2023	15-09-2023
TOC (mg/Nm³)	150	ND	ND	ND	ND	ND	ND
TPM (mg/Nm³)	150	37.82	39.46	26.30	8.09	12.63	7.66
Acid mist (mg/Nm³)	35	<1.0	<1.0	<0.1	<1.0	<1.0	<1.0
ND- Not Detected							

K

Scrubber Stack Emission Monitoring - PA Dedusting 3							
Physical Data:		April 2023	May 2023	June 2023	July 2023	August 2023	September 2023
Stack Height (m)		12 m					
Inside Diameter (m)		0.35 m					
Stack Area (m²)		0.1 m ²					
Flue Gas Temperature (°C)		48 °C	47 °C	45 °C	37 °C	43 °C	43 °C
Velocity m/sec		13.88 m/sec	12.10 m/sec	8.07 m/sec	8.00 m/sec	12.71 m/sec	12.35 m/sec
Flow m³/hr.		5757 m ³ /hr	5024 m ³ /hr	3339 m ³ /hr	3398 m ³ /hr	4071 m ³ /hr	5180 m ³ /hr
PA Dedusting 3	Limiting standard	April 2023	May 2023	June 2023	July 2023	August 2023	September 2023
		14-04-2022	22-05-2023	20-06-2023	29-07-2023	22-08-2023	15-09-2023
TOC (mg/Nm³)	150	ND	ND	ND	ND	ND	ND
TPM (mg/Nm³)	150	30.14	45.85	24.05	9.64	7.51	8.33
Acid mist (mg/Nm³)	35	<1.0	<1.0	<1.0	-	<1.0	<1.0
ND- Not Detected							

L

Stack Emission Monitoring - PA Dedusting 4							
Physical Data:		April 2023	May 2023	June 2023	July 2023	August 2023	September 2023
Stack Height (m)		12 m	12 m	12 m	12 m	12 m	12 m
Inside Diameter (m)		0.35 m	0.35 m	0.35 m	0.35 m	0.35 m	0.35 m
Stack Area (m²)		0.1 m ²	0.1 m ²	0.1 m ²	0.1 m ²	0.1 m ²	0.1 m ²
Flue Gas Temperature (°C)		44 °C	48 °C	47°C	33 °C	°C	42 °C
Velocity m/sec		4.90 m/sec	9.10 m/sec	8.69 m/sec	9.23 m/sec	m/sec	9.01 m/sec
Flow m³/hr.		2058 m ³ /hr	3779 m ³ /hr	3572 m ³ /hr	3851 m ³ /hr	m ³ /hr	3780 m ³ /hr
PA Dedusting 4	Limiting standard	April 2023	May 2023	June 2023	July 2023	August 2023	September 2023
		14-04-2022	22-05-2023	20-06-2023	29-07-2023	-	15-09-2023
TOC (mg/Nm³)	150	ND	ND	ND	ND	-	ND
TPM (mg/Nm³)	150	28.16	35.38	22.01	7.08	-	10.11
Acid mist (mg/Nm³)	25	<1.0	<1.0	<1.0	<1.0	-	<1.0
ND- Not Detected							

M

Scrubber Stack Emission Monitoring - MA Bagging							
Physical Data:		April 2023	May 2023	June 2023	July 2023	August 2023	September 2023
Stack Height (m)		30 m	30 m	30 m	30 m	30 m	30 m
Inside Diameter (m)		0.264 m	0.264 m	0.264 m	0.264 m	0.264 m	0.264 m
Stack Area (m ²)		0.0547 m ²	0.0547 m ²	0.0547 m ²	0.0547 m ²	0.0547 m ²	0.0547 m ²
Flue Gas Temperature (°C)		42 °C	45 °C	43 °C	38 °C	44 °C	44 °C
Velocity m/sec		8.47 m/sec	5.23 m/sec	6.30 m/sec	7.11 m/sec	5.73 m/sec	2.25 m/sec
Flow m ³ /hr.		1483 m ³ /hr	950 m ³ /hr	965 m ³ /hr	1317 m ³ /hr	1050 m ³ /hr	412 m ³ /hr
MA bagging	Limiting standard	April 2023	May 2023	June 2023	July 2023	August 2023	September 2023
		15-04-2023	22-05-2023	21-06-2023	29-07-2023	23-08-2023	16-09-2023
TOC (mg/Nm ³)	150	ND	ND	ND	ND	ND	ND
TPM (mg/Nm ³)	150	29.10	39.29	43.31	23.64	20.17	12.67
Acid Mist (mg/Nm ³)	35	<1.0	<1.0	<1.0	<1.0	<1.0	<1.0
ND- Not Detected							

N

Scrubber Stack Emission Monitoring - MA Flaker							
Physical Data:		April 2023	May 2023	June 2023	July 2023	August 2023	September 2023
Stack Height (m)		30 m					
Inside Diameter (m)		0.264 m					
Stack Area (m ²)		0.0547 m ²					
Flue Gas Temperature (°C)		43 °C	47 °C	41 °C	40 °C	44 °C	43 °C
Velocity m/sec		7.4 m/sec	5.98 m/sec	5.95 m/sec	6.50 m/sec	5.97 m/sec	5.46 m/sec
Flow m ³ /hr.		1367 m ³ /hr	1082 m ³ /hr	1093 m ³ /hr	1192 m ³ /hr	1288 m ³ /hr	1001 m ³ /hr
MA flaker	Limiting standard	April 2023	May 2023	June 2023	July 2023	August 2023	September 2023
		15-04-2023	22-05-2023	21-06-2023	29-07-2023	23-08-2023	16-09-2023
TOC (mg/Nm ³)	150	ND	ND	ND	ND	ND	ND
TPM (mg/Nm ³)	150	34.26	41.71	36.84	10.28	17.73	12.20
Acid mist (mg/Nm ³)		<1.0	<1.0	<1.0	<1.0	<1.0	<1.0
ND- Not Detected							

O

Stack Emission Monitoring DG 2250 KVA							
Physical Data:		April 2023	May 2023	June 2023	July 2023	August 2023	September 2023
Stack Height (m)		30 m					
Inside Diameter (m)		0.5 m					
Stack Area (m ²)		0.196 m ²					
Flue Gas Temperature (°C)		165 °C	150 °C	139 °C	141 °C	131 °C	155 °C
Velocity m/sec		7.07 m/sec	7.09 m/sec	7.05 m/sec	7.21 m/sec	6.84 m/sec	6.80 m/sec
Flow m ³ /hr.		3316 m ³ /hr.	3430 m ³ /hr.	3496 m ³ /hr.	3548 m ³ /hr.	3463 m ³ /hr.	3270 m ³ /hr.
Fuel Used		HSD	HSD	HSD	HSD	HSD	HSD
DG 2250 KVA	Limiting standard	April 2023	May 2023	June 2023	July 2023	August 2023	September 2023
		14-04-2023	24-05-2023	20-06-2023	28-07-2023	21-08-2023	16-09-2023
TPM(mg/Nm ³)	100	51.52	60.03	55.03	46.81	49.44	39.23
Nox conc (mg/Nm ³)	450	35.34	61.58	67.69	62.50	79.00	69.20
SO ₂ (mg/Nm ³)	1700	3.71	38.31	43.57	50.32	50.23	38.66
CO (mg/Nm ³)	200	4.31	20.34	11.57	14.70	15.60	10.25

P

Stack Emission Monitoring DG 2000 KVA							
Physical Data:		April 2023	May 2023	June 2023	July 2023	August 2023	September 2023
Stack Height (m)		30 m	30 m				
Inside Diameter (m)		0.5 m	0.5 m				
Stack Area (m ²)		0.196 m ²	0.196 m ²				
Flue Gas Temperature (°C)		160 °C	148 °C	174 °C	170 °C	138 °C	°C
Velocity m/sec		6.84 m/sec	7.14 m/sec	7.08 m/sec	6.84 m/sec	6.53 m/sec	m/sec
Flow m ³ /hr.		3263 m ³ /hr.	3488 m ³ /hr.	3297 m ³ /hr.	3117 m ³ /hr.	3245 m ³ /hr.	m ³ /hr.
Fuel Used		HSD	HSD	HSD	HSD	HSD	HSD
DG 2000 KVA	Limiting standard	April 2023	May 2023	June 2023	July 2023	August 2023	September 2023
		13-04-2023	24-05-2023	20-06-2023	28-07-2023	21-08-2023	-
TPM(mg/Nm ³)	100	44.81	56.76	51.42	53.68	53.76	-
Nox conc (mg/Nm ³)	450	33.02	30.20	33.32	70.62	67.99	-
SO ₂ (mg/Nm ³)	1700	3.33	34.27	62.68	62.68	44.80	-
CO (mg/Nm ³)	200	18.47	19.86	15.13	16.85	14.70	-

ANNEXURE III

A) DATA ON WATER CONSUMPTION

PERIOD: April 2023 TO September 2023

MIDC Raw water receipt (Apr-2023 to Sept-2023)		
Month	Raw water per month	Raw water per day
April 2023	103530	3451.0
May 2023	107360	3463.2
June 2023	79370	2645.7
July 2023	77230	2491.3
August 2023	85880	2770.3
September 2023	92140	3071.3
Average	90918.3	2982.1

B) DATA ON EFFLUENT GENERATION

PERIOD: April 2023 TO September 2023

CONSENTED EFFLUENT DISCHARGE TO CETP- 220 M3/DAY

Effluent discharged to CETP (Apr-2023 to Sept-2023)		
Month	Effluent per month	Effluent per day
April 2023	3644.7	121.5
May 2023	3840.7	123.9
June 2023	2665.9	88.9
July 2023	2483.6	80.1
August 2023	2582.9	83.3
September 2023	2444.6	81.5
Average	2943.7	96.5

ANNEXURE – IV

RESIDUE GENERATION DATA

PERIOD – April 2023 TO September 2023

MPCB Limit – 455.65 MT/M

Month	Residue Generation (MT)
April 2023	272.89
May 2023	349.53
June 2023	279.41
July 2023	311.25
August 2023	243.72
September 2023	299.70

<Dial 1800266688> <Wear Masks, Stay Safe>



EN181050064IN IVR:6977181050064
SP TALDA A.V. S.O <410208>
Counter No:1,02/06/2023,13:53
To:THE DIRECTOR, MINISTRY OF ENV
PIN:110003, Lodi Road ND
From:1 G PETROCH, PLOT NO T-2 NDC
Wt:995gms
Amt:79.40(Cash)Tax:14.40
<Track on www.indiapost.gov.in>
<Dial 1800266688> <Wear Masks, Stay Safe>

99:40

EN181050076IN IVR:6977181050076
SP TALDA A.V. S.O <410208>
Counter No:1,02/06/2023,13:53
To:CENTRAL POLICE, PAVESH BHAWA
PIN:390123, Subhanpura SO
From:1 G PETROCH, PLOT NO T-2 NDC
Wt:490gms
Amt:70.80(Cash)Tax:10.80
<Track on www.indiapost.gov.in>
<Dial 1800266688> <Wear Masks, Stay Safe>

70:80

EN181050081IN IVR:6977181050081
SP TALDA A.V. S.O <410208>
Counter No:1,02/06/2023,13:53
To:THE MEMBER SE, N POLLUTION COM
PIN:400022, Sion SO
From:1 G PETROCH, PLOT NO T-2 NDC
Wt:495gms
Amt:35.40(Cash)Tax:5.40
<Track on www.indiapost.gov.in>

35:40

Dhairyasheel Shinde

From: Dhairyasheel Shinde
Sent: 01 June 2023 15:19
To: ecompliance-mh@gov.in
Subject: Submission of Six Monthly Environmental Clearance Compliance Status Report.
Attachments: EC COMPLINACE REPORT - OCT 2022 TO MAR 2023.pdf

**The Director
Ministry of Environment, Forest & Climate Change,
Indira Paryavaran Bhavan, Aliganj, Jorbagh Road,
New Delhi – 110 003**

**Sub: Submission of Six Monthly Environmental Clearance Compliance Status Report.
Ref.: Environmental clearances granted for expansion of petrochemical unit, by MOEF &
CC vides clearance no.**

- 1) PA-I EXPANSION EC NO-J-11013/14/2007-IA II (I) dated: 12th June, 2007.
- 2) PA-II EC NO -J-11012/78/96-IA dated 20th June 1997.
- 3) PA-III & BENZOIC ACID EC NO- J-11011/994/2007/IA (II) I, Dated: 03.12.2009.
- 4) PA-IV,MA-IV,BENZOIC ACID EXPANSION-PLASTICIZER EC NO J-1011/73/2016-IA-II (I),
Dated : 18th July, 2017 & amendment in same is received on 20th February 2018.
- 5) MA-III EC NO -J-11011/986/2007-IA -II(I) dated 2nd April 2008.

Dear Sir,

With reference to the above we are submitting herewith our half yearly compliance status report as per condition stipulated in Environmental Clearance for period of **OCT 2022 – MAR 2023**. We hope the above is to your satisfaction.

Thanking You,

**Yours faithfully
FOR I. G. PETROCHEMICALS LTD**

**(J K SABOO)
EXECUTIVE DIRECTOR**

CC to:

1. The CCF, Regional Office, Western Region, Ministry of Environment, Forests & Climate Regional Office (WCZ), Ground Floor, East Wing, New Secretariat Building, Civil Lines, Nagpur-440001
2. The Member Secretary, Maharashtra Pollution Control Board, 3rd floor, Kalpataru Point, Sion, Mumbai – 400 022.

Dhairyasheel Shinde

From: Dhairyasheel Shinde
Sent: 01 June 2023 15:21
To: archituprit.cpcb@nic.in
Subject: Submission of Six Monthly Environmental Clearance Compliance Status Report.
Attachments: EC COMPLINACE REPORT - OCT 2022 TO MAR 2023.pdf

**The Director
Ministry of Environment, Forest & Climate Change,
Indira Paryavaran Bhavan, Aliganj, Jorbagh Road,
New Delhi – 110 003**

**Sub: Submission of Six Monthly Environmental Clearance Compliance Status Report.
Ref.: Environmental clearances granted for expansion of petrochemical unit, by MOEF &
CC vides clearance no.**

- 1) PA-I EXPANSION EC NO-J-11013/14/2007-IA II (I) dated: 12th June, 2007.**
- 2) PA-II EC NO -J-11012/78/96-IA dated 20th June 1997.**
- 3) PA-III & BENZOIC ACID EC NO- J-11011/994/2007/IA (II) I, Dated: 03.12.2009.**
- 4) PA-IV,MA-IV,BENZOIC ACID EXPANSION-PLASTICIZER EC NO J-1011/73/2016-IA-II (I),
Dated : 18th July, 2017 & amendment in same is received on 20th February 2018.**
- 5) MA-III EC NO -J-11011/986/2007-IA -II(I) dated 2nd April 2008.**

Dear Sir,

With reference to the above we are submitting herewith our half yearly compliance status report as per condition stipulated in Environmental Clearance for period of **OCT 2022 – MAR 2023**. We hope the above is to your satisfaction.

Thanking You,

**Yours faithfully
FOR I. G. PETROCHEMICALS LTD**

**(J K SABOO)
EXECUTIVE DIRECTOR**

CC to:

- 1. The CCF, Regional Office, Western Region, Ministry of Environment, Forests & Climate Regional Office (WCZ), Ground Floor, East Wing, New Secretariat Building, Civil Lines, Nagpur-440001**
- 2. The Member Secretary, Maharashtra Pollution Control Board, 3rd floor, Kalpataru Point, Sion, Mumbai – 400 022.**

ANNEXURE - VI

Photographs of Raw Material Storage









Annexure - VII

EXISTING GREEN BELT AREA

PROPOSED GREEN BELT AREA

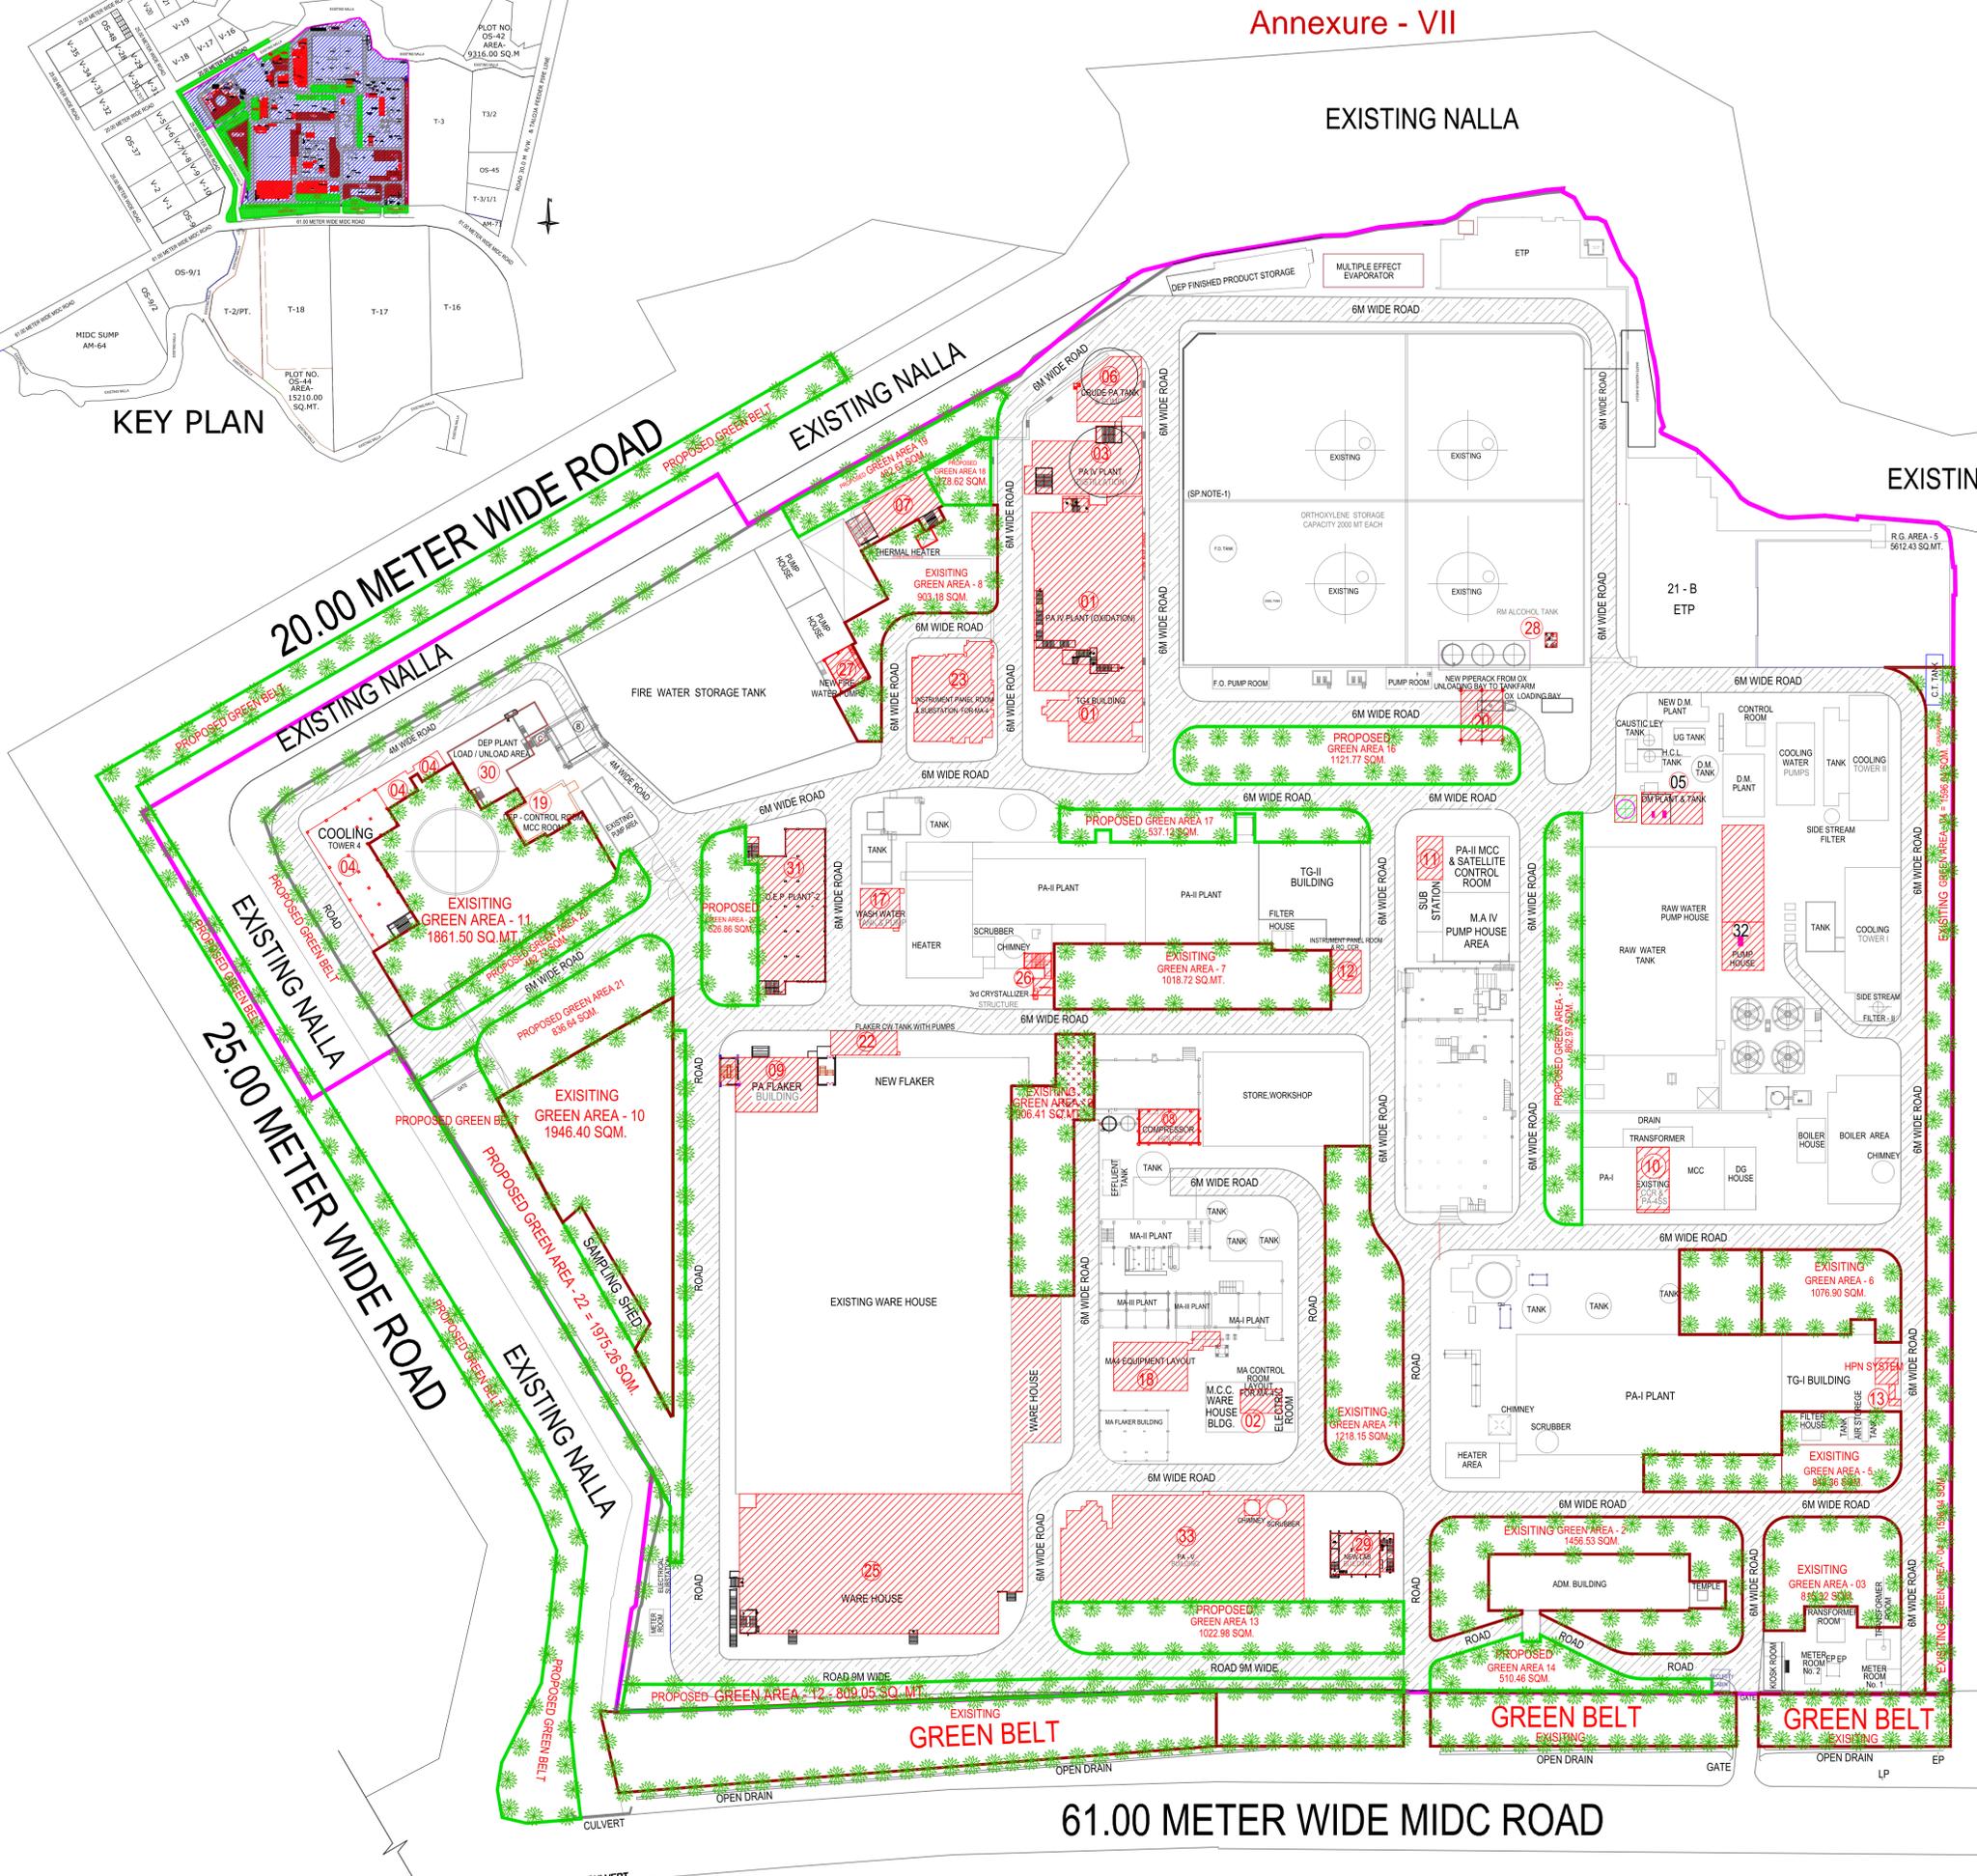

PROPOSED BUILDING AREA STATEMENT

SR. NO.	DESCRIPTION
01	PA IV PLANT (OXIDATION)
02	PA-IV TG-4 BUILDING
03	M.A. CONTROL ROOM LAYOUT
04	PA-IV DISTILLATION
05	COOLING TOWER
06	SIDE STREAM FILTER
07	BLOW DOWN PIT
08	DM PLANT & TANK
09	CRUDE PA & PURE PA
10	PA-IV THERMAL HEATER AREA
11	COMPRESSOR HOUSE
12	PA FALKER HOUSE
13	EXISTING CCR & PA-4SS
14	M.A IV - PUMP HOUSE & SUBSTATION
15	INSTRUMENT PANEL ROOM & RO_CCR
16	HPN SYSTEM
17	WASH WATER TANK
18	MA-4 - EQUIPMENT LAYOUT
19	DEP - CONTROL ROOM & MCC ROOM
20	OX LOADING BAY
21	AREA FOR NEW ETP EQUIPMENT LAYOUT
22	FLAKER CW SYSTEM
23	INSTRUMENT PANEL ROOM & SUBSTATION FOR MA-4
24	02 ETP-MEE-ATFD
25	EXTENDED WAREHOUSE
26	EQUIPMENT LAYOUT PLAN & 3RD CRYSTALLIZER IN PA - 2 PLANT
27	FW PUMP HOUSE
28	RM ALCOHOL TANK
29	NEW LAB BUILDING
30	D.E.P PLANT & LOAD / UNLOAD AREA
31	D.E.P. PLANT 2
32	RAW WATER PUMP HOUSE
33	PA V BUILDING

NAME OF OWNER
IG PETROCHEMICALS LIMITED.

DESCRIPTION OF PROPOSAL AND PROPERTY

PROPOSED FACTORY BUILDING FOR IG PETROCHEMICALS LTD., ON PLOT NO. T2, T2/1, V45, V11 & V12, V13, V14 & T1, TALOJA M.I.D.C. AREA, TAL - PANVEL, DIST- RAIGAD.

NAME OF OWNER

IG PETROCHEMICAL LTD

NAME OF ARCHITECT

M.R. KASHELKAR & CO.

ARCHITECT AND INTERIOR DESIGNER
45/415, GLOMERAL PARK, PUNE-411 004.
REG-117, MIDC RESIDENTIAL ZONE,
MIDC, GANPATI NAGAR,
DOMBIVLI (E) 41 201,
PHONE-98100788

IG PETROCHEMICALS LIMITED.

PROPOSED FACTORY BUILDING FOR IG PETROCHEMICALS LTD., FOR PA - 5 ON PLOT NO. T2, T2/1, V45, V11 & V12, V13, V14 & T1, TALOJA M.I.D.C. AREA, TAL - PANVEL, DIST- RAIGAD.

AREA STATEMENT		SQ. MT.
1	AREA OF THE PLOT	113282.00
2	LESS - NALLA AREA	3838.92
3	TOTAL NET AREA OF THE PLOT	109443.08
4	GREEN BELT AREA REQUIRED 33%	36116.22
	EXISTING GREEN BELT AREA (12%)	13313.45
	PROPOSED GREEN BELT AREA (14%)	16751.18
	EXISTING GREEN BELT AREA OUTSIDE OF THE PLOT (4%)	4149.00
	PROPOSED GREEN BELT AREA OUTSIDE OF THE PLOT (5%)	6069.00
5	PROPOSED TOTAL GREEN BELT AREA	39282.63
6	TOTAL GREEN BELT PROPOSED IN PERCENTAGE	36%

SIGNATURE OF ARCHITECT					
JOB NO	DRG NO	DATE	FOR	DRAWN BY	CHECKED BY
0-21/18-19	EC - 01	18-12-2021	CANCELLED	PPS	KMK
0-21/18-19	EC - 02	25-12-2021	CANCELLED	PPS	KMK
0-21/18-19	EC - 03	30-04-2022	CANCELLED	PPS	KMK
0-21/18-19	EC - 04	10-05-2022	CANCELLED	PPS	KMK
0-21/18-19	EC - 05	01-06-2022	CANCELLED	PPS	KMK
0-21/18-19	EC - 06	01-07-2022	APPROVAL	PPS	KMK

NOTE: THIS DRAWING IS THE PROPERTY OF MRS. M.R. KASHELKAR & CO. DOMBIVLI AND SHOULD NOT BE REPRODUCED, COPIED OR HANDED OVER TO A THIRD PARTY AND USED FOR ANY PURPOSE OTHER THAN FOR WHICH IT IS INTENDED.

ANNEXURE VIII

Note on Occupational Health Surveillance Programme & Proper housekeeping and adequate occupational health programme

1. All employees and contract employees are undergoing bi-annually medical check up every year in the month of January and July through Certifying Surgeon appointed by State Government of Maharashtra.
2. These medical check ups includes general medical examination, weight, height, eye sight, Blood Pressure, lung function test, routine blood examination, routine urine examination and X-ray once in a year.
3. Medical check up reports are available since 2006. As due to flood in July, 2005 all records since commissioning of the plant at Taloja have been lost.
4. Pre-employment medical check up is being carried out for each new recruitee.
5. Employees if meets with any accident or fall sick during the working ours, such employees is admitted or giving treatment in Dr. Gandhi's Hospital, Panvel located at about 14 KM from factory.
6. Full time appointed qualified doctor is appointed as medical officer and is available in factory during general shift. First aid facility is provided at the factory and managed by a whole time during in the General shift. During wee hours first aid Center is looked by mail nurse.
7. First aid centre is equipped with oxygen cylinder, Breathing Apparatus and essential medicines.
8. Ambulance is stationed at factory for all 24 hours and equipped with 2 structures and 2 oxygen cylinders and other accessories.
9. First aid training programmes are conducted every alternative month and about 70 employees trained in first aid.
10. First aider training of employees is being conducted by St. Johns Ambulance Institute, which has nation wide network. Retraining of first aider training is being carried out.

Aspira pathlab & Diagnostics ltd



HEALTH REGISTER

I G PETROCHEMICALS LIMITED

Dr. Pankaj shah
M.D., A.F.I.H., M.B.B.S.,
Industrial Health Consultant

Name of Certifying Surgeon

Dr. Pankaj Shah

Regd. No. 51279

FORM NO. 7

HEALTH REGISTER

From :- 09-03-2023 To 09-03-2024

(In respect of persons employed in occupations declared to be dangerous operations under Sections 87)

Note : (i) Column 8, Detailed summary of reason for transfer of discharge should be stated.

Note : (ii) Column II, should be expressed as Fit/Unfit/Suspended.

Sr. No.	Form No.	EC. No.	Name of Worker	sex	Age (last birth day)	Date of employment of present work	Date of leaving or transfer to other work	Reason for leaving, transfer or discharge	Nature of job or occupation	Raw material or Bye product handled	Date of medical examination by Certifying Surgeon and Result of Medical Examination	If suspended from work state period of suspension with detailed reasons	Certified fit to resume duty on with Signature of certifying Surgeon	If certificate of unfitness or suspension issued to worker	Signature with Certifying Surgeon
1	2	120011	Shankar Lal Sharma	Male	36		--	--	Accounts		09-03-2023 Fit	Not Applicable	Not Applicable		
2	7	160058	Akhil S. Ingle	Male	46		--	--	Projects		09-03-2023 Fit	Not Applicable	Not Applicable		
3	8	240022	Vijay G. Kasar	Male	56		--	--	Quality Control		09-03-2023 Fit	Not Applicable	Not Applicable		
4	9	130012	Renold C. Pinto	Male	50		--	--	HR Admin		09-03-2023 Fit	Not Applicable	Not Applicable		
5	10	160013	Aniket P. Kadam	Male	29		--	--	Purchase		09-03-2023 Fit	Not Applicable	Not Applicable		
6	12	112006	Mini C. Warriar	Female	53		--	--	Accounts		09-03-2023 Fit	Not Applicable	Not Applicable		
7	13	FTA	BAMA N. BALKAR	Male	53		--	--	Admin		09-03-2023 Fit	Not Applicable	Not Applicable		
8	14	230126	Pawan V. Choudhari	Male	36		--	--	Instrument		09-03-2023 Fit	Not Applicable	Not Applicable		
9	15	230117	Santosh Temghare	Male	39		--	--	Instrument		09-03-2023 Fit	Not Applicable	Not Applicable		
10	20	250281	Dornadula A. Reddy	Male	55		--	--	Production		09-03-2023 Fit	Not Applicable	Not Applicable		
11	21	250311	Soymon Thomas P.	Male	52		--	--	Production		09-03-2023 Fit	Not Applicable	Not Applicable		
12	22	240019	Ram Krishna Shodhale	Male	53		--	--	Lab		09-03-2023 Fit	Not Applicable	Not Applicable		
13	24	190016	Gokul B. Khatode	Male	45		--	--	Safety		09-03-2023 Fit	Not Applicable	Not Applicable		
14	25	FTA	PRADEEP SALUNKHE	Male	56		--	--	Security Incharge		09-03-2023 Fit	Not Applicable	Not Applicable		
15	29	250341	Karthigairaj	Male	38		--	--	Production		09-03-2023 Fit	Not Applicable	Not Applicable		
16	30	250373	Kumar D. Thakur	Male	31		--	--	PA Production		09-03-2023 Fit	Not Applicable	Not Applicable		
17	33	250364	Gokeshanath J. Patil	Male	35		--	--	Boiler		09-03-2023 Fit	Not Applicable	Not Applicable		
18	35	240021	Vaibhav B. Patil	Male	40		--	--	Quality Control		09-03-2023 Fit	Not Applicable	Not Applicable		

Name of Certifying Surgeon

Dr. Pankaj ShahRegd. No. 51279

FORM NO. 7

HEALTH REGISTER

From :- 09-03-2023 To 09-03-2024

(In respect of persons employed in occupations declared to be dangerous operations under Sections 87)

Note : (i) Column 8, Detailed summary of reason for transfer of discharge should be stated.

Note : (ii) Column II, should be expressed as Fit/Unfit/Suspended.

Sr. No.	Form No.	EC. No.	Name of Worker	sex	Age (last birthday)	Date of employment of present work	Date of leaving or transfer to other work	Reason for leaving, transfer or discharge	Nature of job or occupation	Raw material or Bye product handled	Date of medical examination by Certifying Surgeon and Result of Medical Examination	If suspended from work safe period of suspension with detailed reasons	Certified fit to resume duty on with Signature of certifying Surgeon	If certificate of unfitness or suspension issued to worker	Signature with Certifying Surgeon
19	36	250388	Jagdish B. Patil	Male	40		--	--	Production		09-03-2023 Fit	Not Applicable	Not Applicable		
20	37	240024	Atul S. Marwade	Male	56		--	--	Lab		09-03-2023 Fit	Not Applicable	Not Applicable		
21	41	250371	Sharad C. Gonbare	Male	30		--	--	Production		09-03-2023 Fit	Not Applicable	Not Applicable		
22	42	250495	Sagar A. Shinde	Male	29		--	--	Production		09-03-2023 Fit	Not Applicable	Not Applicable		
23	44	240027	Siddhesh B. Gharat	Male	29		--	--	Lab		09-03-2023 Fit	Not Applicable	Not Applicable		
24	46	190020	Dhiraj Patil	Male	26		--	--	EHS		09-03-2023 Fit	Not Applicable	Not Applicable		
25	47	190015	Ankit Shrivedi	Male	32		--	--	EHS		09-03-2023 Fit	Not Applicable	Not Applicable		
26	51	190008	Bindeshwar P. Shah	Male	51		--	--	Safety		09-03-2023 Fit	Not Applicable	Not Applicable		
27	52	250436	Rahul R. Patil	Male	25		--	--	Production		09-03-2023 Fit	Not Applicable	Not Applicable		
28	54	FTA	Narayan Pardhi	Male	47		--	--	Security		09-03-2023 Fit	Not Applicable	Not Applicable		
29	55	200005	Chandrashekhar K. Joshi	Male	56		--	--	Projects		09-03-2023 Fit	Not Applicable	Not Applicable		
30	59	250430	Girdhar Rajwans	Male	32		--	--	Production		09-03-2023 Fit	Not Applicable	Not Applicable		
31	66	150012	Rupak B. Kamik	Male	37		--	--	Ergg. Stores		09-03-2023 Fit	Not Applicable	Not Applicable		
32	67	250490	Ketan S. Baikar	Male	27		--	--	MA Production		09-03-2023 Fit	Not Applicable	Not Applicable		
33	75	110014	Santosh Kumar Pandey	Male	52		--	--	Admin		10-03-2023 Fit	Not Applicable	Not Applicable		
34	78	250433	Rahul Bhagat	Male	30		--	--	Production		10-03-2023 Fit	Not Applicable	Not Applicable		
35	80	210082	Yogesh N. Patil	Male	41		--	--	Mechanical		10-03-2023 Fit	Not Applicable	Not Applicable		
36	81	210118	Shriram M. Thakur	Male	35		--	--	Mechanical		10-03-2023 Fit	Not Applicable	Not Applicable		

Name of Certifying Surgeon

Dr. Pankaj Shah

Regd. No. 51279

FORM NO. 7

HEALTH REGISTER

From :- 10-03-2023 To 10-03-2024

(In respect of persons employed in occupations declared to be dangerous operations under Sections 87)

Note : (i) Column 8, Detailed summary of reason for transfer or discharge should be stated.

Note : (ii) Column II, should be expressed as Fit/Unfit/Suspended.

Sr. No.	Form No.	EC. No.	Name of Worker	sex	Age (last birth day)	Date of employment of present work	Date of leaving or transfer to other work	Reason for leaving, transfer or discharge	Nature of job or occupation	Raw material or Bye product handled	Date of medical examination by Certifying Surgeon and Result of Medical Examination	If suspended from work state period of suspension with detailed reasons	Certified fit to resume duty on with Signature of certifying Surgeon	If certificate of unfitness or suspension issued to worker	Signature with Certifying Surgeon
37	82	240010	Rajesh S. Rankar	Male	46		--	--	Quality Control		10-03-2023 Fit	Not Applicable	Not Applicable		
38	84	250276	Rohidas M. Jage	Male	52		--	--	Production		10-03-2023 Fit	Not Applicable	Not Applicable		
39	85	250796	Saurabh C. Khodekar	Male	32		--	--	Production		10-03-2023 Fit	Not Applicable	Not Applicable		
40	86	230119	Jagdish B. Mate	Male	34		--	--	Instrument		10-03-2023 Fit	Not Applicable	Not Applicable		
41	87	250052	Milind G. Patil	Male	48		--	--	Instrument		10-03-2023 Fit	Not Applicable	Not Applicable		
42	88	150004	Dharmendra R. Narasing	Male	58		--	--	Stores		10-03-2023 Fit	Not Applicable	Not Applicable		
43	89	150015	Pradeep R. Singh	Male	38		--	--	Engg. Stores		10-03-2023 Fit	Not Applicable	Not Applicable		
44	90	220091	Prahhakar U. Parise	Male	44		--	--	Electrical		10-03-2023 Fit	Not Applicable	Not Applicable		
45	91	220092	Kasam S. Reddy	Male	31		--	--	Electrical		10-03-2023 Fit	Not Applicable	Not Applicable		
46	92	110009	Mohandas V. Kottu	Male	54		--	--	Commercial		10-03-2023 Fit	Not Applicable	Not Applicable		
47	93	180005	Hariharan S. Iyer	Male	47		--	--	Custom		10-03-2023 Fit	Not Applicable	Not Applicable		
48	95	250294	Millesh S. Pagare	Male	34		--	--	Production		10-03-2023 Fit	Not Applicable	Not Applicable		
49	96	240028	Yogesh S. Zaware	Male	29		--	--	Quality Control		10-03-2023 Fit	Not Applicable	Not Applicable		
50	97	240029	Vishal V. Kadam	Male	29		--	--	Quality Control		10-03-2023 Fit	Not Applicable	Not Applicable		
51	98	240031	Gorakshanth R. Chavan	Male	29		--	--	Quality Control		10-03-2023 Fit	Not Applicable	Not Applicable		
52	101	230144	Nitin Yadav	Male	38		--	--	Maintenance		10-03-2023 Fit	Not Applicable	Not Applicable		
53	102	230142	Ronak Pandey	Male	31		--	--	Instrument		10-03-2023 Fit	Not Applicable	Not Applicable		
54	103	220070	SANJAY D. JAGTAP	Male	47		--	--	Electrical		10-03-2023 Fit	Not Applicable	Not Applicable		

Name of Certifying Surgeon

Dr. Pankaj Shah

Regd. No. 51279

FORM NO. 7

HEALTH REGISTER

From :- 10-03-2023 To 10-03-2024

(In respect of persons employed in occupations declared to be dangerous operations under Sections 87)

Note : (i) Column 8, Detailed summary of reason for transfer of discharge should be stated.

Note : (ii) Column 11, should be expressed as Fit/Unfit/Suspended.

Sr. No.	Form No.	EC. No.	Name of Worker	sex	Age (last birth day)	Date of employment of present work	Date of leaving or transfer to other work	Reason for leaving, transfer or discharge	Nature of job or occupation	Raw material or Bye product handled	Date of medical examination by Certifying Surgeon and Result of Medical Examination	If suspended from work state period of suspension with detailed reasons	Certified fit to resume duty on with Signature of certifying Surgeon	If certificate of unfitness or suspension issued to worker	Signature with Certifying Surgeon
55	105	120018	Ajay G. Konar	Male	33				Accounts		10-03-2023 Fit	Not Applicable	Not Applicable		
56	106	240025	Pratul Khaire	Male	27				Quality Control		10-03-2023 Fit	Not Applicable	Not Applicable		
57	107	210142	Paresh Lad	Male	33				Mechanical		10-03-2023 Fit	Not Applicable	Not Applicable		
58	108	250471	Shrikrishna D. Sarda	Male	26				Production		10-03-2023 Fit	Not Applicable	Not Applicable		
59	109	250464	Sachin R. Khot	Male	27				Production		10-03-2023 Fit	Not Applicable	Not Applicable		
60	110	250439	Laxman K. Davanipurge	Male	26				Production		10-03-2023 Fit	Not Applicable	Not Applicable		
61	111	250408	Bhikamchand Mutha	Male	53				Production		10-03-2023 Fit	Not Applicable	Not Applicable		
62	112	250401	Rajendra G.	Male	48				Production		10-03-2023 Fit	Not Applicable	Not Applicable		
63	115	180002	Keshav S. Patil	Male	57				Customs		10-03-2023 Fit	Not Applicable	Not Applicable		
64	116	130911	Kishor D. Borade	Male	49				HR Admin		10-03-2023 Fit	Not Applicable	Not Applicable		
65	117	250479	Bhagwat S. Bharsake	Male	27				Production		10-03-2023 Fit	Not Applicable	Not Applicable		
66	119	250415	SHRIRAM PAWAR	Male	29				Production		10-03-2023 Fit	Not Applicable	Not Applicable		
67	120	150013	Alays Kumar Khatao	Male	54				Stores		10-03-2023 Fit	Not Applicable	Not Applicable		
68	122	250493	Ammar A. Sange	Male	24				Production		10-03-2023 Fit	Not Applicable	Not Applicable		
69	123	250504	Bhavesh B. Jadhav	Male	25				Production		10-03-2023 Fit	Not Applicable	Not Applicable		
70	125	240026	Suraj Jagtap	Male	31				Quality Control		10-03-2023 Fit	Not Applicable	Not Applicable		
71	130	240032	Shubham A. Shinde	Male	26				Quality Control		10-03-2023 Fit	Not Applicable	Not Applicable		
72	131	190022	Mahendra V. Jadhav	Male	52				Safety		10-03-2023 Fit	Not Applicable	Not Applicable		

Name of Certifying Surgeon

Dr. Pankaj Shah

FORM NO. 7

Regd. No. 51279

HEALTH REGISTER

From :- 10-03-2023 To 10-03-2024

(In respect of persons employed in occupations declared to be dangerous operations under Sections 87)

Note : (i) Column 8, Detailed summary of reason for transfer or discharge should be stated.

Note : (ii) Column II, should be expressed as Fit/Unfit/Suspended.

Sr. No.	Form No.	EC. No.	Name of Worker	sex	Age (last birthday)	Date of employment of present work	Date of leaving or transfer to other work	Reason for leaving, transfer or discharge	Nature of job or occupation	Raw material or Bye product handled	Date of medical examination by Certifying Surgeon and Result of Medical Examination	If suspended from work state period of suspension with detailed reasons	Certified fit to resume duty on with Signature of certifying Surgeon	If certificate of unfitness or suspension issued to worker	Signature with Certifying Surgeon
73	132	210007	Sandeep S. Kulkarni	Male	54		--	--	Mechanical		10-03-2023 Fit	Not Applicable	Not Applicable		
74	133	210102	Sandeep B. Kadam	Male	35		--	--	Mechanical		10-03-2023 Fit	Not Applicable	Not Applicable		
75	134	290424	Sumit Jaiswal	Male	35		--	--	Production		10-03-2023 Fit	Not Applicable	Not Applicable		
76	135	220069	Niwruatti P. Umale	Male	41		--	--	Electrical		14-03-2023 Fit	Not Applicable	Not Applicable		
77	136	170016	Vasudev Sarda	Male	44		--	--	Warehouse		14-03-2023 Fit	Not Applicable	Not Applicable		
78	137	170015	Rajesh Bagri	Male	40		--	--	Raw Material		14-03-2023 Fit	Not Applicable	Not Applicable		
79	138	250386	Laxmikant M. Naik	Male	32		--	--	Technical Service		14-03-2023 Fit	Not Applicable	Not Applicable		
80	140	210134	Kiran K. Patil	Male	27		--	--	Mechanical		14-03-2023 Fit	Not Applicable	Not Applicable		
81	141	210138	Kalyan B. Kharade	Male	29		--	--	Mechanical		14-03-2023 Fit	Not Applicable	Not Applicable		
82	142	210157	Ranjeet Thakur	Male	33		--	--	Mechanical		14-03-2023 Fit	Not Applicable	Not Applicable		
83	143	210139	Vaibhav Gadegaonkar	Male	29		--	--	Mechanical		14-03-2023 Fit	Not Applicable	Not Applicable		
84	144	210153	Lakhan Y. Pawar	Male	22		--	--	Mechanical		14-03-2023 Fit	Not Applicable	Not Applicable		
85	147	230121	Sandesh B. Kadam	Male	30		--	--	Instrument		14-03-2023 Fit	Not Applicable	Not Applicable		
86	159	210121	Mohit Kumar Singh	Male	33		--	--	Mechanical		14-03-2023 Fit	Not Applicable	Not Applicable		
87	182	180066	Ramakant D. Gautam	Male	40		--	--	Custom		14-03-2023 Fit	Not Applicable	Not Applicable		
88	183	180008	Subodh J. Lahoti	Male	30		--	--	Custom & Excise		14-03-2023 Fit	Not Applicable	Not Applicable		
89	191	124902	Arvind G. Deshmukh	Male	53		--	--	Quality Control		14-03-2023 Fit	Not Applicable	Not Applicable		
90	193	240909	Sandip P. Surve	Male	54		--	--	Quality Control		14-03-2023 Fit	Not Applicable	Not Applicable		

Name of Certifying Surgeon

Dr. Pankaj Shah

Regd. No. 51279

FORM NO. 7

HEALTH REGISTER

From :- 14-03-2023 To 14-03-2024

(In respect of persons employed in occupations declared to be dangerous operations under Sections 87)

Note : (i) Column 8, Detailed summary of reason for transfer of discharge should be stated.

Note : (ii) Column II, should be expressed as Fit/Unfit/Suspended.

Sr. No.	Form No.	EC. No.	Name of Worker	sex	Age (last birth day)	Date of employment of present work	Date of leaving or transfer to other work	Reason for leaving, transfer or discharge	Nature of job or occupation	Raw material or Bye product handled	Date of medical examination by Certifying Surgeon and Result of Medical Examination	If suspended from work state period of suspension with detailed reasons	Certified fit to resume duty on with Signature of certifying Surgeon	If certificate of unfitness or suspension issued to worker	Signature with Certifying Surgeon
91	107	170020	Yogesh Sonavane	Male	35		--	--	Warehouse		14-03-2023 Fit	Not Applicable	Not Applicable		
92	199	250463	Ujjwal Kumar Mahanti	Male	54		--	--	Projects		14-03-2023 Fit	Not Applicable	Not Applicable		
93	202	260327	Mangesh S. Kalap	Male	34		--	--	MA Production		14-03-2023 Fit	Not Applicable	Not Applicable		
94	206	220071	Anil S. Mahadik	Male	52		--	--	Electrical		14-03-2023 Fit	Not Applicable	Not Applicable		
95	207	220113	Chintiroddy R. Reddy	Male	35		--	--	Electrical		14-03-2023 Fit	Not Applicable	Not Applicable		
96	208	240012	Shashikant B. Sutar	Male	54		--	--	Quality Control		14-03-2023 Fit	Not Applicable	Not Applicable		
97	210	170028	Vivek G. Thakur	Male	34		--	--	Raw Material		14-03-2023 Fit	Not Applicable	Not Applicable		
98	211	220107	Yogesh Dhongare	Male	26		--	--	Electrical		14-03-2023 Fit	Not Applicable	Not Applicable		
99	212	220106	Lavanam Sai Kumar	Male	36		--	--	Electrical		14-03-2023 Fit	Not Applicable	Not Applicable		
100	213	112004	Paras Jain	Male	56		--	--	Accts		14-03-2023 Fit	Not Applicable	Not Applicable		
101	214	120009	Mahesh R. Somani	Male	59		--	--	Accts		14-03-2023 Fit	Not Applicable	Not Applicable		
102	215	140012	Rahul K. Deshmukh	Male	26		--	--	Digital Transformation		14-03-2023 Fit	Not Applicable	Not Applicable		
103	222	150016	Vaibhav V. Patil	Male	35		--	--	Engg. Stores		14-03-2023 Fit	Not Applicable	Not Applicable		
104	225	250506	Suraj S. Patil	Male	32		--	--	Technical Service		14-03-2023 Fit	Not Applicable	Not Applicable		
105	226	250476	Vishvajit R. Pawar	Male	25		--	--	Technical Service		14-03-2023 Fit	Not Applicable	Not Applicable		
106	227	120008	Satyanarayan Maheshwari	Male	66		--	--	Accts		14-03-2023 Fit	Not Applicable	Not Applicable		
107	229	170014	Gabar Singh A. Panwar	Male	53		--	--	Raw Material		14-03-2023 Fit	Not Applicable	Not Applicable		
108	230	210038	Arya Somayajulu Pivan Kumar	Male	51		--	--	Eagg		14-03-2023 Fit	Not Applicable	Not Applicable		

Name of Certifying Surgeon

Dr. Pankaj ShahRegd. No. 51279

FORM NO. 7

HEALTH REGISTER

From :- 14-03-2023 To 14-03-2024

(In respect of persons employed in occupations declared to be dangerous operations under Sections 87)

Note : (i) Column 8, Detailed summary of reason for transfer of discharge should be stated.

Note : (ii) Column II, should be expressed as Fit/Unfit/Suspended.

Sr. No.	Form No.	EC. No.	Name of Worker	sex	Age (last birth day)	Date of employment of present work	Date of leaving or transfer to other work	Reason for leaving, transfer or discharge	Nature of job or occupation	Raw material or Bye product handled	Date of medical examination by Certifying Surgeon and Result of Medical Examination	If suspended from work state period of suspension with detailed reasons	Certified fit to resume duty on with Signature of certifying Surgeon	If certificate of unfitness or suspension issued to worker	Signature with Certifying Surgeon
109	237	220110	Naveen Pudari	Male	36		--	--	Electrical		14-03-2023 Fit	Not Applicable	Not Applicable		
110	247	140004	Sudhir R. Rane	Male	50		--	--	Purchase		14-03-2023 Fit	Not Applicable	Not Applicable		
111	261	250006	Hemant S. Athalye	Male	56		--	--	Production		14-03-2023 Fit	Not Applicable	Not Applicable		
112	262	230308	Ashok A. Gupta	Male	27		--	--	Production		14-03-2023 Fit	Not Applicable	Not Applicable		
113	263	FTA	Sanil R. Parte	Male	52		--	--	Security		14-03-2023 Fit	Not Applicable	Not Applicable		
114	275	290510	Sejit V. Katkar	Male	24		--	--	PA Production		14-03-2023 Fit	Not Applicable	Not Applicable		
115	276	250507	Kantuk G. Durgoli	Male	29		--	--	Production		14-03-2023 Fit	Not Applicable	Not Applicable		
116	278	250365	Mangesh H. Daravkar	Male	32		--	--	Production		15-03-2023 Fit	Not Applicable	Not Applicable		
117	279	210130	Alluri Satya Krishnam Raju	Male	30		--	--	Mechanical		15-03-2023 Fit	Not Applicable	Not Applicable		
118	280	170019	Rohit Patil	Male	36		--	--	Warehouse		15-03-2023 Fit	Not Applicable	Not Applicable		
119	281	210132	Pankaj Kumar Jha	Male	31		--	--	Mechanical		15-03-2023 Fit	Not Applicable	Not Applicable		
120	282	210129	Nilesh R. Chaudhari	Male	31		--	--	Mechanical		15-03-2023 Fit	Not Applicable	Not Applicable		
121	284	112002	Bhaskar J. Gharat	Male	58		--	--	Accts		15-03-2023 Fit	Not Applicable	Not Applicable		
122	286	170018	Amit Kumar	Male	41		--	--	Warehouse		15-03-2023 Fit	Not Applicable	Not Applicable		
123	287	121007	Vemula Shashidhar Reddy	Male	50		--	--	Mechanical		15-03-2023 Fit	Not Applicable	Not Applicable		
124	291	120010	Rajesh B. Purwar	Male	53		--	--	Accts		15-03-2023 Fit	Not Applicable	Not Applicable		
125	293	112005	Madhvanathi Krishnamurthy	Female	58		--	--	Accts		15-03-2023 Fit	Not Applicable	Not Applicable		
126	295	125068	Vyankatesh M. Kadam	Male	50		--	--	MA Production		15-03-2023 Fit	Not Applicable	Not Applicable		

Name of Certifying Surgeon

Dr. Pankaj ShahRegd. No. 51279

FORM NO. 7

HEALTH REGISTER

From :- 15-03-2023 To 15-03-2024

(In respect of persons employed in occupations declared to be dangerous operations under Sections 87)

Note : (i) Column 8, Detailed summary of reason for transfer or discharge should be stated.

Note : (ii) Column II, should be expressed as Fit/Unfit/Suspended.

Sr. No.	Form No.	EC. No.	Name of Worker	sex	Age (last birth day)	Date of employment of present work	Date of leaving or transfer to other work	Reason for leaving, transfer or discharge	Nature of job or occupation	Raw material or Bye product handled	Date of medical examination by Certifying Surgeon and Result of Medical Examination	If suspended from work state period of suspension with detailed reasons	Certified fit to resume duty on with Signature of certifying Surgeon	If certificate of unfitness or suspension issued to worker	Signature with Certifying Surgeon
127	303	140007	Manish Tiwari	Male	46		--	--	LT.		15-03-2023 Fit	Not Applicable	Not Applicable		[Signature]
128	304	140008	Shailesh M. Chaudhari	Male	43		--	--	LT.		15-03-2023 Fit	Not Applicable	Not Applicable		
129	305	140010	Chetan Badhe	Male	36		--	--	LT.		15-03-2023 Fit	Not Applicable	Not Applicable		
130	308	140006	Anil R. Suradkar	Male	36		--	--	LT.		15-03-2023 Fit	Not Applicable	Not Applicable		
131	309	160009	Ashish Somani	Male	28		--	--	Projects		15-03-2023 Fit	Not Applicable	Not Applicable		
132	313	210152	Jitendra Bisht	Male	34		--	--	Engg.		15-03-2023 Fit	Not Applicable	Not Applicable		
133	314	110021	Tejas Mhatre	Male	31		--	--	Commercial		15-03-2023 Fit	Not Applicable	Not Applicable		
134	315	190021	Kapil Sahu	Male	29		--	--	ITIS		15-03-2023 Fit	Not Applicable	Not Applicable		
135	320	220105	Sushant R. Sonar	Male	29		--	--	Electrical		15-03-2023 Fit	Not Applicable	Not Applicable		
136	323	220095	Bhushan C. Patil	Male	31		--	--	Electrical		15-03-2023 Fit	Not Applicable	Not Applicable		
137	324	220112	Vinit V. Mhatre	Male	33		--	--	Electrical		15-03-2023 Fit	Not Applicable	Not Applicable		
138	327	290341	Ganesh B. Kawade	Male	32		--	--	Production		15-03-2023 Fit	Not Applicable	Not Applicable		
139	329	250429	Suyodhan Todkar	Male	29		--	--	Production		15-03-2023 Fit	Not Applicable	Not Applicable		
140	330	250485	Sumit S. Mahadik	Male	27		--	--	Production		15-03-2023 Fit	Not Applicable	Not Applicable		
141	331	220106	Aakash Mali	Male	37		--	--	Electrical		15-03-2023 Fit	Not Applicable	Not Applicable		
142	332	220114	Rushikesh R. Manve	Male	28		--	--	Electrical		15-03-2023 Fit	Not Applicable	Not Applicable		
143	333	FTA	Bahaso N. Gurav	Male	48		--	--	Security		15-03-2023 Fit	Not Applicable	Not Applicable		
144	337	160012	Aydhut Dhapare	Male	26		--	--	Purchase		15-03-2023 Fit	Not Applicable	Not Applicable		

Name of Certifying Surgeon

Dr. Pankaj Shah

Regd. No. 51279

FORM NO. 7

HEALTH REGISTER

From :- 15-03-2023 To 15-03-2024

(In respect of persons employed in occupations declared to be dangerous operations under Sections 87)

Note : (i) Column 8, Detailed summary of reason for transfer or discharge should be stated.

Note : (ii) Column II, should be expressed as Fit/Unfit/Suspended.

Sr. No.	Form No.	EC. No.	Name of Worker	sex	Age (last birth day)	Date of employment of present work	Date of leaving or transfer to other work	Reason for leaving, transfer or discharge	Nature of job or occupation	Raw material or Bye product handled	Date of medical examination by Certifying Surgeon and Result of Medical Examination	If suspended from work state period of suspension with detailed reasons	Certified fit to resume duty on with Signature of certifying Surgeon	If certificate of unfitness or suspension issued to worker	Signature with Certifying Surgeon
145	338	256491	Sarang D. Maradwar	Male	38		--	--	Projects		15-03-2023 Fit	Not Applicable	Not Applicable		
146	340	189007	Anil V. Pandey	Male	49		--	--	Customs		15-03-2023 Fit	Not Applicable	Not Applicable		
147	341	220101	Swapnil R. Boende	Male	34		--	--	Electrical		15-03-2023 Fit	Not Applicable	Not Applicable		
148	344	220080	Bandaru Srinivas	Male	59		--	--	Electrical		15-03-2023 Fit	Not Applicable	Not Applicable		
149	345	220098	Purneshwar Nila	Male	28		--	--	Electrical		15-03-2023 Fit	Not Applicable	Not Applicable		
150	346	230472	Amol V. Salunkhe	Male	29		--	--	Production Engg.		15-03-2023 Fit	Not Applicable	Not Applicable		
151	347	190024	Sharad S. Bandal	Male	26		--	--	Safety		15-03-2023 Fit	Not Applicable	Not Applicable		
152	348	200001	Shivkumar B. Dhanasare	Male	55		--	--	Civil		15-03-2023 Fit	Not Applicable	Not Applicable		
153	349	--	Vijay Kumar Bhatt	Male	61		--	--	Technical Services		15-03-2023 Fit	Not Applicable	Not Applicable		
154	355	190018	Dhairyasheel R. Shinde	Male	46		--	--	EHS		15-03-2023 Fit	Not Applicable	Not Applicable		
155	356	230230	Mohan S. Khatri	Male	56		--	--	PA Production		15-03-2023 Fit	Not Applicable	Not Applicable		
156	357	230028	Nitin V. Deshmukh	Male	58		--	--	PA Production		15-03-2023 Fit	Not Applicable	Not Applicable		
157	361	230488	Aditya S. Sawant	Male	25		--	--	Production		15-03-2023 Fit	Not Applicable	Not Applicable		
158	366	120016	Pankaj Bhootra	Male	47		--	--	Acets		15-03-2023 Fit	Not Applicable	Not Applicable		
159	368	160001	Bilal A. SHAIKH	Male	54		--	--	Purchase		15-03-2023 Fit	Not Applicable	Not Applicable		
160	369	230132	Yogesh Kachare	Male	30		--	--	Instrument		18-03-2023 Fit	Not Applicable	Not Applicable		
161	370	230149	Surajsingh I. Pundir	Male	27		--	--	Instrumentation		18-03-2023 Fit	Not Applicable	Not Applicable		
162	371	230127	Romit R. Thakur	Male	31		--	--	Instrumentation		18-03-2023 Fit	Not Applicable	Not Applicable		

Name of Certifying Surgeon

Dr. Pankaj Shah

Regd. No. 51279

FORM NO. 7

HEALTH REGISTER

From :- 18-03-2023 To 18-03-2024

(In respect of persons employed in occupations declared to be dangerous operations under Sections 87)

Note : (i) Column 8, Detailed summary of reason for transfer or discharge should be stated.

Note : (ii) Column II, should be expressed as Fit/Unfit/Suspended.

Sr. No.	Form No.	EC. No.	Name of Worker	sex	Age (last birth day)	Date of employment of present work	Date of leaving or transfer to other work	Reason for leaving, transfer or discharge	Nature of job or occupation	Raw material or Bye product handled	Date of medical examination by Certifying Surgeon and Result of Medical Examination	If suspended from work state period of suspension with detailed reasons	Certified fit to resume duty on with Signature of certifying Surgeon	If certificate of unfitness or suspension issued to worker	Signature with Certifying Surgeon
163	372	250147	Ketan K. Bhoir	Male	32		--	--	Instrument		18-03-2023 Fit	Not Applicable	Not Applicable		
164	373	250430	Vishal L. Galkwad	Male	28		--	--	PA Production		18-03-2023 Fit	Not Applicable	Not Applicable		
165	380	250516	Vishwajit S. Dhumal	Male	30		--	--	PA Production		18-03-2023 Fit	Not Applicable	Not Applicable		
166	388	250509	Shankar G. Malusare	Male	28		--	--	PA Production		18-03-2023 Fit	Not Applicable	Not Applicable		
167	390	220117	Sangram Kumar S. Patra	Male	27		--	--	Electrical		18-03-2023 Fit	Not Applicable	Not Applicable		
168	391	210155	Soumya R. Panda	Male	28		--	--	Mechanical		18-03-2023 Fit	Not Applicable	Not Applicable		
169	394	250324	P. Rajesh	Male	40		--	--	Production		18-03-2023 Fit	Not Applicable	Not Applicable		
170	400	250407	Ramesh K. Rayane	Male	36		--	--	EHS		18-03-2023 Fit	Not Applicable	Not Applicable		
171	404	250515	Dheeraj H. Masale	Male	27		--	--	PA Production		18-03-2023 Fit	Not Applicable	Not Applicable		
172	405	250511	Jayesh P. Patil	Male	26		--	--	PA Production		18-03-2023 Fit	Not Applicable	Not Applicable		
173	406	250514	Avdesh Kamar	Male	24		--	--	PA Production		18-03-2023 Fit	Not Applicable	Not Applicable		
174	408	210149	Parag Bhoir	Male	28		--	--	Mechanical		18-03-2023 Fit	Not Applicable	Not Applicable		
175	415	130017	Atul Wadarkar	Male	41		--	--	HR		18-03-2023 Fit	Not Applicable	Not Applicable		
176	420	230130	Atul V. Bhagat	Male	32		--	--	Instrumentation		18-03-2023 Fit	Not Applicable	Not Applicable		
177	421	210127	Amol P. Suryawanshi	Male	33		--	--	Mechanical		18-03-2023 Fit	Not Applicable	Not Applicable		
178	422	220096	Rajmahamad S. Pinjari	Male	35		--	--	Electrical		18-03-2023 Fit	Not Applicable	Not Applicable		
179	426	130015	Sujay Bagwe	Male	34		--	--	HR		18-03-2023 Fit	Not Applicable	Not Applicable		
180	427	210140	Anuj Gupta	Male	28		--	--	Mechanical		18-03-2023 Fit	Not Applicable	Not Applicable		

कारखाने अधिनियम 1947, या कलम 10(9) प्रमाणे
 18-03-2023 Fit Not Applicable Not Applicable
 रॉयल विलेजिअरिटी दिनेक 30/11/21 पास 24/11/22 रॉयल
 18-03-2023 Fit Not Applicable Not Applicable
 रॉयल विलेजिअरिटी दिनेक 30/11/21 पास 24/11/22 रॉयल

Aspira pathlab & Diagnostics Ltd



HEALTH REGISTER

I G PETROCHEMICALS LIMITED

Dr. Pankaj shah
M.D., A.F.I.H., M.B.B.S.,
Industrial Health Consultant

Name of Certifying Surgeon

Dr. Pankaj Shah

Regd. No. 51279

FORM NO. 7

HEALTH REGISTER

From :- 09-03-2023 To 09-03-2024

(In respect of persons employed in occupations declared to be dangerous operations under Sections 87)

Note : (i) Column 8, Detailed summary of reason for transfer or discharge should be stated.

Note : (ii) Column II, should be expressed as Fit/Unfit/Suspended.

Sr. No.	Form No.	EC. No.	Name of Worker	sex	Age (last birth day)	Date of employment of present work	Date of leaving or transfer to other work	Reason for leaving, transfer or discharge	Nature of job or occupation	Raw material or Bye product handled	Date of medical examination by Certifying Surgeon and Result of Medical Examination	If suspended from work state period of suspension with detailed reasons	Certified fit to resume duty on with Signature of certifying Surgeon	If certificate of unfitness or suspension issued to worker	Signature with Certifying Surgeon
1	1	240015	Sameer S. Kane	Male	48		--	--	Quality Control		09-03-2023 Fit	Not Applicable	Not Applicable		[Signature]
2	3	260037	Rajesh R. Prudhm	Male	51		--	--	Instrument		09-03-2023 Fit	Not Applicable	Not Applicable		
3	4	210035	Manojkumar Singh	Male	55		--	--	Mechanical		09-03-2023 Fit	Not Applicable	Not Applicable		
4	5	210144	Vikas V. Patil	Male	33		--	--	Mechanical		09-03-2023 Fit	Not Applicable	Not Applicable		
5	6	210154	Sagar H. Jadhav	Male	28		--	--	Mechanical		09-03-2023 Fit	Not Applicable	Not Applicable		
6	11	249018	Vinayak V. Patil	Male	48		--	--	Lab		09-03-2023 Fit	Not Applicable	Not Applicable		
7	16	258061	Manish S. Wayangankar	Male	51		--	--	Production		09-03-2023 Fit	Not Applicable	Not Applicable		
8	17	122007	Vikram S. Gangurde	Male	50		--	--	Instrument		09-03-2023 Fit	Not Applicable	Not Applicable		
9	18	126009	Kishor S. Madhavi	Male	51		--	--	Quality Control		09-03-2023 Fit	Not Applicable	Not Applicable		
10	19	240017	Laxman K. Dole	Male	49		--	--	Quality Control		09-03-2023 Fit	Not Applicable	Not Applicable		
11	23	240006	Ramakant C. Mhatre	Male	54		--	--	Quality Control		09-03-2023 Fit	Not Applicable	Not Applicable		
12	26	290033	Santosh K. Korgaonkar	Male	58		--	--	Production		09-03-2023 Fit	Not Applicable	Not Applicable		
13	27	258030	Dnyaneshwar N. Naik	Male	56		--	--	Production		09-03-2023 Fit	Not Applicable	Not Applicable		
14	28	258034	Vidhyadhar P. Kulkarni	Male	55		--	--	Production		09-03-2023 Fit	Not Applicable	Not Applicable		
15	31	230045	Nitin B. Dave	Male	49		--	--	Instrument		09-03-2023 Fit	Not Applicable	Not Applicable		
16	32	123004	Ummikrishnan K.	Male	48		--	--	Instrument		09-03-2023 Fit	Not Applicable	Not Applicable		
17	34	260026	Jairam K. Sharma	Male	54		--	--	Lab		09-03-2023 Fit	Not Applicable	Not Applicable		
18	38	140000	Rajesh K. Patil	Male	52		--	--	Warehouse		09-03-2023 Fit	Not Applicable	Not Applicable		

Name of Certifying Surgeon

Dr. Pankaj ShahRegd. No. 51279

FORM NO. 7

HEALTH REGISTER

From :- 09-03-2023 To 09-03-2024

(In respect of persons employed in occupations declared to be dangerous operations under Sections 87)

Note : (i) Column 8, Detailed summary of reason for transfer of discharge should be stated.

Note : (ii) Column II, should be expressed as Fit/Unfit/Suspended.

Sr. No.	Form No.	EC. No.	Name of Worker	sex	Age (last birth day)	Date of employment of present work	Date of leaving or transfer to other work	Reason for leaving, transfer or discharge	Nature of job or occupation	Raw material or Bye product handled	Date of medical examination by Certifying Surgeon and Result of Medical Examination	If suspended from work state period of suspension with detailed reasons	Certified fit to resume duty on with Signature of certifying Surgeon	If certificate of unfitness or suspension issued to worker	Signature with Certifying Surgeon
19	39	170068	Tukaram M. Patil	Male	56		--	--	Warehouse		09-03-2023 Fit	Not Applicable	Not Applicable		
20	40	260028	Janu P. Patil	Male	50		--	--	Instrument		09-03-2023 Fit	Not Applicable	Not Applicable		
21	43	210018	Appu N. Yete	Male	57		--	--	Mechanical		09-03-2023 Fit	Not Applicable	Not Applicable		
22	45	220114	Tejas E. Dalvi	Male	24		--	--	Electrical		09-03-2023 Fit	Not Applicable	Not Applicable		
23	48	210041	Nareshkumar G. Lad	Male	52		--	--	Mechanical		09-03-2023 Fit	Not Applicable	Not Applicable		
24	49	180003	Mahadeo G. Thorat	Male	55		--	--	Warehouse		09-03-2023 Fit	Not Applicable	Not Applicable		
25	50	250025	Girish T.	Male	58		--	--	Lab		09-03-2023 Fit	Not Applicable	Not Applicable		
26	53	220004	Anil V. Chandnani	Male	56		--	--	Electrical		09-03-2023 Fit	Not Applicable	Not Applicable		
27	56	220015	Nandkumar M. Kulkarni	Male	56		--	--	Electrical		09-03-2023 Fit	Not Applicable	Not Applicable		
28	57	260034	Vijaykumar Upadhyay	Male	56		--	--	Electrical		09-03-2023 Fit	Not Applicable	Not Applicable		
29	58	122002	Dilip S. Bhoir	Male	49		--	--	Electrical		09-03-2023 Fit	Not Applicable	Not Applicable		
30	60	120006	Kaushil S. Bhatt	Male	58		--	--	Accounts		09-03-2023 Fit	Not Applicable	Not Applicable		
31	61	210145	Sameer M. Mandhe	Male	28		--	--	Mechanical		09-03-2023 Fit	Not Applicable	Not Applicable		
32	62	210143	Sojan S. Hilal	Male	28		--	--	Mechanical		09-03-2023 Fit	Not Applicable	Not Applicable		
33	63	210151	Sahil A. Tefange	Male	25		--	--	Mechanical		09-03-2023 Fit	Not Applicable	Not Applicable		
34	64	126014	Lahu S. Nighukar	Male	49		--	--	Instrument		09-03-2023 Fit	Not Applicable	Not Applicable		
35	65	250045	Siddharan N. Khadpe	Male	57		--	--	Production		09-03-2023 Fit	Not Applicable	Not Applicable		
36	68	250453	Pranij V. Rotkar	Male	26		--	--	MA Production		09-03-2023 Fit	Not Applicable	Not Applicable		

Name of Certifying Surgeon

Dr. Pankaj Shah

Regd. No. 51279

FORM NO. 7

HEALTH REGISTER

From :- 10-03-2023 To 10-03-2024

(In respect of persons employed in occupations declared to be dangerous operations under Sections 87)

Note : (i) Column 8, Detailed summary of reason for transfer or discharge should be stated.

Note : (ii) Column II, should be expressed as Fit/Unfit/Suspended.

Sr. No.	Form No.	EC. No.	Name of Worker	sex	Age (last birth day)	Date of employment of present work	Date of leaving or transfer to other work	Reason for leaving, transfer or discharge	Nature of job or occupation	Raw material or Bye product handled	Date of medical examination by Certifying Surgeon and Result of Medical Examination	If suspended from work state period of suspension with detailed reasons	Certified fit to resume duty on with Signature of certifying Surgeon	If certificate of unfitness or suspension issued to worker	Signature with Certifying Surgeon
37	69	260035	Anandkumar V. Tiwari	Male	53	--	--	--	Warehouse		10-03-2023 Fit	Not Applicable	Not Applicable		(S)
38	70	260023	Shrikrushna S. Nigudar	Male	58	--	--	--	Production		10-03-2023 Fit	Not Applicable	Not Applicable		(S)
39	71	170022	Hasanain	Male	35	--	--	--	Warehouse		10-03-2023 Fit	Not Applicable	Not Applicable		(S)
40	72	126017	Shripat R. Mhatre	Male	50	--	--	--	Instrument		10-03-2023 Fit	Not Applicable	Not Applicable		(S)
41	73	230143	Pransy S. Thakur	Male	28	--	--	--	Instrument		10-03-2023 Fit	Not Applicable	Not Applicable		(S)
42	74	230137	Rajesh H. Sangade	Male	31	--	--	--	Instrument		10-03-2023 Fit	Not Applicable	Not Applicable		(S)
43	76	126013	Rajkishor M. Kapar	Male	48	--	--	--	Lab		10-03-2023 Fit	Not Applicable	Not Applicable		(S)
44	77	111082	Raghnathprasad B. Tiwari	Male	50	--	--	--	Warehouse		10-03-2023 Fit	Not Applicable	Not Applicable		(S)
45	79	260042	Prakash R. Patil	Male	52	--	--	--	Mechanical		10-03-2023 Fit	Not Applicable	Not Applicable		(S)
46	83	170029	Rushikesh M. Patil	Male	24	--	--	--	Raw Material		10-03-2023 Fit	Not Applicable	Not Applicable		(S)
47	94	210012	Manikant M. Dubey	Male	53	--	--	--	Mechanical		10-03-2023 Fit	Not Applicable	Not Applicable		(S)
48	99	260024	Laxmikant Tiwari	Male	49	--	--	--	Quality Control		10-03-2023 Fit	Not Applicable	Not Applicable		(S)
49	100	250405	Umesh P. Mhatre	Male	40	--	--	--	Production		10-03-2023 Fit	Not Applicable	Not Applicable		(S)
50	104	240002	Shashikant G. Rupale	Male	52	--	--	--	Lab		10-03-2023 Fit	Not Applicable	Not Applicable		(S)
51	113	126006	Vijay P. Patil	Male	51	--	--	--	Instrument		10-03-2023 Fit	Not Applicable	Not Applicable		(S)
52	114	210147	Pravin D. Bhalckar	Male	32	--	--	--	Mechanical		10-03-2023 Fit	Not Applicable	Not Applicable		(S)
53	118	250046	Naresh B. Shelake	Male	56	--	--	--	Production		10-03-2023 Fit	Not Applicable	Not Applicable		(S)
54	121	126018	Santosh L. Patil	Male	53	--	--	--	Mechanical		10-03-2023 Fit	Not Applicable	Not Applicable		(S)

Name of Certifying Surgeon

Dr. Pankaj ShahRegd. No. 51279

FORM NO. 7

HEALTH REGISTER

From :- 10-03-2023 To 10-03-2024

(In respect of persons employed in occupations declared to be dangerous operations under Sections 87)

Note : (i) Column 8, Detailed summary of reason for transfer of discharge should be stated.

Note : (ii) Column II, should be expressed as Fit/Unfit/Suspended.

Sr. No.	Form No.	EC. No.	Name of Worker	sex	Age (last birth day)	Date of employment of present work	Date of leaving or transfer to other work	Reason for leaving, transfer or discharge	Nature of job or occupation	Raw material or Bye product handled	Date of medical examination by Certifying Surgeon and Result of Medical Examination	If suspended from work state period of suspension with detailed reasons	Certified fit to resume duty on with Signature of certifying Surgeon	If certificate of unfitness or suspension issued to worker	Signature with Certifying Surgeon
55	124	170021	Rushikesh H. Patil	Male	26		--	--	Warehouse		10-03-2023 Fit	Not Applicable	Not Applicable		[Signature]
56	126	210034	Avinash T. Dhawale	Male	46		--	--	Mechanical		10-03-2023 Fit	Not Applicable	Not Applicable		
57	127	111004	Abodh S. Raut	Male	51		--	--	Warehouse		10-03-2023 Fit	Not Applicable	Not Applicable		
58	128	240009	Sunil K. Shinde	Male	53		--	--	Quality Control		10-03-2023 Fit	Not Applicable	Not Applicable		
59	129	123008	Vidyadhar P. Joshi	Male	49		--	--	Instrument		10-03-2023 Fit	Not Applicable	Not Applicable		
60	139	240001	Prakash B. Ghangrekar	Male	57		--	--	Quality Control		14-03-2023 Fit	Not Applicable	Not Applicable		
61	162	230145	Kalpesh S. Bhoir	Male	27		--	--	Instrument		14-03-2023 Fit	Not Applicable	Not Applicable		
62	163	260051	AnandKumar Upadhyay	Male	48		--	--	Quality Control		14-03-2023 Fit	Not Applicable	Not Applicable		
63	166	260025	Sunil G. Kamat	Male	49		--	--	Lab		14-03-2023 Fit	Not Applicable	Not Applicable		
64	201	250048	Sandesh V. Patil	Male	53		--	--	Production		14-03-2023 Fit	Not Applicable	Not Applicable		
65	204	220013	Sandeep A. Kabadi	Male	53		--	--	Electrical		14-03-2023 Fit	Not Applicable	Not Applicable		
66	219	160002	Manish J. Sawant	Male	54		--	--	Purchase		14-03-2023 Fit	Not Applicable	Not Applicable		
67	252	250414	Umesh H. Gondhali	Male	30		--	--	PA Production		14-03-2023 Fit	Not Applicable	Not Applicable		
68	254	260049	Bahuran A. Patil	Male	56		--	--	Lab		14-03-2023 Fit	Not Applicable	Not Applicable		
69	256	240010	Deepak B. Gurjar	Male	47		--	--	Quality Control		14-03-2023 Fit	Not Applicable	Not Applicable		
70	264	250019	Ashok S. Dhavale	Male	57		--	--	Production		14-03-2023 Fit	Not Applicable	Not Applicable		
71	265	250088	Rishikesh J. Patil	Male	49		--	--	Production		14-03-2023 Fit	Not Applicable	Not Applicable		
72	266	250051	Milind R. Pathare	Male	54		--	--	Production		14-03-2023 Fit	Not Applicable	Not Applicable		

Name of Certifying Surgeon

Dr. Pankaj Shah

Regd. No. 51279

FORM NO. 7

HEALTH REGISTER

From :- 14-03-2023 To 14-03-2024

(In respect of persons employed in occupations declared to be dangerous operations under Sections 87)

Note : (i) Column 8, Detailed summary of reason for transfer or discharge should be stated.

Note : (ii) Column II, should be expressed as Fit/Unfit/Suspended.

Sr. No.	Form No.	EC. No.	Name of Worker	sex	Age (last birthday)	Date of employment of present work	Date of leaving or transfer to other work	Reason for leaving, transfer or discharge	Nature of job or occupation	Raw material or Bye product handled	Date of medical examination by Certifying Surgeon and Result of Medical Examination	If suspended from work state period of suspension with detailed reasons	Certified fit to resume duty on with Signature of certifying Surgeon	If certificate of unfitness or suspension issued to worker	Signature with Certifying Surgeon
73	267	250690	Anil P. Bhide	Male	52		--	--	Production		14-03-2023 Fit	Not Applicable	Not Applicable		[Signature]
74	271	250827	Shripad M. Sonawane	Male	52		--	--	Production		14-03-2023 Fit	Not Applicable	Not Applicable		
75	272	260090	Yogesh C. Desai	Male	46		--	--	Lab		14-03-2023 Fit	Not Applicable	Not Applicable		
76	273	126020	Dilip M. Patil	Male	53		--	--	Lab		14-03-2023 Fit	Not Applicable	Not Applicable		
77	283	259029	Bhaskar S. Koparkar	Male	55		--	--	Production		15-03-2023 Fit	Not Applicable	Not Applicable		
78	285	250406	Vinayak V. Bhoir	Male	39		--	--	Production		15-03-2023 Fit	Not Applicable	Not Applicable		
79	292	110006	Meena R. Shrivastava	Female	54		--	--	Commercial		15-03-2023 Fit	Not Applicable	Not Applicable		
80	318	126022	Eknath P. Jale	Male	48		--	--	Electrical		15-03-2023 Fit	Not Applicable	Not Applicable		
81	328	111006	Vasudeo B. Patil	Male	53		--	--	Ware House		15-03-2023 Fit	Not Applicable	Not Applicable		
82	339	220115	Kunal D. Gadhari	Male	28		--	--	Electrical		15-03-2023 Fit	Not Applicable	Not Applicable		
83	342	220118	Vishal S. Sonawane	Male	22		--	--	Electrical		15-03-2023 Fit	Not Applicable	Not Applicable		
84	343	260022	Shankar S. Patil	Male	59		--	--	Mechanical		15-03-2023 Fit	Not Applicable	Not Applicable		
85	354	110004	Pradnya P. Bhatkar	Female	54		--	--	HR		15-03-2023 Fit	Not Applicable	Not Applicable		
86	360	230136	Sachin C. Bagul	Male	43		--	--	Instrument		15-03-2023 Fit	Not Applicable	Not Applicable		
87	362	210014	Arjankumar Jha	Male	58		--	--	Mechanical		15-03-2023 Fit	Not Applicable	Not Applicable		
88	363	260020	Shivram M. Patil	Male	58		--	--	Mechanical	[Signature]	15-03-2023 Fit	Not Applicable	Not Applicable		
89	364	230009	Devu P. Babu	Male	57		--	--	Instrument		15-03-2023 Fit	Not Applicable	Not Applicable		
90	365	250985	Anil Kumar R. Tripathi	Male	51		--	--	MA Production		15-03-2023 Fit	Not Applicable	Not Applicable		

Name of Certifying Surgeon

Dr. Pankaj Shah

Regd. No. 51279

FORM NO. 7

HEALTH REGISTER

From :- 15-03-2023 To 15-03-2024

(In respect of persons employed in occupations declared to be dangerous operations under Sections 87)

Note : (i) Column 8, Detailed summary of reason for transfer of discharge should be stated.

Note : (ii) Column II, should be expressed as Fit/Unfit/Suspended.

Sr. No.	Form No.	EC. No.	Name of Worker	sex	Age (last birth day)	Date of employment of present work	Date of leaving or transfer to other work	Reason for leaving, transfer or discharge	Nature of job or occupation	Raw material or Bye product handled	Date of medical examination by Certifying Surgeon and Result of Medical Examination	If suspended from work state period of suspension with detailed reasons	Certified fit to resume duty on with Signature of certifying Surgeon	If certificate of unfitness or suspension issued to worker	Signature with Certifying Surgeon
91	367	230013	Mahesh C. Bagul	Male	50		--	--	Instrument		15-03-2023 Fit	Not Applicable	Not Applicable		
92	396	170001	Dolfi J. Vae	Male	52		--	--	R.M.		18-03-2023 Fit	Not Applicable	Not Applicable		
93	397	126008	Ananta B. Patil	Male	57		--	--	R.M.		18-03-2023 Fit	Not Applicable	Not Applicable		
94	419	250039	Ashok V. Bagul	Male	52		--	--	Production		18-03-2023 Fit	Not Applicable	Not Applicable		
95	428	250026	Balasaheb B. Thete	Male	56		--	--	Production		18-03-2023 Fit	Not Applicable	Not Applicable		
96	429	250084	Yashwant R. Raskar	Male	50		--	--	Production		18-03-2023 Fit	Not Applicable	Not Applicable		
97	436	260041	Ashok M. Nigakar	Male	52		--	--	Mechanical		18-03-2023 Fit	Not Applicable	Not Applicable		

PS

कारखाने अधिनियम १९४७ का कलम १७(२) प्रमाणे
उपरोक्त प्रमाणपत्र दिनांक 30/11/23 पासून 29/11/23 पर्यंत
प्रमाणित प्रमाणपत्राधिकारिका क्र. ACS25-PS/2021

Aspira pathlab & Diagnostics Ltd



HEALTH REGISTER

Dr. Pankaj shah
M.D., A.F.I.H., M.B.B.S.,
Industrial Health Consultant

Name of Certifying Surgeon

Dr. Pankaj Shah

FORM NO. 7

Regd. No. 51279

HEALTH REGISTER

From :- 14-03-2023 To 14-03-2024

(In respect of persons employed in occupations declared to be dangerous operations under Sections 87)

Note : (i) Column 8, Detailed summary of reason for transfer of discharge should be stated.

Note : (ii) Column II, should be expressed as Fit/Unfit/Suspended.

Sr. No.	Form No.	EC. No.	Name of Worker	sex	Age (last birth day)	Date of employment of present work	Date of leaving or transfer to other work	Reason for leaving, transfer or discharge	Nature of job or occupation	Raw material or Bye product handled	Date of medical examination by Certifying Surgeon and Result of Medical Examination	If suspended from work state period of suspension with detailed reasons	Certified fit to resume duty on with Signature of certifying Surgeon	If certificate of unfitness or suspension issued to worker	Signature with Certifying Surgeon
1	145	-	Praad	Male	25		--	--	Loading		14-03-2023 Fit	Not Applicable	Not Applicable		[Handwritten signature]
2	146	-	Akash Y. Solankar	Male	28		--	--	Loading		14-03-2023 Fit	Not Applicable	Not Applicable		
3	148	-	Ashok P. Waghmode	Male	50		--	--	Loading		14-03-2023 Fit	Not Applicable	Not Applicable		
4	149	-	Ashok Chougule	Male	38		--	--	Loading		14-03-2023 Fit	Not Applicable	Not Applicable		
5	150	-	Balbhini Solankar	Male	45		--	--	Loading		14-03-2023 Fit	Not Applicable	Not Applicable		
6	151	-	Balaji A. Solankar	Male	30		--	--	Loading		14-03-2023 Fit	Not Applicable	Not Applicable		
7	152	-	Dilip N. Solankar	Male	26		--	--	Loading		14-03-2023 Fit	Not Applicable	Not Applicable		
8	153	-	Dattatray S. Satpute	Male	28		--	--	Loading		14-03-2023 Fit	Not Applicable	Not Applicable		
9	154	-	Akash N. Solankar	Male	24		--	--	Loading		14-03-2023 Fit	Not Applicable	Not Applicable		
10	155	-	Yogesh M. Sarvade	Male	23		--	--	Loading		14-03-2023 Fit	Not Applicable	Not Applicable		
11	156	-	Arjun B. More	Male	39		--	--	Loading		14-03-2023 Fit	Not Applicable	Not Applicable		
12	157	-	Satish Waghmode	Male	21		--	--	Loading		14-03-2023 Fit	Not Applicable	Not Applicable		
13	158	-	Sachin B. Ghule	Male	25		--	--	Loading		14-03-2023 Fit	Not Applicable	Not Applicable		
14	160	-	Shiwappa A. Wakshe	Male	25		--	--	Loading		14-03-2023 Fit	Not Applicable	Not Applicable		
15	161	-	Bapu D. Nitve	Male	40		--	--	Loading		14-03-2023 Fit	Not Applicable	Not Applicable		
16	164	-	Rajaram Bangar	Male	44		--	--	Loading		14-03-2023 Fit	Not Applicable	Not Applicable		
17	165	-	Rajkumar B. Jarug	Male	30		--	--	Loading		14-03-2023 Fit	Not Applicable	Not Applicable		
18	167	-	Prashant V. Dorge	Male	24		--	--	Loading		14-03-2023 Fit	Not Applicable	Not Applicable		

Name of Certifying Surgeon

Dr. Pankaj Shah

Regd. No. 51279

FORM NO. 7

HEALTH REGISTER

From :- 14-03-2023 To 14-03-2024

(In respect of persons employed in occupations declared to be dangerous operations under Sections 87)

Note : (i) Column 8, Detailed summary of reason for transfer of discharge should be stated.

Note : (ii) Column II, should be expressed as Fit/Unfit/Suspended.

Sr. No.	Form No.	EC. No.	Name of Worker	sex	Age (last birth day)	Date of employment of present work	Date of leaving or transfer to other work	Reason for leaving, transfer or discharge	Nature of job or occupation	Raw material or Bye product handled	Date of medical examination by Certifying Surgeon and Result of Medical Examination	If suspended from work state period of suspension with detailed reasons	Certified fit to resume duty on with Signature of certifying Surgeon	If certificate of unfitness or suspension issued to worker	Signature with Certifying Surgeon
19	168	-	Agatrao R. Kolekar	Male	52		--	--	Loading		14-03-2023 Fit	Not Applicable	Not Applicable		168
20	169	-	Sharad J. Solankar	Male	30		--	--	Loading		14-03-2023 Fit	Not Applicable	Not Applicable		169
21	170	-	Rajnish V. Navsare	Male	23		--	--	Loading		14-03-2023 Fit	Not Applicable	Not Applicable		170
22	171	-	Sayaji J. Solankar	Male	27		--	--	Loading		14-03-2023 Fit	Not Applicable	Not Applicable		171
23	172	-	Shantilal K. Galande	Male	35		--	--	Loading		14-03-2023 Fit	Not Applicable	Not Applicable		172
24	173	-	Balkrishna M. Dorge	Male	44		--	--	Loading		14-03-2023 Fit	Not Applicable	Not Applicable		173
25	174	-	Suryakant M. Mane	Male	30		--	--	Loading		14-03-2023 Fit	Not Applicable	Not Applicable		174
26	175	-	Teyappa T. Kafam	Male	54		--	--	Loading		14-03-2023 Fit	Not Applicable	Not Applicable		175
27	176	-	Bapurao M. Dorge	Male	48		--	--	Loading		14-03-2023 Fit	Not Applicable	Not Applicable		176
28	177	-	Appa K. Dorge	Male	48		--	--	Loading		14-03-2023 Fit	Not Applicable	Not Applicable		177
29	178	-	Changdeo D. Hazare	Male	50		--	--	Loading		14-03-2023 Fit	Not Applicable	Not Applicable		178
30	179	-	Sanjay Metkari	Male	40		--	--	Loading		14-03-2023 Fit	Not Applicable	Not Applicable		179
31	180	-	Sattu R. Mudhe	Male	38		--	--	Loading		14-03-2023 Fit	Not Applicable	Not Applicable		180
32	181	-	Suryakant Gawade	Male	57		--	--	Loading		14-03-2023 Fit	Not Applicable	Not Applicable		181
33	184	-	Pranod Y. Thakre	Male	27		--	--	Fire & Safety		14-03-2023 Fit	Not Applicable	Not Applicable		184
34	185	-	Ajay Kumar Singh	Male	36		--	--	Security		14-03-2023 Fit	Not Applicable	Not Applicable		185
35	186	-	Rupchand	Male	54		--	--	Canteen		14-03-2023 Fit	Not Applicable	Not Applicable		186
36	187	-	Deepak Kumar Ram	Male	20		--	--	Canteen		14-03-2023 Fit	Not Applicable	Not Applicable		187

Name of Certifying Surgeon

Dr. Pankaj Shah

Regd. No. 51279

FORM NO. 7

HEALTH REGISTER

From :- 14-03-2023 To 14-03-2024

(In respect of persons employed in occupations declared to be dangerous operations under Sections 87)

Note : (i) Column 8, Detailed summary of reason for transfer or discharge should be stated.

Note : (ii) Column II, should be expressed as Fit/Unfit/Suspended.

Sr. No.	Form No.	EC. No.	Name of Worker	sex	Age (last birthday)	Date of employment of present work	Date of leaving or transfer to other work	Reason for leaving, transfer or discharge	Nature of job or occupation	Raw material or Bye product handled	Date of medical examination by Certifying Surgeon and Result of Medical Examination	If suspended from work state period of suspension with detailed reasons	Certified fit to resume duty on with Signature of certifying Surgeon	If certificate of unfitness or suspension issued to worker	Signature with Certifying Surgeon
37	188	-	Ganesh Kadam	Male	37		--	--	House Keeping		14-03-2023 Fit	Not Applicable	Not Applicable		[Signature]
38	189	-	Balaram J. Patil	Male	53		--	--	House Keeping		14-03-2023 Fit	Not Applicable	Not Applicable		
39	190	-	Balaram D. Madhavi	Male	49		--	--	House Keeping		14-03-2023 Fit	Not Applicable	Not Applicable		
40	192	-	Dhruva Deka	Male	35		--	--	Security		14-03-2023 Fit	Not Applicable	Not Applicable		
41	194	-	Jay Prakash	Male	39		--	--	Security		14-03-2023 Fit	Not Applicable	Not Applicable		
42	195	-	Sudhanshu Giri	Male	41		--	--	Canteen		14-03-2023 Fit	Not Applicable	Not Applicable		
43	196	-	Sonu Kumar A. Singh	Male	28		--	--	Security		14-03-2023 Fit	Not Applicable	Not Applicable		
44	198	-	Purna chandra Parhi	Male	41		--	--	Canteen		14-03-2023 Fit	Not Applicable	Not Applicable		
45	200	-	Lahoo Patil	Male	53		--	--	House Keeping		14-03-2023 Fit	Not Applicable	Not Applicable		
46	203	-	Moham Kumar Jha	Male	40		--	--	Security		14-03-2023 Fit	Not Applicable	Not Applicable		
47	205	-	Kamlesh Kumar	Male	19		--	--	Canteen		14-03-2023 Fit	Not Applicable	Not Applicable		
48	209	-	Surentra Nayak	Male	51		--	--	Canteen		14-03-2023 Fit	Not Applicable	Not Applicable		
49	216	-	Lahu chavan	Male	45		--	--	Security		14-03-2023 Fit	Not Applicable	Not Applicable		
50	217	-	Ajay Choudhary	Male	23		--	--	Canteen		14-03-2023 Fit	Not Applicable	Not Applicable		
51	218	-	Vipin Vishwakarma	Male	24		--	--	Canteen		14-03-2023 Fit	Not Applicable	Not Applicable		
52	220	-	Badu Rathod	Male	27		--	--	Security		14-03-2023 Fit	Not Applicable	Not Applicable		
53	221	-	Prabhanshi Parwan	Male	25		--	--	Security		14-03-2023 Fit	Not Applicable	Not Applicable		
54	223	-	Pawan Kumar	Male	28		--	--	Security		14-03-2023 Fit	Not Applicable	Not Applicable		

Name of Certifying Surgeon

Dr. Pankaj Shah

Regd. No. 51279

FORM NO. 7

HEALTH REGISTER

From :- 14-03-2023 To 14-03-2024

(In respect of persons employed in occupations declared to be dangerous operations under Sections 87)

Note : (i) Column 8, Detailed summary of reason for transfer or discharge should be stated.

Note : (ii) Column II, should be expressed as Fit/Unfit/Suspended.

Sr. No.	Form No.	EC. No.	Name of Worker	sex	Age (last birth day)	Date of employment of present work	Date of leaving or transfer to other work	Reason for leaving, transfer or discharge	Nature of job or occupation	Raw material or Bye product handled	Date of medical examination by Certifying Surgeon and Result of Medical Examination	If suspended from work state period of suspension with detailed reasons	Certified fit to resume duty on with Signature of certifying Surgeon	If certificate of unfitness or suspension issued to worker	Signature with Certifying Surgeon
55	224	-	Sumit Kumar	Male	23		--	--	Security		14-03-2023 Fit	Not Applicable	Not Applicable		
56	228	-	Rushikesh Kasar	Male	23		--	--	Fire & Safety		14-03-2023 Fit	Not Applicable	Not Applicable		
57	231	-	Vishwanath Patil	Male	42		--	--	House Keeping		14-03-2023 Fit	Not Applicable	Not Applicable		
58	232	-	Kristna Dhumal	Male	41		--	--	House Keeping		14-03-2023 Fit	Not Applicable	Not Applicable		
59	233	-	Suresh Patil	Male	43		--	--	House Keeping		14-03-2023 Fit	Not Applicable	Not Applicable		
60	234	-	Ramesh Nighokar	Male	49		--	--	House Keeping		14-03-2023 Fit	Not Applicable	Not Applicable		
61	235	-	Nagendra yadav	Male	31		--	--	Security		14-03-2023 Fit	Not Applicable	Not Applicable		
62	236	-	Ram Babu Kumar	Male	34		--	--	Security		14-03-2023 Fit	Not Applicable	Not Applicable		
63	238	-	Lalchand Madhavi	Male	45		--	--	House Keeping		14-03-2023 Fit	Not Applicable	Not Applicable		
64	239	-	Nishant Rai	Male	26		--	--	Security		14-03-2023 Fit	Not Applicable	Not Applicable		
65	240	-	Kantilal Gochare	Male	27		--	--	Security		14-03-2023 Fit	Not Applicable	Not Applicable		
66	241	-	Prashant Pawar	Male	42		--	--	Security		14-03-2023 Fit	Not Applicable	Not Applicable		
67	242	-	Narayan Tripathi	Male	36		--	--	Canteen		14-03-2023 Fit	Not Applicable	Not Applicable		
68	243	-	Ravindra Dewri	Male	26		--	--	Canteen		14-03-2023 Fit	Not Applicable	Not Applicable		
69	244	-	Rajesh Modak	Male	26		--	--	Canteen		14-03-2023 Fit	Not Applicable	Not Applicable		
70	245	-	Ravi Gaikwad	Male	30		--	--	Driver		14-03-2023 Fit	Not Applicable	Not Applicable		
71	246	-	Janki Lodhi	Male	26		--	--	Fire & Safety		14-03-2023 Fit	Not Applicable	Not Applicable		
72	248	-	Balu Tayade	Male	32		--	--	Driver		14-03-2023 Fit	Not Applicable	Not Applicable		

Name of Certifying Surgeon

Dr. Pankaj Shah

Regd. No. 51279

FORM NO. 7

HEALTH REGISTER

From :- 14-03-2023 To 14-03-2024

(In respect of persons employed in occupations declared to be dangerous operations under Sections 87)

Note : (i) Column 8, Detailed summary of reason for transfer or discharge should be stated.

Note : (ii) Column II, should be expressed as Fit/Unfit/Suspended.

Sr. No.	Form No.	EC. No.	Name of Worker	sex	Age (last birth day)	Date of employment of present work	Date of leaving or transfer to other work	Reason for leaving, transfer or discharge	Nature of job or occupation	Raw material or By product handled	Date of medical examination by Certifying Surgeon and Result of Medical Examination	If suspended from work state period of suspension with detailed reasons	Certified fit to resume duty on with Signature of certifying Surgeon	If certificate of unfitness or suspension issued to worker	Signature with Certifying Surgeon
73	249	-	Pramod S. Kale	Male	21	--	--	--	PA Bagging		14-03-2023 Fit	Not Applicable	Not Applicable		[Signature]
74	250	-	Sudarshan Mahato	Male	55	--	--	--	Canteen		14-03-2023 Fit	Not Applicable	Not Applicable		
75	251	-	Rupeshwar Saikia	Male	43	--	--	--	Security		14-03-2023 Fit	Not Applicable	Not Applicable		
76	253	-	Balaram C. Patil	Male	58	--	--	--	House Keeping		14-03-2023 Fit	Not Applicable	Not Applicable		
77	255	-	Santosh Choudhary	Male	39	--	--	--	Security		14-03-2023 Fit	Not Applicable	Not Applicable		
78	257	-	Sanjay S. Maharnor	Male	26	--	--	--	Bagging		14-03-2023 Fit	Not Applicable	Not Applicable		
79	258	-	Sunil D. Bangar	Male	26	--	--	--	Bagging		14-03-2023 Fit	Not Applicable	Not Applicable		
80	259	-	Rutik D. Patil	Male	21	--	--	--	MA Bagging		14-03-2023 Fit	Not Applicable	Not Applicable		
81	260	-	Rajendra D. Narbat	Male	19	--	--	--	MA Bagging		14-03-2023 Fit	Not Applicable	Not Applicable		
82	268	-	Durgesh	Male	26	--	--	--	Driver		14-03-2023 Fit	Not Applicable	Not Applicable		
83	269	-	Mansohar S. Wakshe	Male	45	--	--	--	PA Bagging		14-03-2023 Fit	Not Applicable	Not Applicable		
84	270	-	Ashok Sakpal	Male	49	--	--	--	Security		14-03-2023 Fit	Not Applicable	Not Applicable		
85	274	-	Humen Chauriya	Male	28	--	--	--	Security		14-03-2023 Fit	Not Applicable	Not Applicable		
86	277	-	Nimal Kumar Singh	Male	38	--	--	--	Security		14-03-2023 Fit	Not Applicable	Not Applicable		
87	288	-	Shivnath Patil	Male	42	--	--	--	Warehouse		15-03-2023 Fit	Not Applicable	Not Applicable		
88	289	-	Namdeo Thombre	Male	50	--	--	--	MA Production		15-03-2023 Fit	Not Applicable	Not Applicable		
89	290	-	Rohidas Patil	Male	53	--	--	--	H.K.		15-03-2023 Fit	Not Applicable	Not Applicable		
90	294	-	Lalaso Dorne	Male	38	--	--	--	Loading		15-03-2023 Fit	Not Applicable	Not Applicable		

Name of Certifying Surgeon

Dr. Pankaj Shah

Regd. No. 51279

FORM NO. 7

HEALTH REGISTER

From :- 15-03-2023 To 15-03-2024

(In respect of persons employed in occupations declared to be dangerous operations under Sections 87)

Note : (i) Column 8, Detailed summary of reason for transfer or discharge should be stated.

Note : (ii) Column II, should be expressed as Fit/Unfit/Suspended.

Sr. No.	Form No.	EC. No.	Name of Worker	sex	Age (last birth day)	Date of employment of present work	Date of leaving or transfer to other work	Reason for leaving, transfer or discharge	Nature of job or occupation	Raw material or Bye product handled	Date of medical examination by Certifying Surgeon and Result of Medical Examination	If suspended from work state period of suspension with detailed reasons	Certified fit to resume duty on with Signature of Certifying Surgeon	If certificate of unfitness or suspension issued to worker	Signature with Certifying Surgeon
91	296	-	Manohar H. Shinde	Male	40		--	--	Loading		15-03-2023 Fit	Not Applicable	Not Applicable		[Signature]
92	297	-	Bhanudas Gole	Male	33		--	--	Loading		15-03-2023 Fit	Not Applicable	Not Applicable		
93	298	-	Rohan K. Salunkhe	Male	26		--	--	Loading		15-03-2023 Fit	Not Applicable	Not Applicable		
94	299	-	Sachin Khandekar	Male	30		--	--	Loading		15-03-2023 Fit	Not Applicable	Not Applicable		
95	300	-	Raja C. Patil	Male	33		--	--	Loading		15-03-2023 Fit	Not Applicable	Not Applicable		
96	301	-	Tanaji Sotankar	Male	26		--	--	Loading		15-03-2023 Fit	Not Applicable	Not Applicable		
97	302	-	Dadasaheb Kale	Male	30		--	--	Loading		15-03-2023 Fit	Not Applicable	Not Applicable		
98	306	-	Kiran A. Bandgar	Male	23		--	--	Loading		15-03-2023 Fit	Not Applicable	Not Applicable		
99	307	-	Lata s. Jadhav	Male	45		--	--	Bagging		15-03-2023 Fit	Not Applicable	Not Applicable		
100	310	-	Shakti M. Jadhav	Male	33		--	--	Bagging		15-03-2023 Fit	Not Applicable	Not Applicable		
101	311	-	Subhash P. Kadam	Male	47		--	--	Bagging		15-03-2023 Fit	Not Applicable	Not Applicable		
102	312	-	Suryakant J. Khatal	Male	35		--	--	Bagging		15-03-2023 Fit	Not Applicable	Not Applicable		
103	316	-	Sagar T. Kotekar	Male	21		--	--	Bagging		15-03-2023 Fit	Not Applicable	Not Applicable		
104	317	-	Kakasa A. Mudbe	Male	41		--	--	Bagging		15-03-2023 Fit	Not Applicable	Not Applicable		
105	319	-	PRALHAD RAJE	Male	42		--	--	Stores		15-03-2023 Fit	Not Applicable	Not Applicable		
106	321	-	Ramesh Phadke	Male	29		--	--	Stores		15-03-2023 Fit	Not Applicable	Not Applicable		
107	322	-	Ramesh K. Patil	Male	48		--	--	Housekeeping		15-03-2023 Fit	Not Applicable	Not Applicable		
108	325	-	Arun Mahato	Male	46		--	--	Ware House		15-03-2023 Fit	Not Applicable	Not Applicable		

Name of Certifying Surgeon

Dr. Pankaj ShahRegd. No. 51279

FORM NO. 7

HEALTH REGISTER

From :- 15-03-2023 To 15-03-2024

(In respect of persons employed in occupations declared to be dangerous operations under Sections 87)

Note : (i) Column 8, Detailed summary of reason for transfer or discharge should be stated.

Note : (ii) Column II, should be expressed as Fit/Unfit/Suspended.

Sr. No.	Form No.	EC. No.	Name of Worker	sex	Age (last birth day)	Date of employment of present work	Date of leaving or transfer to other work	Reason for leaving, transfer or discharge	Nature of job or occupation	Raw material or Bye product handled	Date of medical examination by Certifying Surgeon and Result of Medical Examination	If suspended from work state period of suspension with detailed reasons	Certified fit to resume duty on with Signature of certifying Surgeon	If certificate of unfitness or suspension issued to worker	Signature with Certifying Surgeon
109	326	-	Shekhar S. Gawade	Male	25		--	--	Loading		15-03-2023 Fit	Not Applicable	Not Applicable		[Signature]
110	334	-	Dinesh Gupta	Male	25		--	--	Male Nurse		15-03-2023 Fit	Not Applicable	Not Applicable		
111	335	-	Shyam Thakur	Male	48		--	--	Ware House		15-03-2023 Fit	Not Applicable	Not Applicable		
112	336	-	Deepak K. Shefar	Male	52		--	--	Bagging		15-03-2023 Fit	Not Applicable	Not Applicable		
113	350	-	Uttam M. Shiode	Male	50		--	--	Bagging		15-03-2023 Fit	Not Applicable	Not Applicable		
114	351	-	Vasant Patil	Male	53		--	--	House Keeping		15-03-2023 Fit	Not Applicable	Not Applicable		
115	352	-	Ramchandra A. Patil	Male	54		--	--	House Keeping		15-03-2023 Fit	Not Applicable	Not Applicable		
116	353	-	Anan G. Patil	Male	50		--	--	House Keeping		15-03-2023 Fit	Not Applicable	Not Applicable		
117	358	-	Bhausheb B. Gore	Male	38		--	--	Bagging		15-03-2023 Fit	Not Applicable	Not Applicable		
118	359	-	Jimesh S. Jaitu	Male	21		--	--	Bagging		15-03-2023 Fit	Not Applicable	Not Applicable		
119	374	-	Vikesh Kumar	Male	28		--	--	Security		18-03-2023 Fit	Not Applicable	Not Applicable		
120	375	-	Prashant Chautiya	Male	31		--	--	Security		18-03-2023 Fit	Not Applicable	Not Applicable		
121	376	-	Abhishek Upadhyay	Male	33		--	--	Security		18-03-2023 Fit	Not Applicable	Not Applicable		
122	377	-	Abhishek Kumar singh	Male	38		--	--	Security		18-03-2023 Fit	Not Applicable	Not Applicable		
123	378	-	Pankaj Kushwaha	Male	25		--	--	Canteen		18-03-2023 Fit	Not Applicable	Not Applicable		
124	379	-	Soumesh Mishra	Male	30		--	--	Security		18-03-2023 Fit	Not Applicable	Not Applicable		
125	381	-	Sandeep Kumar	Male	32		--	--	Security		18-03-2023 Fit	Not Applicable	Not Applicable		
126	382	-	Sagar Kathe	Male	34		--	--	Stores		18-03-2023 Fit	Not Applicable	Not Applicable		

Name of Certifying Surgeon

Dr. Pankaj Shah

Regd. No. 51279

FORM NO. 7

HEALTH REGISTER

From :- 18-03-2023 To 18-03-2024

(In respect of persons employed in occupations declared to be dangerous operations under Sections 87)

Note : (i) Column 8, Detailed summary of reason for transfer of discharge should be stated.

Note : (ii) Column II, should be expressed as Fit/Unfit/Suspended.

Sr. No.	Form No.	EC. No.	Name of Worker	sex	Age (last birth day)	Date of employment of present work	Date of leaving or transfer to other work	Reason for leaving, transfer or discharge	Nature of job or occupation	Raw material or Bye product handled	Date of medical examination by Certifying Surgeon and Result of Medical Examination	If suspended from work state period of suspension with detailed reasons	Certified fit to resume duty on with Signature of certifying Surgeon	If certificate of unfitness or suspension issued to worker	Signature with Certifying Surgeon
127	383	-	Nilesh Gondhali	Male	37		--	--	PAC		18-03-2023 Fit	Not Applicable	Not Applicable		[Signature]
128	384	-	Rajaram Singh	Male	39		--	--	Security		18-03-2023 Fit	Not Applicable	Not Applicable		
129	385	-	Bipul Tanti	Male	36		--	--	Security		18-03-2023 Fit	Not Applicable	Not Applicable		
130	386	-	Dhiraj S. Chouhan	Male	52		--	--	Security		18-03-2023 Fit	Not Applicable	Not Applicable		
131	387	-	SushilKumar Pandey	Male	30		--	--	Security		18-03-2023 Fit	Not Applicable	Not Applicable		
132	389	-	Sonu Kumar Sadhu Singh	Male	27		--	--	Security		18-03-2023 Fit	Not Applicable	Not Applicable		
133	392	-	Mono Das	Male	37		--	--	Security		18-03-2023 Fit	Not Applicable	Not Applicable		
134	393	-	Sachin Yadav	Male	25		--	--	Security		18-03-2023 Fit	Not Applicable	Not Applicable		
135	395	-	Krishea Kumar Ram	Male	41		--	--	Security		18-03-2023 Fit	Not Applicable	Not Applicable		
136	398	-	Adhik Kumar Yadav	Male	32		--	--	Security		18-03-2023 Fit	Not Applicable	Not Applicable		
137	399	-	Jay Prakash Yadav	Male	28		--	--	Security		18-03-2023 Fit	Not Applicable	Not Applicable		
138	401	-	Raju Tanti	Male	34		--	--	Security		18-03-2023 Fit	Not Applicable	Not Applicable		
139	402	-	Onkar More	Male	29		--	--	Fire & Safety		18-03-2023 Fit	Not Applicable	Not Applicable		
140	403	-	Ajit More	Male	24		--	--	Fire & Safety		18-03-2023 Fit	Not Applicable	Not Applicable		
141	407	-	Dravkar Chalake	Male	32		--	--	ETP		18-03-2023 Fit	Not Applicable	Not Applicable		
142	409	-	Kiran Gondhali	Male	28		--	--	ETP		18-03-2023 Fit	Not Applicable	Not Applicable		
143	410	-	Onkar Kudavkar	Male	30		--	--	ETP		18-03-2023 Fit	Not Applicable	Not Applicable		
144	411	-	Sagar Jitkar	Male	30		--	--	ETP		18-03-2023 Fit	Not Applicable	Not Applicable		

Name of Certifying Surgeon

Dr. Pankaj Shah

Regd. No. 51279

FORM NO. 7

HEALTH REGISTER

From :- 18-03-2023 To 18-03-2024

(In respect of persons employed in occupations declared to be dangerous operations under Sections 87)

Note : (i) Column 8, Detailed summary of reason for transfer of discharge should be stated.

Note : (ii) Column II, should be expressed as Fit/Unfit/Suspended.

Sr. No.	Form No.	EC. No.	Name of Worker	sex	Age (last birth day)	Date of employment of present work	Date of leaving or transfer to other work	Reason for leaving, transfer or discharge	Nature of job or occupation	Raw material or Bye product handled	Date of medical examination by Certifying Surgeon and Result of Medical Examination	If suspended from work state period of suspension with detailed reasons	Certified fit to resume duty on with Signature of certifying Surgeon	If certificate of unfitness or suspension issued to worker	Signature with Certifying Surgeon
145	412	--	Rupesh Salunkhe	Male	22	--	--	--	ETP		18-03-2023 Fit	Not Applicable	Not Applicable		
146	413	--	Rehit R. Patil	Male	23	--	--	--	ETP		18-03-2023 Fit	Not Applicable	Not Applicable		
147	414	--	Sandesh Patil	Male	29	--	--	--	ETP		18-03-2023 Fit	Not Applicable	Not Applicable		
148	416	--	Vickesh J. Patil	Male	30	--	--	--	ETP		18-03-2023 Fit	Not Applicable	Not Applicable		
149	417	--	Mohan K. Bangar	Male	43	--	--	--	Bagging		18-03-2023 Fit	Not Applicable	Not Applicable		
150	418	--	Nikhillesh Nighokar	Male	25	--	--	--	ETP		18-03-2023 Fit	Not Applicable	Not Applicable		
151	423	--	Sachin J. Khundekar	Male	28	--	--	--	Bagging		18-03-2023 Fit	Not Applicable	Not Applicable		
152	424	--	Nagesh V. Zimal	Male	23	--	--	--	Bagging		18-03-2023 Fit	Not Applicable	Not Applicable		
153	425	--	Santosh M. Karande	Male	39	--	--	--	Bagging		18-03-2023 Fit	Not Applicable	Not Applicable		
154	431	--	Pramod Jitkar	Male	38	--	--	--	ETP		18-03-2023 Fit	Not Applicable	Not Applicable		
155	432	--	Pritesh M. Guikar	Male	29	--	--	--	ETP		18-03-2023 Fit	Not Applicable	Not Applicable		
156	433	--	Nikhil N. Mhatre	Male	24	--	--	--	Bagging		18-03-2023 Fit	Not Applicable	Not Applicable		
157	434	--	Vijay P. Shinde	Male	37	--	--	--	Bagging		18-03-2023 Fit	Not Applicable	Not Applicable		
158	435	--	Kiran A. Dorge	Male	21	--	--	--	Bagging		18-03-2023 Fit	Not Applicable	Not Applicable		
159	436	--	Nitin T. Madhe	Male	32	--	--	--	Bagging		18-03-2023 Fit	Not Applicable	Not Applicable		
160	437	--	Shivaji Mane	Male	28	--	--	--	Bagging		18-03-2023 Fit	Not Applicable	Not Applicable		
161	438	--	Amol D. Vaghe	Male	36	--	--	--	Bagging		18-03-2023 Fit	Not Applicable	Not Applicable		
162	439	--	Vijay Gaikwad	Male	32	--	--	--	ETP		18-03-2023 Fit	Not Applicable	Not Applicable		

Name of Certifying Surgeon

Dr. Pankaj Shah

Regd. No. 51279

FORM NO. 7

HEALTH REGISTER

From :- 18-03-2023 To 18-03-2024

(In respect of persons employed in occupations declared to be dangerous operations under Sections 87)

Note : (i) Column 8, Detailed summary of reason for transfer of discharge should be stated.

Note : (ii) Column II, should be expressed as Fit/Unfit/Suspended.

Sr. No.	Form No.	EC. No.	Name of Worker	sex	Age (last birth day)	Date of employment of present work	Date of leaving or transfer to other work	Reason for leaving, transfer or discharge	Nature of job or occupation	Raw material or Bye product handled	Date of medical examination by Certifying Surgeon and Result of Medical Examination	If suspended from work state period of suspension with detailed reasons	Certified fit to resume duty on with Signature of certifying Surgeon	If certificate of unfitness or suspension issued to worker	Signature with Certifying Surgeon
163	440	-	Dattatray G. Pisal	Male	35		--	--	Bugging		18-03-2023 Fit	Not Applicable	Not Applicable		<i>Rb</i>

7.36

कारखाने अधिनियम १९४८ म्या कलम १७(२) प्रमाणे
जमगट जिल्हाकारखाना दिनांक ३०/११/२०२१ पासून २५/११/२०२३ पर्यंत
प्रमाणित प्रमाणक वाचनचिकित्सक डॉ. ACS25-PS/2021

ANNEXURE – IX

Budget For Environment Monitoring and Pollution Control		
SR. NO.	HEADS	AMOUNT (Rs IN LACS)
1	Chemicals for ETP, RO & MEE plant operation	133.86
2	ETP Operation & Maintenance	92.16
3	Environmental monitoring	25.54
4	Hazardous waste disposal	114.12
5	AMC for OCEMS & ETP on line analyzers	14.99
	TOTAL	380.67

THE FREE PRESS JOURNAL ■ Mumbai ■ Saturday June 30, 2007

PUBLIC ANNOUNCEMENT

The proposed debottlenecking and resultant expansion of manufacturing capacity at I. G. Petrochemicals Ltd's plant at T 2 MIDC Talaja, 410208, Dist. Raigarh, has been accorded environmental clearance by The Ministry of Environment & Forests, Govt. of India. Copies of the clearance are available with Maharashtra Pollution Control Board and on ministry web site <http://envfor.nic.in>

नवशक्ति, मुंबई, शनिवार ३० जून, २००७

जाहीन सूचना

भारत सरकारच्या वन व पर्यावरण
मंत्रालयाने आय. जी. पेट्रोकेमिकल्स
लि. टी. २, एम. आय. टी. सी,
ता. तालाजा - ४१०२०८, जि. रायगड
येथील वारखान्याच्या निमित्त
यंत्रसुधारणा व त्यामुळे होणाऱ्या
उत्पादन वाढीस मान्यता दिली आहे.
मान्यतापत्र महाराष्ट्र इंधन नियंत्रण
मंडळ व वन / पर्यावरण मंत्रालयाकडे
वेबसाईट - <http://envfor.nic.in>
येथे उपलब्ध आहे.

PUBLIC ANNOUNCEMENT

The Proposed Expansion of Petrochemicals and synthetic organic chemicals manufacturing facility at Plot No. T-2, Talaja Industrial Area, MIDC Talaja, Dist. Rajgad by I G Petrochemicals Ltd. has been accorded Environmental Clearance by the Ministry of Environment, Forest & Climate Change vide letter no. J-11011/73/2016-IA-II (I) dated 20th February 2018. Copy of the said environment clearance is available with Maharashtra Pollution Control Board & on website of the MoEF & CC at <http://environmentclearance.nic.in/onlineSearchmodi.aspx?pid=ECAnendment>

I G Petrochemicals Ltd.
Authorized Signatory

८

नवशक्ति

मुंबई, शनिवार, ३ मार्च २०१८

जाहीर नोटीस

सर्व संबंधितांना माहिती देण्यात येते की, प्लॉट क्रमांक टी-२, तळोजा एम.आय.टी.सी., जिल्हा रायगड, महाराष्ट्र येथील आय. जी. पेट्रोकेमिकलस लि. द्वारा प्रस्तावित प्रकल्प, कृत्रिम सॅड्रिल रसायनिक उत्पादन सुविधेच्या संबंधित असून या प्रकल्पाला पर्यावरण वन एवढा जलवायु परिवर्तन मंत्रालय, भारत सरकार (MoEF & CC) समितीने संमती सरपत्र अक्षा क्र. J-11011/73/2016-IA-II (I), दिनांक २० फेब्रुवारी २०१८ प्रमाणे दिली आहे. सरपत्र पर्यावरणीय संमती पत्राची प्रत महाराष्ट्र प्रदूषण नियंत्रण मंडळाकडे तसेच मंत्रालयाच्या पर्यावरणीय विभागाच्या <http://environmentclearance.nic.in/onlineSearchmodi.aspx?pid=ECAnendment> या संकेत स्थळांका उपलब्ध आहे.

आय. जी. पेट्रोकेमिकलस लि.
अधिकृत सहीधारक

ANNEXURE – XI

EFFLUENT TREATMENT PLANT OVERVIEW

1. Description:

1.1 Primary Treatment

In the Primary Treatment Section the process effluent will be first passed through an Oil & Grease separation tank. After correction of pH with HCl, the neutralised Process effluent will be further coagulated with Ferrous Sulphate and neutralised with Hydrated Lime. After flocculation with a Polyelectrolyte the effluent will be clarified in a Primary Clarifier and will be collected in Tricking Filter Feed Sump for further secondary treatment.

1.2 Secondary Treatment

The clarified effluent from the Tricking Filter Feed sump will be pumped to the Tricking Filter as biodegradation polishing treatment. The anaerobically anoxically biodegraded effluent will be passed through a clarifier to separate the biomass and clarified effluent will be fed to the aerobic biodegradation treatment from where the effluent with biomass will be clarified of biomass in a secondary clarifier.

The domestic effluent generated on the premises will be transferred to the aeration tank for biodegradation as well as a source of biomass and nutrients.

1.3 Tertiary Treatment

The clarified effluent from the secondary clarifier will be treated though a Pressure Sand Filter and an Activated Carbon Adsorber. The treated effluent will then be collected in the final treated effluent collection sump for discharge to MIDC sewer for further treatment at Taloja CETP as a Phase I activity.

The Phase II activity will comprise of further treating the ETP Treated Effluent by 2 stage Reverse Osmosis System. The Permeate generated will be recycled and reused in the process plant for suitable activity while the Reject generated will be evaporated to separate the salt which will be landfilled at the authorised Secured Landfill site.

1.4 Reverse Osmosis Systems

The treated effluent from ETP and the utility effluent from CT and DM will be combined Upgradation of ETP including Phase II for proposed PA – IV & Plasticizer together and fed to Ultra Filtration (UF) and Reverse Osmosis (RO) system. There will be 2 parallel equal streams for UF/RO for operational flexibility. It is envisaged that 2 stage Reverse

Osmosis systems complete with all peripherals will be required for maximum recovery of reusable permeate. The permeate will be recycled and reused depending upon the quality of permeate and suitability of reuse in the process.

The Reject from both the RO Systems will be evaporated in the Multi Effect Evaporator and the salt separated will be sent for Secured Landfill. The Condensate will be treated in the ETP.

1.5 Multi Effect Evaporator

A multiple effect evaporator will be provided to treat RO Rejects as well as to separate salt from the MA Plant Caustic Neutralised effluent and Heater Scrubber neutralized effluent. The condensate will require further treatment and will therefore be treated in the ETP. The evaporator will be followed by agitated thin film dryer to ensure conversion of the slurry to almost dry solids. The salt thus separated will be disposed off to secured landfill.

1.6 Sludge Handling

Centrifuge and Filter Press systems are provided for sludge handling. Sludge is collected in bags and filtrate has taken to treatment again in ETP system. Sludge is disposed to sludge disposal site CHWTSDf, Talaja.

Details of various units provided in ETP are as below:

Sr. No	Name of Unit	Size m x m x m	Nos	Total Liquid Volume/ Plan Area	MOC
1	Oil and grease removal	10 x 1.5 x 3	1	45	RCC with epoxy
2	Equalization Tank For Process	6.5 x 5 x 3	2	195	
3	Equalization Tank For DM	6.5 x 5 x 3	2	195	
4	CT Blowdown Sump	8x 5 x 3	2	240	
5	Equalization Tank For MA Caustic Neutralized Effluent & Heater Scrubber Neutralized Effluent	6 x 3 x 2	2	72	RCC with Epoxy
6	Blending tank	6 x 6 x 3	2	216	RCC with Epoxy
7	RO feed tank	9 x 9 x 3	4	972	RCC with Epoxy
8	Evaporator feed tank	6 x 6 x 2.5	2	180	RCC with Epoxy
9	Ferrous Sulphate Coagulation Tank	1 x 1 x 1	1	1	RCC with Epoxy
10	Lime Neutralization Tank	1.5 x 1.5 x 1.5	1	2.25	RCC with Epoxy
11	Polyelectrolyte Flash Mixer	0.5 x 0.5x 0.5	1	0.13	PP/HDPE
12	Flocculator	1.25 dia x 1.5	1	1.8	MS EP
13	Primary Clarifier	3 dia x 2.5	1	17.7	RCC
14	Trickling Filter Feed Tank	7 x 7 x 3	1	147	RCC
15	Trickling filter	10 dia x 5	1	393	RCC
16	Trickling Filter Settling Tank	4x 4 x 3	1	48	RCC
17	Aeration Tank	10 x 10 x 4.5	1	450	RCC
18	Secondary Clarifier	6 dia x 3	1	85	RCC
19	Sludge collection tank	2.6 dia x 3	2	32	RCC
20	Treated Effluent PSF feed sump	5 x 5 x 2.5	1	63	RCC
21	Hypochlorite disinfection tank	2 dia x 2	1	6	RCC with epoxy/tiling

22	Final treated effluent sump (UF Feed)	10 x 10 x 3	1	300	RCC covered tank
23	UF Permeate (RO 1 feed)				RCC covered tank
24	RO Permeate tank	8 x 8 x 3	4	768	RCC covered tank
25	RO Reject Stage 2	5 x 4 x 3	2	120	RCC covered with lining /tiling
26	Evaporator plan area	25 x 7.5	1	187.5	

M/s - I G Petrochemicals Ltd

**Address – Plot No. T - 1 & T - 2, Taloja
Industrial Area, MIDC Taloja, Tal - Panvel,
Dist Raigad. PIN - 410208**

Date of update of Display: 01/11/2023

**Consent Order No: Format 1.0/CAC UAN
NO.MPCB-CONSENT-
0000115836/CR/2207000116, VALID
UPTO 31/08/2026.**

Operational Status: Operational

Production Details

Products Manufactured

Quantity MT/A

Phthalic Anhydride

222110

Maleic Anhydride

7660

Di Ethyl/Methyl Phthalate

12600

Benzoic Acid

1500

Hazardous chemicals

**Hazardous
Chemicals**

Quantity MT

Purpose

Ortho Xylene

10752

Raw Material

Diesel

50

Fuel

Furnace Oil

250

Fuel

Caustic Lye

50

**Treatment
Chemical**

Hazardous chemicals

Hazardous Chemicals	Quantity MT	Purpose
HCL	40	Treatment Chemical
Sulfuric Acid	20	Raw Material
Alcohol	441	Raw Material

Hazardous Waste

HW – Type & Category	Quantity	Mode of Treatment
1.2 - Still bottom from distillation process	455.65 MT/M	Used as fuel in oil heater/ Thermal oxidizer
1.4 – Organic Residue	150 MT/A	CHWTSDF

Hazardous Waste

HW – Type & Category

Quantity

Mode of Treatment

1.6- Spent Catalyst and molecular sieves

7.5 MT/M

Returned to manufacturer /CHWTSDF

5.1- Used or Spent oil

3.75 MT/M

Sale to authorized party

Hazardous Waste

HW – Type & Category

Quantity

Mode of Treatment

**33.1 Empty barrels/
Containers/
Liners**

104 NOs/M

**Sale to
authorized
party/
CHWTSDf**

**35.3 – Chemical sludge
from Waste water
treatment.**

1.5 MT/M

**Sent to
CHWTSDf**

Hazardous Waste

Type

Quantity

Mode of Treatment

37.1 – Ash from incinerator and flue gas cleaning residue

0.8 MT/M

Sent to CHWTSDf

37.3- Concentration or evaporation residue

250 MT/M

Sent to CHWTSDf

36.2 Spent carbon or filter medium

7.81 MT/M

Sent to CHWTSDf

Hazardous Waste

HW – Type & Category

Quantity

Mode of Treatment

15.2- Discarded asbestos

3.6 MT/M

Sent to CHWTSDF

By- product Sodium Sulphate

75 MT/M

**Sale to authorized party/
CHWTSDF**

Hazardous Waste

HW – Type & Category

Quantity

Mode of Treatment

**By-product
Phthalic Acid**

66.67 MT/M

**Sale to
authorized party/
CHWTSDf**

**By- product
Mono ester salts**

250 MT/M

**Sale to
authorized party/
CHWTSDf**

**Spent ion
exchange resin
containing toxic
metals**

7500 Lit/A

CHWTSDf

Hazardous Waste

HW – Type & Category

Quantity

Mode of Treatment

37.1- Sludge from wet scrubber

0.42 MT/M

CHWTSDf

33.1- Discarded bags used for hazardous chemicals

0.21 MT/M

CHWTSDf

Hazardous Waste

HW – Type & Category

Quantity

Mode of Treatment

Battery waste

100 Nos/Y

Sent back to manufacturer

Plastic waste

500 Kg/M

**Sale to authorized party/
Recycler**

Hazardous Waste

HW – Type & Category

Quantity

Mode of Treatment

**IT/Telecom,
Electrical,
Electronic Waste**

600 Kg/M

**Sale to authorized
E waste handler/
Recycler**

BMW - Yellow

10 Kg/M

CBMWTSDf

Hazardous Waste

**HW – Type &
Category**

Quantity

**Mode of
Treatment**

**BMW -
Translucent**

2 Kg/M

CBMWTSDF

Air Emission

Source	Fuel	APCD
Scrubber	Not Applicable	Wet Scrubbers
Boiler	FO	Stack designed for sufficient dispersion
Hot Oil Heaters	FO + Distillation Residue	Wet Scrubbers

Air Emission

Source

Fuel

APCD

**DG Set
2000/2500 KVA**

Diesel

**Stack designed for
sufficient
dispersion**

De-dusting units

Not Applicable

Bag Filters

MA Bagging

Not Applicable

Scrubber

Air Emission

Source

Fuel

APCD

MA Flaker

**Not
Applicable**

Wet Scrubber

*** OCEMS connectivity details (Date of installations & operations status) -
23/03/2017;Operational**

Effluent Discharge

Source of Effluent

Discharge With Quantity

Treatment Method

Industrial Effluent - 791 cum/day

**Through MIDC Sewer To CETP
83.04 cum/day**

ETP / Reverse Osmosis / Multiple Effect Evaporator - 791 m³/day

Effluent Discharge

Source of Effluent

Discharge With Quantity

Treatment Method

Domestic Effluent - 36 cum/day

Trough MIDC Sewer To CETP

Septic Tank & Soak Pit

*** OCEMS connectivity details (Date of installations & operations status) - 22/09/2015;Operational**

Effluent Discharge Monitoring

Parameter	Unit	MPCB Limit / Actual	
pH	—	5.5 to 9.0	7.72
TSS	mg/l	100	6.01
COD	mg/lit	250	64.78
BOD	mg/lit	100	16.36



Sustainability

Mumbai Waste Management Limited

CERTIFICATE OF MEMBERSHIP

m/s. I.G. Petrochemicals Limited.

*is a registered member of
CHW-TSDF at MIDC - Taloja for
safe and secure disposal of
Hazardous waste.*

Membership No: MWML-HZW - TAL - 946

This Certificate is valid up to 31/03/2025

Onkar Kulkarni
Manager - BMD

Somnath Malgar
Director



Maharashtra Pollution Control Board

महाराष्ट्र प्रदूषण नियंत्रण मंडळ

Form 4

See rules 6(5),13(8),16(6) and 20(2) of Hazardous and other wastes 2016

FORM FOR FILING ANNUAL RETURNS

[To be submitted to state pollution control board/pollution control committee by 30th June of every year for the preceeding period April to march]

Unique Application Number:

MPCB-HW_ANNUAL_RETURN-0000039014

Submitted On:

27-06-2023

Industry Type :

Generator

Submitted for Year:

April 2022 to March 2023

1. Name of the generator/operator of facility

I G Petrochemicals Ltd

Address of the unit/facility

Plot No T 1 & T 2, V-11 to V-14 , V-45 Taloja Industrial Area, MIDC Taloja, Tal- Panvel, Dist - Raigad, 410208

1b. Authorization Number

Format1.0/CAC/UAN No.MPCB-CONSENT-0000115836/CR/2207000116

Date of issue

Jul 2, 2022

Date of validity of consent

Aug 31, 2026

2. Name of the authorised person

Mr. Sagar Jadhav

Full address of authorised person

Plot No T 1 & T 2, V-11 to V-14 , V-45 Taloja Industrial Area, MIDC Taloja, Tal- Panvel, Dist - Raigad, 410208

Telephone

2268479100

Fax

2227410192

Email

sjadhav@igpetro.com

3. Production during the year (product wise), wherever applicable

Product Type *	Product Name *	Consented Quantity	Actual Quantity	UOM
Petrochemicals	Phthalic Anhydride	222110.0000	204554.350	MT/A
Petrochemicals	Benzoic Acid	1500.0000	816.830	MT/A
Petrochemicals	Maleic Anhydride	7660.0000	6904.225	MT/A
Petrochemicals	Di Ethyl Phthalate/ Di Methyl Phthalate	12600.0000	4678.0	MT/A

PART A: To be filled by hazardous waste generators

1. Total Quantity of waste generated category wise

Type of hazardous waste	Waste Name	Consented Quantity	Quantity	UOM
1.2 Tarry residues and still bottoms from distillation	Still bottom from distillation process	5467.800	3728.7	MTA
1.6 Spent catalyst and molecular sieves	Spent catalyst and molecular sieves	90.000	23.93	MTA
5.1 Used or spent oil	Used or spent oil	45.000	5.2	MTA
15.2 Discarded asbestos	Discarded asbestos	43.000	0.28	MTA
33.1 Empty barrels /containers /liners contaminated with hazardous chemicals /wastes	Empty barrels/containers/liners contaminated with hazardous chemicals /wastes	1248.000	1046	numbers/anum

36.2 Spent carbon or filter medium	Spent Carbon	93.720	37.86	MTA
35.3 Chemical sludge from waste water treatment	Chemical Sludge from Waste Water Treatment	18.000	4.201	MTA
1.4 Organic residues	Organic Residue	150.000	139.38	MTA
37.3 Concentration or evaporation residues	Concentration or Evaporation Residue	3000.000	522.02	MTA
37.1 Sludge from wet scrubbers	Sludge from wet Scrubber	5.040	0.37	MTA
33.1 Empty barrels /containers /liners contaminated with hazardous chemicals /wastes	Discarded Bags used for Hazardous Material	2.520	1.30	MTA
37.2 Ash from incinerator and flue gas cleaning residue	Ash from Incinerator and flue gas	9.600	2.65	MTA
Other Hazardous Waste	By product phthalic acid	800.040	148.51	MTA
Other Hazardous Waste	By product sodium sulphate	900.000	18.88	MTA
35.2 Spent ion exchange resin containing toxic metals	Spent ion exchange resins	7.500	4.32	KL/Anum

2. Quantity dispatched category wise.

Type of Waste	Quantity of waste	UOM	Dispatched to	Facility Name
1.6 Spent catalyst and molecular sieves	23.93	MTA	Disposal Facility	Mumbai Waste Management
5.1 Used or spent oil	5.2	MTA	Recycler or Actual user	M/s. Plus Lubricants
15.2 Discarded asbestos	0.28	MTA	Disposal Facility	Mumbai Waste Management
33.1 Empty barrels /containers /liners contaminated with hazardous chemicals /wastes	1046	numbers/anum	Disposal Facility	Mumbai Waste Management
36.2 Spent carbon or filter medium	37.86	MTA	Disposal Facility	Mumbai Waste Management
35.3 Chemical sludge from waste water treatment	4.25	MTA	Disposal Facility	Mumbai Waste Management
1.4 Organic residues	139.38	MTA	Disposal Facility	Mumbai Waste Management
37.3 Concentration or evaporation residues	521.29	MTA	Disposal Facility	Mumbai Waste Management
37.1 Sludge from wet scrubbers	0.37	MTA	Disposal Facility	Mumbai Waste Management
37.2 Ash from incinerator and flue gas cleaning residue	2.65	MTA	Disposal Facility	Mumbai Waste Management
33.1 Empty barrels /containers /liners contaminated with hazardous chemicals /wastes	1.3	MTA	Disposal Facility	Discarded Bags used for Haz.waste sent Mumbai Waste Management
Other Hazardous Waste	148.51	MTA	Disposal Facility	By Product Phthalic Acid sent toMumbai Waste Management
Other Hazardous Waste	18.88	MTA	Disposal Facility	By Product Sodium Sulphate sent toMumbai Waste Management
35.2 Spent ion exchange resin containing toxic metals	4.32	KL/Anum	Disposal Facility	Mumbai Waste Management

3. Quantity Utilised in-house,If any

Type of Waste	Name of Waste	Quantity of Waste	UOM
1.2 Tarry residues and still bottoms from distillation	Still Bottom from distillation process	3730.39	MTA

4. Quantity in storage at the end of the year

Type of Waste	Name of Waste	Quantity of Waste	UOM
1.2 Tarry residues and still bottoms from distillation	Still Bottom from distillation process	0	MTA
1.6 Spent catalyst and molecular sieves	Spent Catalyst and Molecular sieves	0	MTA
5.1 Used or spent oil	Used or Spent oil	0	MTA
15.2 Discarded asbestos	Discarded Asbestos	0	MTA
33.1 Empty barrels /containers /liners contaminated with hazardous chemicals /wastes	Empty barrels/containers/liners	0	numbers/anum
36.2 Spent carbon or filter medium	Spent Carbon	0	MTA
35.3 Chemical sludge from waste water treatment	Chemical Sludge from ETP	0.015	MTA
1.4 Organic residues	Organic Residue	0	MTA
37.3 Concentration or evaporation residues	Concentration or evaporation residue	2.0	MTA
37.1 Sludge from wet scrubbers	Sludge from wet scrubbers	0	MTA
37.2 Ash from incinerator and flue gas cleaning residue	Ash from Incinerator and flue gas	0	MTA
33.1 Empty barrels /containers /liners contaminated with hazardous chemicals /wastes	Discarded bags used for haz. chemicals	0	MTA
Other Hazardous Waste	By product phthalic acid	0	MTA
Other Hazardous Waste	By product sodium sulphate	0	MTA
35.2 Spent ion exchange resin containing toxic metals	Spent ion exchange resins	0	KL/Anum

5. Quantity disposed in landfills as such and after treatment

Type	Quantity	UOM
Direct landfilling	NA	KL/Anum
Landfill after treatment	NA	KL/Anum

6. Quantity incinerated (if applicable)

	UOM
NA	KL/Anum

PART B: To be filled bt Treatment,storage, and disposal facility operators

1.Total Quantity received	UOM	State Name
NA	KL/Anum	Maharashtra
2. Quantity in stock at the beginning of the year	UOM	
NA	KL/Anum	
3. Quantity treated	UOM	

NA

KL/Anum

4. Quantity disposed in landfills as such and after treatment

Type

Direct landfilling

Quantity

NA

UOM

KL/Anum

Landfill after treatment

NA

KL/Anum

5. Quantity incinerated (if applicable)

UOM

NA

KL/Anum

6. Quantity processed other than specified above

UOM

NA

KL/Anum

7. Quantity in storage at the end of the year.

UOM

NA

KL/Anum

PART C: To be filled by recyclers or co-processors or other users

1. Quantity of waste received during the year

Waste Name/Category	Country Name	State Name	Quantity of waste received from domestic sources	Quantity of waste imported(If any)	Units
NA	India	Maharashtra	NA	NA	KL/Anum

2. Quantity in stock at the beginning of the year

Waste Name/Category	Quantity	UOM
NA	NA	KL/Anum

3. Quantity of waste recycled or co-processed or used

Name of Waste	Type of Waste	Quantity	UOM
NA	NA	NA	KL/Anum

4. Quantity of products dispatched (wherever applicable)

Name of product	Quantity	UOM
NA	NA	KL/Anum

5. Total quantity of waste generated

Waste name/category	quantity	UOM
NA	NA	KL/Anum

6. Total quantity of waste disposed

Waste name/category	quantity	UOM
NA	NA	KL/Anum

7. Total quantity of waste re-exported (If Applicable)

Waste name/category	quantity	UOM
NA	NA	KL/Anum

8. Quantity in storage at the end of the year

Waste name/category	quantity	UOM
NA	NA	KL/Anum

9. Quantity disposed in landfills as such and after treatment

Type	Quantity	UOM
Direct landfilling	NA	KL/Anum
Landfill after treatment	NA	KL/Anum

10. Quantity incinerated (if applicable)

UOM
NA

Personal Details

Place	Date	Designation
--------------	-------------	--------------------

MAHARASHTRA POLLUTION CONTROL BOARD

Tel: 24010706/24010437
 Fax: 24023516
 Website: <http://mpcb.gov.in>
 Email: cac-cell@mpcb.gov.in



Kalpataru Point, 2nd and
 4th floor, Opp. Cine Planet
 Cinema, Near Sion Circle,
 Sion (E), Mumbai-400022

RED/L.S.I (R57)
**No:- Format1.0/CAC/UAN No.MPCB-
 CONSENT-0000115836/CR/2207000116**

Date: 02/07/2022

To,
**M/s I G Petrochemicals Ltd.,
 Plot Nos. T-1, T-2, T-2/1, V-11, V-12, V-13, V-14 &
 V-45 Talaja Industrial Area,
 MIDC,Taloja, Tal. Panvel, Dist. Raigad - 410 208.**



Your Service is Our Duty

Sub: Grant of Renewal of Consent to Operate under Red/LSI

- Ref:**
1. Environment Clearance accorded vide No. F. No. J-11011/ 73/ 2016-IAII(I) dtd. 18/07/2017.
 2. Environment Clearance amendment accorded vide No. F. No. J-11011/ 73/ 2016-IAII(I) dtd. 20/02/2018.
 3. Consent to Operate granted vide No. Format 1.0/ CC/ UAN No. 0000101662/ CO-2107000003 dtd. 01/7/2021
 4. Minutes of Consent Appraisal Committee meeting held on 20/5/2022

Your application No.MPCB-CONSENT-0000115836 Dated 15.06.2021

For: grant of Consent to Renewal under Section 26 of the Water (Prevention & Control of Pollution) Act, 1974 & under Section 21 of the Air (Prevention & Control of Pollution) Act, 1981 and Authorization under Rule 6 of the Hazardous & Other Wastes (Management & Transboundary Movement) Rules 2016 is considered and the consent is hereby granted subject to the following terms and conditions and as detailed in the schedule I, II, III & IV annexed to this order:

1. **The consent to renewal is granted for a period up to 31/08/2026**
2. **The capital investment of the project is Rs.1169.8758 Crs. (As per C.A Certificate submitted by industry Existing C.I. Rs. 1167 Crs + Increase in C.I. Rs. 2.8758 Crs)**
3. **Consent is valid for the manufacture of:**

Sr No	Product	Maximum Quantity	UOM
Products			
1	Di Ethyl Phthalate/ Di Methyl Phthalate	12600	MT/A
2	Maleic Anhydride	7660	MT/A
3	Phthalic Anhydride	222110	MT/A
4	Benzoic Acid	1500	MT/A
5	Power (Transmitted to Grid)	2.5	MW

4. **Conditions under Water (P&CP), 1974 Act for discharge of effluent:**

Sr No	Description	Permitted (in CMD)	Standards to	Disposal Path
1.	Trade effluent	791	As per Schedule-I	Recycle 607 CMD treated effluent into process, for cooling tower make up, fire-fighting, utility purposes etc. and discharge 220 CMD treated effluent into CETP
2.	Domestic effluent	36	As per Schedule-I	As above

5. **Conditions under Air (P& CP) Act, 1981 for air emissions:**

Sr No.	Stack No.	Description of stack / source	Number of Stack	Standards to be achieved
1	S-1	Boilers (3 Nos.)	1	As per Schedule -II
2	S-2 (A&B)	PA- I & II -Hot Oil Heaters	1	As per Schedule -II
3	S-3	PA-I Scrubber	1	As per Schedule -II
4	S-4	PA-II Scrubber	1	As per Schedule -II
5	S-5	PA-III Scrubber	1	As per Schedule -II
6	S-6	PA De-Dusting-1	1	As per Schedule -II
7	S-7	PA De-Dusting 2	1	As per Schedule -II
8	S-8	PA De-Dusting 3	1	As per Schedule -II
9	S-9	MA Bagging	1	As per Schedule -II
10	S-10	MA Flaker	1	As per Schedule -II
11	S-11	DG Set (2000 KVA)	1	As per Schedule -II
12	S-12	PA-IV Scrubber	1	As per Schedule -II
13	S-13	PA-IV Scrubber	1	As per Schedule -II
14	S-14	PA De-Dusting 4	1	As per Schedule -II
15	S-15	D.G. Set (2500 KVA)	1	As per Schedule -II

6. **Non-Hazardous Wastes:**

Sr No	Type of Waste	Quantity	UoM	Treatment	Disposal
1	Debris during maintenance activities like insulation/ packing material/ scrap iron etc.	9.0	MT/M	NA	Sale to Auth. Party/ CHWTSDF
2	Biological sludge from waste water treatment	35	MT/M	Drying	Used as manure for gardening

7. **Conditions under Hazardous & Other Wastes (M & T M) Rules 2016 for treatment and disposal of hazardous waste:**

Sr No	Category No./ Type	Quantity	UoM	Treatment	Disposal
1	1.2 Tarry residues and still bottoms from distillation	455.65	MT/M	Incineration	Used as fuel in Oil Heater/ Thermal Oxidizer
2	1.4 Organic residues	150	MT/A	Incineration	CHWTSDF
3	1.6 Spent catalyst and molecular sieves	7.5	MT/M	Recycle/ Incineration	Return to manufacturer/ CHWTSDF
4	5.1 Used or spent oil	3.75	MT/M	Recycle	Sale to Auth. Party
5	33.1 Empty barrels /containers /liners contaminated with hazardous chemicals /wastes	104	No/M	Recycle*	Sale to Auth. Party having permission under Rule 9/ CHWTSDF
6	35.3 Chemical sludge from waste water treatment	1.5	MT/M	Secured Landfill	CHWTSDF
7	37.2 Ash from incinerator and flue gas cleaning residue	0.8	MT/M	Secured Landfill	CHWTSDF
8	37.3 Concentration or evaporation residues	250	MT/M	Secured Landfill after treatment	CHWTSDF
9	36.2 Spent carbon or filter medium	7.81	MT/M	Incineration	CHWTSDF
10	15.2 Discarded asbestos	3.6	MT/M	Secured Landfill	CHWTSDF
11	37.1 Sludge from wet scrubbers	0.42	MT/M	Secured Landfill after treatment	CHWTSDF
12	33.1 Discarded Bags used for hazardous chemicals	0.21	MT/M	Incineration	CHWTSDF
13	35.2 Spent ion exchange resin containing toxic metals	7500	Ltr/A	Incineration	CHWTSDF
14	By-product Sodium Sulphate	75	MT/M	Recycle*/Landfill	Sale to Auth. Party having permission under Rule 9/ CHWTSDF
15	By-product Phthalic Acid	66.67	MT/M	Recycle*/Landfill	Sale to Auth. Party having permission under Rule 9/ CHWTSDF

Sr No	Category No./ Type	Quantity	UoM	Treatment	Disposal
16	By-product Mono Ester Salts	250	MT/M	Recycle*/Landfill	Sale to Auth. Party having permission under Rule 9/ CHWTSDf

8. **Conditions under Batteries (Management & Handling) Rules, 2001:**

Sr No	Type of Waste	Quantity	UoM	Disposal Path
1	Battery waste	100.00	Nos./Y	Sent back to manufacturer

Specific Conditions for used Batteries:

- i. The applicant shall ensure that used batteries are not disposed of in any manner other than by depositing with the authorized dealer/ manufacturer/ registered recycler/ importer/ re-conditioner or at the designated collection center.
- ii. The applicant shall file half-yearly return in Form VIII to the M.P.C. Board.
- iii. Bulk consumers to their user units may auction used batteries to registered recyclers only.

9. **Conditions under Plastic Waste Management Rules, 2016 (Notification dtd. 18/03/2016):**

Sr No	Type of Waste	Quantity	UoM	Disposal Path
1	Plastic waste	500.00	Kg/M	Sale to Auth. Party/ Recycler

10. **Conditions under E-Waste Management:**

Sr No	Type of Waste	Quantity	UoM	Disposal Path
1	IT/ Telecom, Electrical, Electronic wastes	600.00	Kg/M	Sale to Auth. E waste handler/ Recycler

11. The Board reserves the right to review, amend, suspend, revoke this consent and the same shall be binding on the industry.
12. This consent should not be construed as exemption from obtaining necessary NOC/ permission from any other Government authorities.
13. Industry shall operate and maintain ETP so as to achieve Consented standards.
14. Industry shall adopt Cleaner fuel in place of Furnace Oil in compliance with Board's Circular dtd. 20/02/2020.
15. Industry shall comply with the conditions stipulated in Environment Clearance accorded vide No. F. No. J-11011/ 73/ 2016-IAII(I) dtd. 18/07/2017 and amendment dtd. 20/02/2018.
16. The applicant shall ensure disposal of by-products to Actual user having permission under Rule 9 of Hazardous and Other Wastes(Management & Transboundary Movement) Rules 2016.
17. This consent is issued as per the minutes of Consent Appraisal Committee meeting held on 20/5/2022



Received Consent fee of -

Sr.No	Amount(Rs.)	Transaction/DR.No.	Date	Transaction Type
1	10488892.00	MPCB-DR-6679	01/07/2021	RTGS
2	50000.00	TXN2206001444	14/06/2022	Online Payment

Total fee required to pay Rs. 11713758 (5 term fee + C to E for increased CI). Industry has paid consent fee of Rs. 11830310/- (Rs. 10488892/- + Rs. 50000/- along with application + Rs. 1291418/- balance fee of Rs. 1291418 as per existing consent to operate dated 01/7/2021). Now, Rs. 116552/- will remain balance with the Board.

Copy to:

1. Regional Officer, MPCB, Navi Mumbai and Sub-Regional Officer, MPCB, Talaja
- They are directed to ensure the compliance of the consent conditions.
2. Chief Accounts Officer, MPCB, Sion, Mumbai
3. CC-CAC Desk- for record & website updating purpose.



SCHEDULE-I

Terms & conditions for compliance of Water Pollution Control:

- 1) A] As per your application, you have provided Effluent Treatment Plant (ETP) of designed capacity 799 CMD consisting of Primary, Secondary, Tertiary treatment followed by UF, Two stage RO, 4 effect MEE & ATFD for the treatment of 791 CMD industrial effluent.
- B] The Applicant shall operate the effluent treatment plant (ETP) to treat the trade effluent so as to achieve the following standards prescribed by the Board or under EP Act, 1986 and Rules made there under from time to time, whichever is stringent.

Sr. No.	Parameters	Limiting concentration not to exceed in mg/l, except for pH
1	pH	5.5 to 9.0
2	Oil & Grease	10 mg/l
3	BOD	100 mg/l
4	COD	250 mg/l
5	Suspended Solids	100 mg/l
6	Chloride	600 mg/l
7	Sulphate	1000 mg/l
8	TDS	2100 mg/l
9	TAN	50 mg/l

- C] The 607 CMD treated effluent (including 36 CMD domestic effluent) shall be recycled into process, for cooling tower make up, fire-fighting, utility purposes etc. and restrict discharge of 220 CMD treated effluent into CETP with water metering system for further treatment & disposal. In no any case treated/untreated effluent shall find its way outside the factory premises directly or indirectly.
- D] Industry shall ensure that the OCEMS is equipped with remote calibrating facility and online monitoring data is connected to MPCB & CPCB Servers.
- 2) A] As per your application, you have provided septic tank and soak pit for the treatment of 36.00 CMD sewage.
- B] Overflow is connected to Aeration tank of ETP.
- 3) The Applicant shall comply with the provisions of the Water (Prevention & Control of Pollution) Act, 1974 and as amended, by installing water meters, and other provisions as contained in the said act:

Sr. No.	Purpose for water consumed	Water consumption quantity (CMD)
1.	Industrial Cooling, spraying in mine pits or boiler feed	4776.00
2.	Domestic purpose	44.00
3.	Processing whereby water gets polluted & pollutants are easily biodegradable	733.00

4.	Processing whereby water gets polluted & pollutants are not easily biodegradable and are toxic	0.00
5.	Gardening	10

- 4) **The Applicant shall comply with the provisions of the Water (Prevention & Control of Pollution) Act, 1974 and as amended, by installing water meters, and other provisions as contained in the said act:**
- 5) **Prior permission shall be obtained from CGWA / irrigation department if ground Water/surface water is being used for industrial/Domestic purpose.**
- 6) **The project proponent shall monitor regularly ground water quality at least twice a year (pre and post monsoon) at sufficient numbers of piezometers/sampling wells in the plant and adjacent areas through labs recognized under Environment (Protection) Act, 1986 or through NABL accredited laboratories.**



SCHEDULE-II

Terms & conditions for compliance of Air Pollution Control:

- 1) As per your application, you have provided the Air pollution control (APC) system and erected following stack(s) and observe the following fuel pattern-

Stack No.	Stack Attached To	APC System	Height in Mtrs.	Type of Fuel	Quantity & UoM	S%	SO ₂ (kg/day)
S-1	Boilers (3 Nos.)	Stack	55	LSHS	27 MT/Day	1.20	648.00
S-2	Hot Oil Heaters (2A & 2 B)	Stack	31	LSHS	4MT/Day	4.50	96.00
	Hot Oil Heaters (2 Nos.)			Distillation Residue	7MT/Day	0.00	0.00
S-3 to S-5	Process Vents PA- I, II & II	Scrubber	50	--	--	--	--
S-6 to S-8	PA De-dusting filter (3 Nos.)	Wet Scrubber	12	--	--	--	--
S-9	MA Bagging	Wet Scrubber	30	--	--	--	--
S-10	MA Flaker	Bag Filter	30	--	--	--	--
S-11	D.G. Set (2000 KVA)	Acoustic Enclosure/ Stack	15	HSD	8.3 MT/Day	1.00	166.00
S-12	Hot Oil Heater/ Thermal Oxidizer	Wet Scrubber	31	HSD	2.5MT/Day	1.00	50.00
				Distillation Residue	4.2MT/Day	0.00	0.00
S-13	Process Vent PV-IV	Wet Scrubber	50	--	--	--	--
S-14	PA De-dusting filter	Bag Filter	12	--	--	--	--
S-15	D.G. Set (2500 KVA)	Acoustic Enclosure/ Stack	30	HSD	380 Kg/Hr	1.00	182.40

- 2) The Applicant shall provide Specific Air Pollution control equipments as per the conditions of EP Act, 1986 and rule made there under from time to time/ Environmental Clearance / CREP guidelines.

3) The applicant shall operate and maintain above mentioned air pollution control system, so as to achieve the level of pollutants to the following standards:

A. Emission from Chimney /stack

Sr No.	Parameters	Fuel Type	Limiting Concentration not to exceed
1	Sulphur Di Oxide (SO ₂)	Liquid	850
2	Oxides of Nitrogen (NO _x)	Liquid	350
3	Particulate Matter	Liquid	50
4	Carbon Monoxide (CO)	Liquid	150

B. Process Emission (specific from Chimney /stack :

Sr No.	Parameters	Source	Limiting Concentration not to exceed
1	Organic Particulate	PA, MA and TDI Plants	25

C. Load Based Standards :

Sr No.	Parameters	Source	Quantum limit in gm/hour for New/ Expansion Plants (gm/hr)
--------	------------	--------	--

4) Storage of Volatile Liquids : General Petroleum/Petrochem Products

- 1) Storage tanks with capacity between 4 to 75m³ and total vapour Pressure (TVP) of more than 10 kpa should have Fixed Roof Tank (FRT) with pressure valve vent.
- 2) Storage tank with the capacity between 75 to 500 m³ and total vapour Pressure (TVP) of 10 to 76 kpa should have Internal Floating Root Tank (IFRT) or External Floating Root Tank (EFRT) or Fixed Roof Tank with vapour control or vapour balancing system.
- 3) Storage tanks with the capacity of more than 500 m³ and total vapour Pressure (TVP) of 10 to 76 kpa should have Internal Floating Roof Tank or External Floating Roof Tank or Fixed Roof Tank with vapour control system.
- 4) The tanks with the capacity of more than 75 m³ and total vapour Pressure (TVP) of more than 76 kpa should have Fixed Root Tank with vapour control system.

5) Requirement for seals in Floating Roof Tanks:

- i) a) IFRT and EFRT shall be provided with double seals with minimum vapour recovery of 96%.
 - b) Primary seal shall be liquid or shoe mounted for EFRT and vapour mounted for IFRT. Maximum seal gap width will be 4 cm and maximum gap area will be 200 cm²/m of tank diameter.
 - c) Secondary seal shall be rim mounted. Maximum seal gap width will be 1.3 cm and maximum gap area will be 20 cm²/m of tank diameter.
 - d) Material of seal and construction shall ensure high performance and durability
- ii) Fixed Roof Tanks shall have vapor control efficiency of 95% and vapour balancing efficiency of 90%
- iii) Inspection and maintenance of storage tanks shall be carried out under strict control. For the inspection, API RP 575 may be adopted, In-service inspection with regard seal gap should be carried out once in every six months and repair to be implemented in short time. In future, possibility of on-stream repair of both seals shall be examined.
- iv) Storage tanks shall be painted with white colour shade, except for derogation of visually sensitive area.

5) Storage of Benzene, VCM and ACN

- i. FRT with vapour for inceneration with 99.9% of removal efficiency for volatile organic compounds (VOCs) shall be provided, or
- ii. IFRT/EFRT with double seals, emissio-reducing roof fitting and fitted with fixed roof with vapour removal efficiency of atleast 99% shall be provided, or
- iii. Internal floating roof and nitrogen blanketing in between fixed and floating roofs shall be provided.

6) Emission control for Road tank truck/Rail tank wagon loading

Loading of Volatile Products	Gasoline and Naphtha: (i) VOC reduction, % (ii) Emission, gm/m ³	(i) 99.50 (ii) 5.00
	Benzene: (i) VOC reduction, % (ii) Emission, mg/m ³	(i) 99.99 (ii) 20.00
	Toluene/Xylene: (i) VOC reduction, % (ii) Emission, mg/m ³	(i) 99.98 (ii) 150.00

Note:
 (i) It shall be applicable for Gasoline, Naphtha, Benzene, Toluene and Xylene loading.
 (ii) Road tank Truck shall have Bottom loading and Roll tank wagon shall have Top submerged loading.
 (iii) Annual leak testing for vapour collection shall be done.

7) VOC Emission Controls: -

- a) The Industry shall take all operational practices & implement control measures to limit VOC emission during breathing (tank evaporative emission) and during filling of storage tanks as mandated under storage tank provision of GSR 186 (E) Dt.18.03.2008.
- b) Industry shall keep record indicating type of chemical stored in different tanks & submit the same to MPCB every month.
- c) The tanks shall be maintained as per the API RP 575 Standards and provided with modern instrumentation to ensure that there shall be no leakage or spillage during handling.
- d) The industry shall have preventive maintenance plan and keep records of preventative maintenance carried out. For IFR Tanks, this shall include regular inspection of seals, seal gap, condition of various sleeves, jackets etc.
- e) The industry shall monitor vapor pressure in the tanks. The Industry shall spray water on tanks shells by water sprinklers installed, provided tank vapor pressure exceeds set norms. Industry shall maintain records of operation of fire water sprinkler & submit the same to MPCB every month.
- f) The industry shall provide adequate arrangement for capturing VOC emission during tanker filling. This shall include providing compatible lids (with suitable openings for filling pipe and fume extraction vent) to close the manholes on the tanker top so that no VOC emissions leaks into the environment. Alternative bottom loading of tankers with leak proof vapour collection facilities at the manholes will be provided. Compatible loading arms with level gauge, metered flow to tanker to ensure control filling to be provided. Vapour capturing hoses shall be connected to central header and shall have extra provision for collecting VOC emissions from maintenance activities and during pigging of pipelines.
- g) The collection header shall be connected to Air pollution control system consisting of brine chiller followed by activated carbon/charcoal to meet standard as given in DSR -186 (E) Dt.18.03.2008
- h) The industry shall explore possibility of collecting vapours from open manholes during tank washing and diverting the same to the air pollution control system provided.
- i) Industry shall ensure that the nitrogen /air used during pigging operations shall be diverted to the air pollution control system provided.
- j) The air blown from manifold to tanker filling point shall be diverted to air pollution control system provided.
- k) High level alarm synchronized with cut off capacity shall be provided to the storage tanks.
- l) The internal roads shall be cement concrete and shall be maintained with adequate green belt.
- m) The industry shall monitor ambient air quality on a monthly basis and the emission of Volatile Organic Compound particularly Toluene, Xylene and non-methane Hydro Carbon from MoEF approved laboratory.
- n) The industry shall not cause any nuisance in surrounding area.

8) Industry shall provide Air Pollution Control System for Paint Booth (Water contain) and leak detection system with alarm.

- 9) Industry shall install 24*7 online continuous emission monitoring system at process stack to monitor stack emissions as per CPCB guidelines and it's connectivity to CPCB & MPCB Servers . PP shall Calibrate these system from time to time according to equipment supplier specification through labs recognized under Environment (Protection) Act , 1986 or NABL accredited laboratories.
- 10) Project proponent shall monitor fugitive emissions in the plant premises at least once in every quarter through labs recognized under Environment (Protection) Act, 1986.
- 11) National Emissions standards for Organic chemicals manufacturing Industry Issued by MOEFCC vide G.S.R. No 608 E DATED 21 July 2010 and amended from time to time shall be followed.
- 12) The National Emission Standards for Petroleum Oil Refinery issued by the Ministry vide G.S.R. 186(E) dated 18th March, 2008 and G.S.R. 595 (E) dated 9th November, 2012 as amended time to time be followed.
- 13) The National Emission Standards for Petrochem (Basic & Intermediates) issued by the Ministry vide G.S.R. 820 (E) dated 9th November, 2012 as amended time to time shall be followed.

SCHEDULE-III

Details of Bank Guarantees:

Sr. No	Consent (C2E/C2O/C2R)	Amt of BG Imposed	Submission Period	Purpose of BG	Compliance Period	Validity Date
1	C2O	2400000	Existing	Towards O&M of pollution control systems and towards compliance of the Consent conditions	31/8/2026	28/2/2027
2	C2O	200000	Existing	Towards O&M of pollution control systems and towards compliance of the Consent conditions	31/8/2026	28/2/2027

BG Forfeiture History

Srno.	Consent (C2E/C2O/C2R)	Amount of BG imposed	Submission Period	Purpose of BG	Amount of BG Forfeiture	Reason of BG Forfeiture
NA						

BG Return details

Srno.	Consent (C2E/C2O/C2R)	BG imposed	Purpose of BG	Amount of BG Returned
NA				

SCHEDULE-IV
General Conditions:

1. The waste generator shall.-
 - a) take steps to minimize generation of plastic waste and segregate plastic waste at source in accordance with the Plastic Waste Management Rules, 2016 or as amended from time to time.
 - b) not litter the plastic waste and ensure segregated storage of waste at source and handover segregated waste to urban local body or gram panchayat or agencies appointed by them or registered waste pickers', registered recyclers or waste collection agencies;
2. All institutional generators of plastic waste, shall segregate and store the waste generated by them in accordance with the Plastic Waste Management Rules, 2016 amendment from time to time and handover segregated wastes to authorized waste processing or disposal facilities or deposition centers either on its own or through the authorized waste collection agency.
3. All waste generators shall pay such user fee or charge as may be specified in the byelaws of the local bodies for plastic waste management such as waste collection or operation of the facility thereof, etc.;
4. Every person responsible for organizing an event in open space, which involves service of food stuff in plastic or multilayered packaging shall segregate and manage the waste generated during such events in accordance with the Plastic Waste Management Rules, 2016 amendment from time to time.
5. Consumers or bulk consumers of electrical and electronic equipment listed in Schedule I shall ensure that e-waste generated by them is channelised through collection centre or dealer of authorised producer or dismantler or recycler or through the designated take back service provider of the producer to authorised dismantler or recycler
6. Bulk consumers of electrical and electronic equipment listed in Schedule I shall maintain records of e-waste generated by them in Form-2 and make such records available for scrutiny by the concerned State Pollution Control Board
7. Consumers or bulk consumers of electrical and electronic equipment listed in Schedule I shall ensure that such end-of-life electrical and electronic equipment are not admixed with e-waste containing radioactive material as covered under the provisions of the Atomic Energy Act, 1962 (33 of 1962) and rules made there under;
8. Bulk consumers of electrical and electronic equipment listed in Schedule I shall file annual returns in Form-3, to the concerned State Pollution Control Board on or before the 30th day of June following the financial year to which that return relates. In case of the bulk consumer with multiple offices in a State, one annual return combining information from all the offices shall be filed to the concerned State Pollution Control Board on or before the 30th day of June following the financial year to which that return relates.
9. Specific Conditions for storage, Handling and Disposal of Waste from Electrical & Electronic equipment (WEEE):
 1. **Collection of WEEE** - The applicant must provide appropriate and dedicated vehicles duly identified as per the norms for transportation of Hazardous Waste. The applicant shall obtain all the required permits for transportation of WEEE from competent authority. The applicant shall ensure the safe transport of the WEEE without any spillage during transportation.
Storage for disassembled parts: The applicant must provide appropriate storage for disassembled spare parts from WEEE. Some spare parts (e.g. motors and compressors) will contain oil and/or other fluids. Such part must be appropriately segregated and stored in containers that are secured such that oil and other fluids cannot escape from them. These containers must be stored on an area with an area with an impermeable surface and a sealed drainage system.

2. **Storage for other components and residues:**Other components and residues arising from the treatment of WEEE will need to be contained following their removal for disposal or recovery. Where they contain hazardous substances they should be stored on impermeable surface and in appropriate containers or bays with weatherproof covering. Containers should be clearly labelled to identify their contents and must be secured so that liquids, including rain water cannot enter them. Components should be segregated having regard to their eventual destinations and the compatibility of the component types. All batteries should be handled and stored having regard to the potential fire risk associated with team.
3. **Balances :** WEEE Guidelines also requires that sites for handling of WEEE have “balances to measure the weight of the segregated waste’. The objective is to ensure that a record of weights can be maintained of WEEE entering a facility and components and materials leaving each site (together with their destinations). The nature of the weighing equipment should be appropriate for the type and quantity of WEEE being processed.
4. Plastic, which cannot be recycled and is hazardous in nature, is recommended to be land filled in nearby CHWTSDF.
5. Ferrous and nonferrous metal recycling facilities fall under the purview of existing environmental regulations for air, water, noise, land and soil pollution and generation of hazardous waste and the same should be followed.
6. CFCS should be either reused or incinerated in common hazardous waste Incineration facilities at CHWTSDF.
7. Waste Oil should be either reused or incinerated in common hazardous waste incineration facilities.
8. PCB's containing capacitors shall be incinerated in common hazardous waste incineration facilities at CHWTSDF.
9. Mercury recovery and lead recycling facilities from batteries fall under the Hazardous & Other Wastes (M & TM) Rules, 2016.
10. Existing environmental regulations for air; water; noise, land and soil pollution and generation of hazardous waste and the same should be followed. In case Mercury or lead recovery is very low, they can be temporarily stored at e-waste recycling facility and later disposed in TSDF.
11. The industry shall maintain records of the e-waste purchased, processed in Form-2 and shall file annual returns of its activities of previous year in Form-3 as per Rules 11(9) & 13(3)(vii) of the E-Waste(M) Rules, 2016; on or before 30th day of June of every year.
10. The Energy source for lighting purpose shall preferably be LED based
11. The PP shall harvest rainwater from roof tops of the buildings and storm water drains to recharge the ground water and utilize the same for different industrial applications within the plant
12. Conditions for D.G. Set
 - a) Noise from the D.G. Set should be controlled by providing an acoustic enclosure or by treating the room acoustically.
 - b) Industry should provide acoustic enclosure for control of noise. The acoustic enclosure/ acoustic treatment of the room should be designed for minimum 25 dB (A) insertion loss or for meeting the ambient noise standards, whichever is on higher side. A suitable exhaust muffler with insertion loss of 25 dB (A) shall also be provided. The measurement of insertion loss will be done at different points at 0.5 meters from acoustic enclosure/room and then average.
 - c) Industry should make efforts to bring down noise level due to DG set, outside industrial premises, within ambient noise requirements by proper siting and control measures.

- d) Installation of DG Set must be strictly in compliance with recommendations of DG Set manufacturer.
- e) A proper routine and preventive maintenance procedure for DG set should be set and followed in consultation with the DG manufacturer which would help to prevent noise levels of DG set from deteriorating with use.
- f) D.G. Set shall be operated only in case of power failure.
- g) The applicant should not cause any nuisance in the surrounding area due to operation of D.G. Set.
- h) The applicant shall comply with the notification of MoEFCC, India on Environment (Protection) second Amendment Rules vide GSR 371(E) dated 17.05.2002 and its amendments regarding noise limit for generator sets run with diesel.
13. The applicant shall maintain good housekeeping.
14. The non-hazardous solid waste arising in the factory premises, sweepings, etc. be disposed of scientifically so as not to cause any nuisance / pollution. The applicant shall take necessary permissions from civic authorities for disposal of solid waste.
15. The applicant shall not change or alter the quantity, quality, the rate of discharge, temperature or the mode of the effluent/emissions or hazardous wastes or control equipments provided for without previous written permission of the Board. The industry will not carry out any activity, for which this consent has not been granted/without prior consent of the Board.
16. The industry shall ensure that fugitive emissions from the activity are controlled so as to maintain clean and safe environment in and around the factory premises.
17. The industry shall submit quarterly statement in respect of industries obligation towards consent and pollution control compliance's duly supported with documentary evidences (format can downloaded from MPCB official site).
18. The industry shall submit official e-mail address and any change will be duly informed to the MPCB.
19. The industry shall achieve the National Ambient Air Quality standards prescribed vide Government of India, Notification No. B-29016/20/90/PCI-L dated. 18.11.2009 as amended.
20. The Board reserves its rights to review plans, specifications or other data relating to plant setup for the treatment of waterworks for the purification thereof & the system for the disposal of sewage or trade effluent or in connection with the grant of any consent conditions. The Applicant shall obtain prior consent of the Board to take steps to establish the unit or establish any treatment and disposal system or an extension or addition thereto.
21. The industry shall ensure replacement of pollution control system or its parts after expiry of its expected life as defined by manufacturer so as to ensure the compliance of standards and safety of the operation thereof.
22. The PP shall provide personal protection equipment as per norms of Factory Act
23. Industry should monitor effluent quality, stack emissions and ambient air quality monthly/quarterly.
24. Whenever due to any accident or other unforeseen act or even, such emissions occur or is apprehended to occur in excess of standards laid down, such information shall be forthwith Reported to Board, concerned Police Station, office of Directorate of Health Services, Department of Explosives, Inspectorate of Factories and Local Body. In case of failure of pollution control equipments, the production process connected to it shall be stopped.
25. The applicant shall provide an alternate electric power source sufficient to operate all pollution control facilities installed to maintain compliance with the terms and conditions of the consent. In the absence, the applicant shall stop, reduce or otherwise, control production to abide by terms and conditions of this consent.


26. The industry shall recycle/reprocess/reuse/recover Hazardous Waste as per the provision contain in the Hazardous and Other Wastes (M & TM) Rules 2016, which can be recycled /processed /reused /recovered and only waste which has to be incinerated shall go to incineration and waste which can be used for land filling and cannot be recycled/reprocessed etc. should go for that purpose, in order to reduce load on incineration and landfill site/environment.
27. An inspection book shall be opened and made available to the Board's officers during their visit to the applicant.
28. Industry shall strictly comply with the Water (P&CP) Act, 1974, Air (P&CP) Act, 1981 and Environmental Protection Act, 1986 and industry specific standard under EP Rules 1986 which are available on MPCB website (www.mpcb.gov.in).
29. Separate drainage system shall be provided for collection of trade and sewage effluents. Terminal manholes shall be provided at the end of the collection system with arrangement for measuring the flow. No effluent shall be admitted in the pipes/sewers downstream of the terminal manholes. No effluent shall find its way other than in designed and provided collection system.
30. Neither storm water nor discharge from other premises shall be allowed to mix with the effluents from the factory.
31. The industry should not cause any nuisance in surrounding area.
32. The industry shall take adequate measures for control of noise levels from its own sources within the premises so as to maintain ambient air quality standard in respect of noise to less than 75 dB (A) during day time and 70 dB (A) during night time. Day time is reckoned in between 6 a.m. and 10 p.m. and night time is reckoned between 10 p.m. and 6 a.m.
33. The industry shall create the Environmental Cell by appointing an Environmental Engineer, Chemist and Agriculture expert for looking after day to day activities related to Environment and irrigation field where treated effluent is used for irrigation.
34. The applicant shall provide ports in the chimney/(s) and facilities such as ladder, platform etc. for monitoring the air emissions and the same shall be open for inspection to/and for use of the Board's Staff. The chimney(s) vents attached to various sources of emission shall be designated by numbers such as S-1, S-2, etc. and these shall be painted/ displayed to facilitate identification.
35. The industry should comply with the Hazardous and Other Wastes (M & TM) Rules, 2016 and submit the Annual Returns as per Rule 6(5) & 20(2) of Hazardous and Other Wastes (M & TM) Rules, 2016 for the preceding year April to March in Form-IV by 30th June of every year.
36. The applicant shall install a separate meter showing the consumption of energy for operation of domestic and industrial effluent treatment plants and air pollution control system. A register showing consumption of chemicals used for treatment shall be maintained.
37. The applicant shall bring minimum 33% of the available open land under green coverage/ plantation. The applicant shall submit a yearly statement by 30th September every year on available open plot area, number of trees surviving as on 31st March of the year and number of trees planted by September end.
38. The Board reserves its rights to review plans, specifications or other data relating to plant setup for the treatment of waterworks for the purification thereof & the system for the disposal of sewage or trade effluent or in connection with the grant of any consent conditions.

39. The firm shall submit to this office, the 30th day of September every year, the Environment Statement Report for the financial year ending 31st March in the prescribed FORM-V as per the provisions of Rule 14 of the Environment (Protection) (second Amendment) Rules, 1992.
40. The Applicant shall obtain necessary prior permission for providing additional control equipment with necessary specifications and operation thereof or alteration or replacement/alteration well before its life come to an end or erection of new pollution control equipment.
41. The Board reserves its rights to vary all or any of the condition in the consent, if due to any technological improvement or otherwise such variation (including the change of any control equipment, other in whole or in part is necessary).
42. The applicant shall provide facility for collection of environmental samples and samples of trade and sewage effluents, air emissions and hazardous waste to the Board staff at the terminal or designated points and shall pay to the Board for the services rendered in this behalf.

This certificate is digitally & electronically signed.



ANNEXURE – 16 – OCEMS DASHBOARD

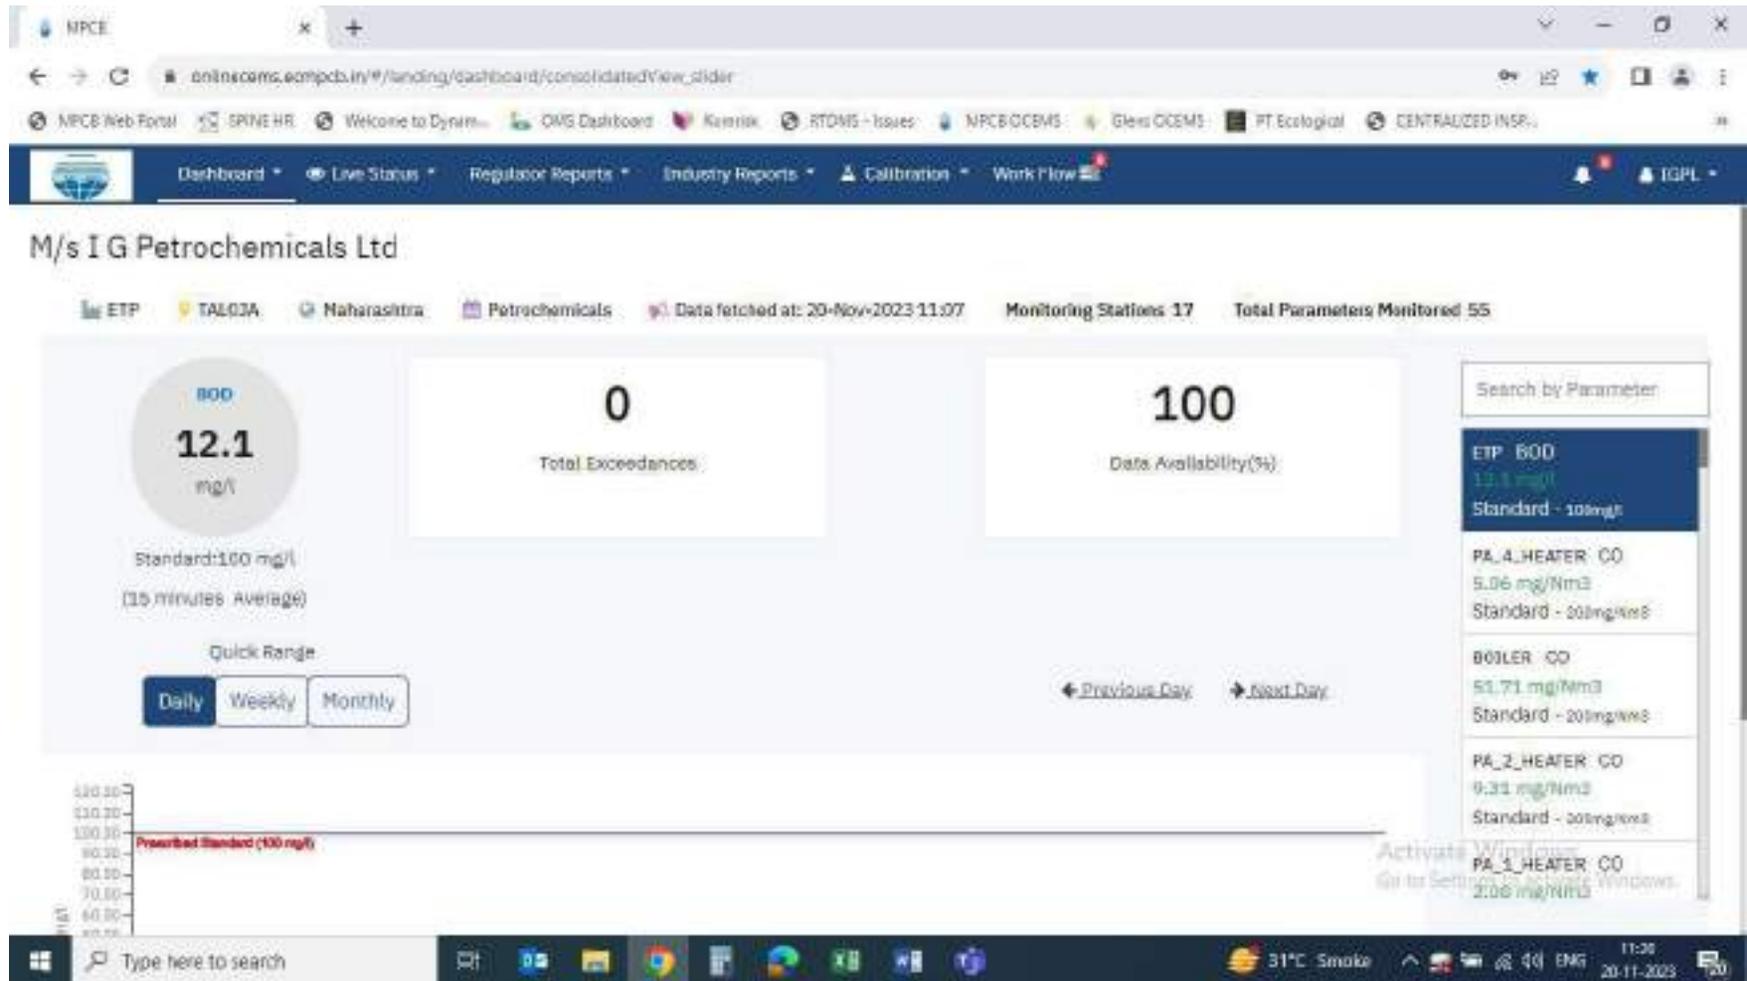

ANNEXURE - XVII

I G PETROCHEMICALS LIMITED

DETAILS OF EXPENDITURE ON ENVIRONMENT SOCIAL RESPONSIBILITY

PERIOD 01.04.2023 TO 30.09.23

Sr.No 56

SR. NO.	PAID TO	PERIOD		AMOUNT	Voucher No.	Voucher Date
		FROM	TO			
1	<u>TALOJA FACTORY</u>					
	<u>Maintenance of Trees (By K D Patil)</u>					
	(At Koyanavele/ghotcamp,Bhoirwada Road, Nitlas Village & FG Glass MIDC Road Divider)					
	Water supply Thru Water Tanker	4/1/2023	4/30/2023	65,000.00	PV-TAL/2324090050	15-Sep-23
		5/1/2023	5/31/2023	65,000.00	PV-TAL/2324090049	15-Sep-23
		6/1/2023	6/30/2023	65,000.00	PV-TAL/2324090048	15-Sep-23
		7/1/2023	7/31/2023	65,000.00	PV-TAL/2324090047	15-Sep-23
	8/1/2023	8/31/2023	65,000.00	PV-TAL/2324100270	31-Oct-23	
	9/1/2023	9/30/2023	-	Bill to be passed		
	TOTAL-Expenses			325,000.00		

ANNEXURE - XVIII

**I G PETROCHEMICALS LIMITED
DETAILS OF EXPENDITURE ON CORPORATE SOCIAL RESPONSIBILITY
PERIOD 01.04.2023 TO 30.09.2023**

SR. NO.	PAID TO	AMOUNT	GST AMOUNT	TOTAL	Voucher No.	Voucher Date
A	<u>BOMBAY OFFICE</u>					
1	INTERNATION SOCIETY FOR KRISHNA CONSCIOUSNESS (Goseva for Talasari)	1,000,000.00	-	1,000,000.00	MUM-BP/2324060263	14-Jun-23
2	Saraswati shishu mandir Trust CIT (S) 12A (A) 94/95 MADHURA-/96 DTD 06.02.95 (Donation)	5,000,000.00 5,000,000.00		5,000,000.00 5,000,000.00	MUM-BP/2324060258 MUM-BP/2324080461	14-Jun-23 24-Aug-23
	Total - (A)	11,000,000.00	-	11,000,000.00		
B	<u>TALOJA FACTORY</u>					
1	<u>Param Shantidham Vridhashram</u> Taloja MIDC , Opposite -Tecnova Co, Post - Koyalnaweale, Taluka-Panvel PAN:- AAATP 3007C , DIT (E) /MC/80G/2930/2009-10 (Registration No 12962 Income Tax Act 1961 U/S 80G)	30,000.00 30,000.00 30,000.00 30,000.00 30,000.00	- - - - -	30,000.00 30,000.00 30,000.00 30,000.00 30,000.00	TL-BP/2324040206 TL-BP/2324060001 TL-BP/2324060001 TL-BP/2324070295 TL-BP/2324080001 TL-BP/2324090001	18-Apr-23 1-Jun-23 1-Jun-23 21-Jul-23 1-Aug-23 1-Sep-23
	Total - (B)	180,000.00	-	180,000.00		
	TOTAL	11,180,000.00	-	11,180,000.00		

ANNEXURE - XIX



F. No. J-11011/73/2016-IA-II(I)
Government of India
Ministry of Environment, Forest & Climate Change
Impact Assessment Division

Indira Paryavaran Bhawan,
Jor Bagh Road, New Delhi-110 003

Dated: 6th October, 2022

To,

M/s. IG Petrochemicals Limited,
MIDC Taloja, Tehsil: Panvel,
Dist.: Raigad, Maharashtra.

Sub: Proposed expansion of Petrochemical manufacturing facility located at Plot No.: T-2, V-45, V-11 to V-14, T-2/1, T-1, MIDC Taloja, Tehsil: Panvel, Dist.: Raigad, Maharashtra by M/s. IG Petrochemicals Limited– Amendment in Environmental Clearance reg.

Sir,

This refers to your online proposal No. IA/MH/IND2/284398/2022 dated 10th August, 2022 for amendment in the environmental clearance to the above mentioned project.

2. The Ministry of Environment, Forest and Climate Change has considered the above proposal for amendment in the environmental clearance granted by the Ministry vide EC Identification No. EC22A020MH142817 (File No. J-11011/73/2016-IA-II(I)) dated 14th March, 2022 for Proposed expansion of Petrochemical manufacturing facility located at plot No.: T-2, V-45, V-11 to V-14, T-2/1, T-1, MIDC Taloja, Tehsil Panvel, District Raigad, State Maharashtra by M/s. IG Petrochemicals Limited.

3. The project proponent has requested for amendment in the EC with the details are as under.

S. N.	Para of EC	Details as per EC dated 14 th March, 2022 (From)	To be revised (Read as)	Justification/ Reasons
1	Para- 17 and 22 (A) Specific condition i	Industry shall install solar power of at least 10% of its total power requirement within plant/ nearby villages as a part of EMP.	Industry shall install solar power of at least 16% of the power requirement of proposed expansion project within plant.	Power requirement for proposed expansion project is 2750 KW. Proposal for installing solar power unit on warehouse roof (4288 m ² area) which will generate approx. 400 KW. (16% of proposed expansion power requirement). Industry generates power from waste steam generated from exothermic heat of reaction (green power) and is self-sufficient in power requirement. The same will be applicable for expansion. No grid power required during normal plant operations.
2.	Para 22 (A) Specific Condition ii	The project proponent will treat and reuse the treated water within the factory	Industry shall restrict CETP discharge to existing 220 CMD and no additional effluent	The received EC is for proposed expansion (phase V) project. The 68 CMD effluent proposed to be generated in phase V expansion will be treated and recycled totally.

S. N.	Para of EC	Details as per EC dated 14 th March, 2022 (From)	To be revised (Read as)	Justification/ Reasons
		and no waste or treated water shall be discharged outside the premises.	shall be discharged from the proposed expansion project. Additional treated effluent from the proposed expansion shall be treated and recycled completely.	
3.	Specific Condition vii	Process organic residue and spent carbon, if any, shall be sent to cement industries.	Process organic residue (distillation residues from Phthalic Anhydride and Maleic Anhydride process) shall be used as fuel in Thermic Fluid Heaters. Spent carbon and process organic residue from tank cleaning, if any, shall be sent to CHWTSDF.	<p>Residue from Distillation: Existing (5467.8 MT/A) and Proposed (1316 MT/A) residue will be generated in Phthalic Anhydride and Maleic Anhydride distillation is utilized as fuel in thermic fluid heaters. The total saving of LSHS/ FO will be 3028 MT/year. Rule 9 (of Hazardous and Other Wastes (M and TM) Rules, 2016) exemption permission obtained from MOEFCC for use of distillation residue vide letter no. 23/47/2017-HSM dt. 19th September 2017. Residue use in thermic fluid heaters is approved by MPCB in the Consent to Operate granted to the unit for the last more than 30 years. Residue is handled (stored and consumed) under totally close system and has to be handled in hot condition (temperature- 150-170 deg C). Considering this, transportation of residue poses a major challenge. The nearest cement plant from the site is 600 km away. Hence, Residue from Distillation are proposed to be utilized as fuel in thermic fluid heaters. Details of residue generation and disposal submitted in EIA report and affidavit letter Ref. no. IGPL/JKS/2022/PA-V dated 11.02.2022.</p> <p>Solids from Residue, Wash Water Tank Cleaning and Spent Carbon Solids Generated from residue and wash water tanks cleaning. Estimated quantity post expansion is 190 MT/A. The generation is infrequent. Spent carbon generation is 93.7 MT/A which is very low. In</p>

S. N.	Para of EC	Details as per EC dated 14 th March, 2022 (From)	To be revised (Read as)	Justification/ Reasons
				existing facility, sent to CHWTSDF (Mumbai Waste Management Ltd.) which is located 4 km away. Disposal to CHWTSDF be allowed as per existing Consent to Operate granted by MPCB. Nearest cement plant is located 600 km away and it is not viable. Details of residue generation and disposal submitted in EIA report and affidavit letter Ref. no. IGPL/JKS/2022/PA-V dated 11.02.2022.
4.	Specific Condition xii	The green belt of 5-10 m width shall be developed in more than 33% of the total project area, mainly along the plant periphery, in downward wind direction, and along road sides etc.	Industry will develop 26% (29064.63 m ²) of the total plot area as greenbelt within the plant premises and 10% additional green belt shall be developed outside plant premises adjacent to the plant within MIDC Industrial area.	The plant has been in existence since 1990-91. Existing green belt area within plot is 12% (13313.45 m ²). 6 m wide road around the plant is mandatory for safety purposes as per MIDC Development Control Rules and DISH requirements under Factories Act, 1941. With optimization within plot, PP proposes to increase green belt area within plot upto 26% (29064.63 m ²). Further optimization within plot is very difficult. Further, PP informed that to develop additional green belt area 10% (10218 m ²) adjacent to the plant within the MIDC Industrial Area. Agreement has been signed with MIDC for tree plantation. This will cover the plant with dense green belt on three sides. Total green belt area within and outside the plant (39282.63 m ²) i.e. 36% of total plot area will be developed.

4. The proposal was considered by the EAC (Meeting ID: IA/IND2/13327/01/09/2022) in its meeting held during 01st - 02nd September, 2022 in the Ministry. After detailed deliberations, EAC recommended the proposal for amendment in EC as proposed by the project proponent at para 3 above subject to the following additional conditions:

- (i) Industry shall obtain prior approval from SPCB for discharge of effluent to CETP. Industry shall discharge 220 KLPD of treated effluent to CETP after achieving the discharge norms specified by the SPCB. Online monitoring system shall be installed and connected to the CPCB and SPCB server.
- (ii) Air emissions from Thermic Fluid Heaters shall be monitored and emission levels shall not exceed the prescribed limit.
- (iii) For outside greenbelt development, PP shall take land for long term lease of 25 years and greenbelt shall be maintained properly.

- (iv) PP shall sensitize and create awareness among the people working within the project area as well as its surrounding area on the ban of Single Use Plastic in order to ensure the compliance of Notification published by MOEFCC on 12th August, 2021. A report along with photographs on the measures taken shall also be included in the six-monthly compliance report being submitted to concerned authority.

5. Based on recommendations of the EAC, the Ministry of Environment, Forest and Climate Change hereby accords approval to the proposed amendments in the environmental clearance dated 14th March, 2022 as stated at paras 3 and 4 above, for the project Proposed expansion of Petrochemical manufacturing facility located at Plot No.: T-2, V-45, V-11 to V-14, T-2/1, T-1, MIDC Taloja, Tehsil: Panvel, Dist.: Raigad, Maharashtra by M/s. IG Petrochemicals Limited. However, all other terms and conditions as mentioned in EC Identification No. EC22A020MH142817 (File No. J-11011/73/2016-IA-II(I)) dated 14th March, 2022 shall remain unchanged.

6. This issues with approval of the competent authority.



(A. N. Singh)
Scientist-'E'

Copy to: -

1. The Secretary, Department of Environment, Government of Maharashtra, Mumbai 400 032
2. The Regional Officer, Ministry of Env., Forest and Climate Change, Integrated Regional Office, Ground Floor, East Wing, New Secretariat Building, Civil Lines, Nagpur- 440001 Maharashtra
3. The Chairman, Central Pollution Control Board Parivesh Bhavan, CBD-cum-Office Complex, East Arjun Nagar, Delhi -32
4. The Member Secretary, Maharashtra Pollution Control Board, Kalpataru Point, 3rd and 4th floor, Opp. Cine Planet, Sion Circle, Mumbai – 22
5. Monitoring Cell, Ministry of Environment, Forest and Climate Change, Indira Paryavaran Bhawan, Jor Bagh Road, New Delhi
6. The District Collector, District Raigad, Maharashtra
7. Guard File/Monitoring File/Parivesh portal/Record File



(A.N. Singh)
Scientist-'E'
E-mail: aditya.narayan@nic.in
Tel. No. 11-24642176

ANNEXURE -XX

SAFETY TRAINING PHOTOS



**FORM V**

(See Rule 14)

Environmental Audit Report for the financial Year ending the 31st March 2023**Unique Application Number**

MPCB-ENVIRONMENT_STATEMENT-0000059865

Submitted Date

26-09-2023

PART A**Company Information****Company Name**

I. G. Petrochemicals Ltd.

Application UAN number

0000115836

Address

I G Petrochemicals Ltd, Plot No T-1& 2, MIDC Industrial Area ,Taloja, Dist- Raigad

Plot no

T- 1, T-2, T-2/1, V-11/12/13/14/45

Taluka

Panvel

Village

Taloja Industrial Area

Capital Investment (In lakhs)

1169.8758

Scale

Large Scale Industry (LSI)

City

Panvel

Pincode

410208

Person Name

Mr. Sagar Jadhav

Designation

Chief - Manufacturing Operations

Telephone Number

2268479103

Fax Number

2227410192

Email

sjadhav@igpetro.com

Region

SRO-Taloja

Industry Category

Red

Industry Type

R57 Petrochemicals Manufacturing (including processing of Emulsions of oil and water)

Last Environmental statement submitted online

yes

Consent Number**Consent Issue Date**

2022-07-02

Consent Valid Upto

2026-08-31

Establishment Year

1992

Date of last environment statement submitted

Jan 1 1900 12:00:00:000AM

Industry Category Primary (STC Code) & Secondary (STC Code)**Product Information****Product Name**

Phthalic Anhydride

Consent Quantity

222110

Actual Quantity

204554.35

UOM

MT/A

Benzoic Acid

1500

816.83

MT/A

Maleic Anhydride

7660

6904.23

MT/A

Di Ethyl Phthalate

12600

4678.00

MT/A

By-product Information**By Product Name**

0

Consent Quantity

0

Actual Quantity

0

UOM

MT/A

Part-B (Water & Raw Material Consumption)

1) Water Consumption in m3/day

Water Consumption for Process	Consent Quantity in m3/day	Actual Quantity in m3/day
Cooling	4776.00	2791.10
Domestic	44.00	25.70
All others	10.00	5.80
Total	5563.00	3251.00

2) Effluent Generation in CMD / MLD

Particulars	Consent Quantity	Actual Quantity	UOM
Daily Quantity of trade effluent from the factory	791	313.1	CMD
Daily Quantity of sewage from the factory	36	24	CMD
Daily quantity of treated effluent	220	193.9	CMD

2) Product Wise Process Water Consumption (cubic meter of process water per unit of product)

Name of Products (Production)	During the Previous financial Year	During the current Financial year	UOM
Phthalic Anhydride	1.12	0.66	CMD
Benzoic Acid	0.0	0	CMD
Maleic Anhydride	0.1	0.1	CMD
DI-Ethyl Phthalate	0	0	CMD

3) Raw Material Consumption (Consumption of raw material per unit of product)

Name of Raw Materials	During the Previous financial Year	During the current Financial year	UOM
o-Xylene	0.923	0.94	Ton/Ton

4) Fuel Consumption

Fuel Name	Consent quantity	Actual Quantity	UOM
LSHS	11325	5977.60	MT/A
HSD(High Speed Diesel)	3942	422.40	MT/A
Distillation Residue	4088	3730.39	MT/A

Part-C

Pollution discharged to environment/unit of output (Parameter as specified in the consent issued)

[A] Water

Pollutants Detail	Quantity of Pollutants discharged (kL/day)	Concentration of Pollutants discharged(Mg/Lit) Except PH,Temp,Colour	Percentage of variation from prescribed standards with reasons	Standard	Reason
	Quantity	Concentration	%variation		
pH	0	7.40	0	5.5 - 9.0	NA
Suspended Solids	6.66	34.30	0	100 mg/l	NA
BOD	5.91	30.50	0	100 mg/l	NA

COD	14.54	75.00	0	250 mg/l	NA
Oil & Grease	0.39	2.00	0	10 mg/l	NA
Total Dissolved Solids	180.65	931.70	0	2100 mg/l	NA
Chloride	33.43	172.40	0	600 mg/l	NA
Sulphate	25.58	131.90	0	1000 mg/l	NA
TAN	0.11	0.60	0	50 mg/l	NA

[B] Air (Stack)

Pollutants Detail	Quantity of Pollutants discharged (kL/day)	Concentration of Pollutants discharged(Mg/NM3)	Percentage of variation from prescribed standards with reasons	Standard	Reason
	Quantity	Concentration	%variation		
Stack - I (Boiler)- TPM	75.85	50.65	0	100 mg/Nm3	NA
Stack - I (Boiler)- SO2	86.96	58.07	0	1700 mg/Nm3	NA
Stack - I (Boiler) - NOX	78.96	52.73	0	450 mg/Nm3	NA
Stack - I (Boiler) - CO	23.22	15.50	0	200 mg/Nm3	NA
Stack - II-A-PA I Heater PM	4.66	51.01	0	100 mg/Nm3	NA
Stack - II-A-PA I Heater SO2	10.11	110.67	0	1700 mg/Nm3	NA
Stack - II-A-PA I Heater NOX	22.86	250.09	0	450 mg/Nm3	NA
Stack - II-A-PA I Heater CO	1.02	11.16	0	200 mg/Nm3	NA
Stack - II-B-PA II Heater PM	5.35	46.36	0	100 mg/Nm3	NA
Stack - II-B-PA II Heater SO2	8.88	76.99	0	1700 mg/Nm3	NA
Stack - II-B-PA II Heater NOX	4.50	39.03	0	450 mg/Nm3	NA
Stack - II-B-PA II Heater CO	1.63	14.14	0	200 mg/Nm3	NA
Stack - III- PA I Scrubber TOC	0.00	0.00	0	150 mg/Nm3	NA
Stack - III- PA I Scrubber PM	59.62	31.26	0	50 mg/Nm3	NA
Stack - III- PA I Scrubber SO2	9.25	4.85	0	850 mg/Nm3	NA
Stack - III- PA I Scrubber NOX	51.35	26.92	0	350 mg/Nm3	NA
Stack - IV- PA II Scrubber TOC	0.00	0.00	0	150 mg/Nm3	NA
Stack - IV- PA II Scrubber PM	47.46	33.56	0	100 mg/Nm3	NA
Stack - IV- PA II Scrubber SO2	12.66	8.95	0	1700 mg/Nm3	NA
Stack - IV- PA II Scrubber NOX	36.54	25.84	0	450 mg/Nm3	NA
Stack - V- PA III Scrubber TOC	0.00	0.00	0	150 mg/Nm3	NA
Stack - V- PA III Scrubber PM	41.73	31.84	0	100 mg/Nm3	NA
Stack - V- PA III Scrubber SO2	9.76	7.45	0	1700 mg/Nm3	NA
Stack - V- PA III Scrubber NOX	41.46	31.63	0	450 mg/Nm3	NA
Stack - VI- PA Dedusting 1 PM	3.37	34.16	0	150 mg/Nm3	NA
Stack - VI- PA Dedusting 1 TOC	0.00	0.00	0	150 mg/Nm3	NA
Stack - VII PA Dedusting 2 PM	3.96	29.45	0	150 mg/Nm3	NA
Stack - VII PA Dedusting 2 TOC	0.00	0.00	0	150 mg/Nm3	NA
Stack - VIII PA Dedusting 3 PM	3.33	35.20	0	150 mg/Nm3	NA
Stack - VIII PA Dedusting 3 TOC	0.00	0.00	0	150 mg/Nm3	NA

Stack - IX MA Bagging PM	0.63	23.75	0	150 mg/Nm ³	NA
Stack - IX MA Bagging TOC	0.00	0.00	0	150 mg/Nm ³	NA
Stack - X MA Flaker PM	0.68	24.88	0	150 mg/Nm ³	NA
Stack - X MA Flaker TOC	0.00	0.00	0	150 mg/Nm ³	NA
Stack - XI- DG- PM	4.19	50.07	0	150 mg/Nm ³	NA
Stack - XI- DG- SO ₂	3.69	44.06	0	1700 mg/Nm ³	NA
Stack - XI- DG- NO _x	3.90	46.53	0	710 mg/Nm ³	NA
Stack - XI- DG- CO	1.26	14.99	0	150 mg/Nm ³	NA
Stack - XII PA 4 Scrubber TOC	0.00	0.00	0	150 mg/Nm ³	NA
Stack - XII PA 4 Scrubber PM	42.05	30.65	0	50 mg/Nm ³	NA
Stack - XII PA 4 Scrubber SO ₂	12.60	9.18	0	850 mg/Nm ³	NA
Stack - XII PA 4 Scrubber NO _x	43.91	32.00	0	350 mg/Nm ³	NA
Stack - XIII PA 4 Heater PM	12.22	52.86	0	100 mg/Nm ³	NA
Stack - XIII PA 4 Heater SO ₂	15.07	65.20	0	1700 mg/Nm ³	NA
Stack - XIII PA 4 Heater NO _x	9.08	39.25	0	450 mg/Nm ³	NA
Stack - XIII PA 4 Heater CO	3.54	15.31	0	200 mg/Nm ³	NA
Stack - XIV PA Dedusting 4 PM	2.72	31.25	0	150 mg/Nm ³	NA
Stack - XIV PA Dedusting 4 TOC	0.00	0.00	0	150 mg/Nm ³	NA
Stack - XV DG 2050 KVA PM	4.48	52.25	0	150 mg/Nm ³	NA
Stack - XV DG 2050 KVA SO ₂	4.12	47.97	0	1700 mg/Nm ³	NA
Stack - XV DG 2050 KVA NO _x	4.26	49.67	0	710 mg/Nm ³	NA
Stack - XV DG 2050 KVA CO	1.36	15.83	0	150 mg/Nm ³	NA

Part-D

HAZARDOUS WASTES

1) From Process

Hazardous Waste Type	Total During Previous Financial year	Total During Current Financial year	UOM
1.2 Tarry residues and still bottoms from distillation	3613.2	3730.39	MT/A
1.6 Spent catalyst and molecular sieves	55.94	23.93	MT/A
5.1 Used or spent oil	16.8	5.2	MT/A
15.2 Discarded asbestos	2.54	0.28	MT/A
33.1 Empty barrels /containers /liners contaminated with hazardous chemicals /wastes	1228	1046	Nos./Y
36.2 Spent carbon or filter medium	9.69	37.86	MT/A
37.2 Ash from incinerator and flue gas cleaning residue	6.25	2.65	MT/A
1.4 Organic residues	110.89	139.38	MT/A
37.3 Concentration or evaporation residues	402.71	521.29	MT/A
37.1 Sludge from wet scrubbers	2.73	0.37	MT/A
33.1 Empty barrels /containers /liners contaminated with hazardous chemicals /wastes	1.82	1.3	MT/A
35.2 Spent ion exchange resin containing toxic metals	0	4.32	Ltr/A

Other Hazardous Waste	19.32	148.51	MT/A
Other Hazardous Waste	0	18.88	MT/A

2) From Pollution Control Facilities

Hazardous Waste Type	Total During Previous Financial year	Total During Current Financial year	UOM
35.3 Chemical sludge from waste water treatment	3.264	4.25	MT/A

Part-E

SOLID WASTES

1) From Process

Non Hazardous Waste Type	Total During Previous Financial year	Total During Current Financial year	UOM
Other debris like insulation, packaging materials etc	44.9	20.97	MT/A

2) From Pollution Control Facilities

Non Hazardous Waste Type	Total During Previous Financial year	Total During Current Financial year	UOM
Biological Sludge from waste water treatment	178.34	103.42	MT/A

3) Quantity Recycled or Re-utilized within the unit

Waste Type	Total During Previous Financial year	Total During Current Financial year	UOM
1.2 Tarry residues and still bottoms from distillation	3611.51	3730.39	MT/A

Part-F

Please specify the characteristics(in terms of concentration and quantum) of hazardous as well as solid wastes and indicate disposal practice adopted for both these categories of wastes.

1) Hazardous Waste

Type of Hazardous Waste Generated	Qty of Hazardous Waste	UOM	Concentration of Hazardous Waste
1.2 Tarry residues and still bottoms from distillation	3728.7	MT/A	Viscous (Disposal - Use as fuel heater)
1.6 Spent catalyst and molecular sieves	23.93	MT/A	Solid (Disposal - Sent to CHWTSDF)
5.1 Used or spent oil	5.2	MT/A	Liquid (Disposal - Sale CPCB / MPCB authorized parties Liquid (Disposal - Sale CPCB / MPCB authorized parties)
15.2 Discarded asbestos	0.28	MT/A	Solid (Disposal - Sent to CHWTSDF)
33.1 Empty barrels /containers /liners contaminated with hazardous chemicals /wastes	1046	Nos./Y	Solid (Disposal - Sent to CHWTSDF)
36.2 Spent carbon or filter medium	37.86	MT/A	Solid (Disposal - Sent to CHWTSDF)
35.3 Chemical sludge from waste water treatment	4.201	MT/A	Solid (Disposal - Sent to CHWTSDF)
37.2 Ash from incinerator and flue gas cleaning residue	2.65	MT/A	Solid (Disposal - Sent to CHWTSDF)
1.4 Organic residues	139.38	MT/A	Solid (Disposal-Sent to CHWTSDF) Solid (Disposal-Sent to CHWTSDF)
37.3 Concentration or evaporation residues	522.02	MT/A	Solid (Disposal-Sent to CHWTSDF) Solid (Disposal-Sent to CHWTSDF)

37.1 Sludge from wet scrubbers	0.37	MT/A	Solid (Disposal-Sent to CHWTSDF) Solid (Disposal-Sent to CHWTSDF)
35.2 Spent ion exchange resin containing toxic metals	4.32	Ltr/A	Solid (Disposal-Sent to CHWTSDF) Solid (Disposal-Sent to CHWTSDF)
Other Hazardous Waste	148.51	MT/A	Solid (Disposal-Sent to CHWTSDF) Phthalic Acid Solid (Disposal-Sent to CHWTSDF) Phthalic Acid
Other Hazardous Waste	18.88	MT/A	Solid (Disposal-Sent to CHWTSDF) Sodium Sulphate Solid (Disposal-Sent to CHWTSDF) Sodium Sulphate
33.1 Empty barrels /containers /liners contaminated with hazardous chemicals /wastes	1.3	MT/A	Solid (Disposal-Sent to CHWTSDF) Discarded bags used for hazardous chemicals

2) Solid Waste

Type of Solid Waste Generated	Qty of Solid Waste	UOM	Concentration of Solid Waste
Other debris like insulation, packaging materials etc	20.97	MT/A	Solid (Disposal-Sent to CHWTSDF) Solid (Disposal-Sent to CHWTSDF)
Biological Sludge from waste water treatment	103.42	MT/A	Solid (Disposal-Sent to CHWTSDF) Solid (Disposal-Sent to CHWTSDF)

Part-G

Impact of the pollution Control measures taken on conservation of natural resources and consequently on the cost of production.

Description	Reduction in Water Consumption (M3/day)	Reduction in Fuel & Solvent Consumption (KL/day)	Reduction in Raw Material (Kg)	Reduction in Power Consumption (KWH)	Capital Investment(in Lacs)	Reduction in Maintenance(in Lacs)
RO Permeate Reused	87.78	0	0	0	0	0

Part-H

Additional measures/investment proposal for environmental protection abatement of pollution, prevention of pollution.

[A] Investment made during the period of Environmental Statement

Detail of measures for Environmental Protection	Environmental Protection Measures	Capital Investment (Lacks)
Partial ZLD	Efficient treatment provided.	0

[B] Investment Proposed for next Year

Detail of measures for Environmental Protection	Environmental Protection Measures	Capital Investment (Lacks)
Optimization of Cooling Tower blowdown.	Electrolytic system provided.	50

Part-I

Any other particulars for improving the quality of the environment.

Particulars

NA

Name & Designation

Mr. Sagar Jadhav - Chief Manufacturing Operation



UAN No:

MPCB-ENVIRONMENT_STATEMENT-0000059865

Submitted On:

ANNEXURE – XXII

IGPL WEBSITE SNAPSHOTS

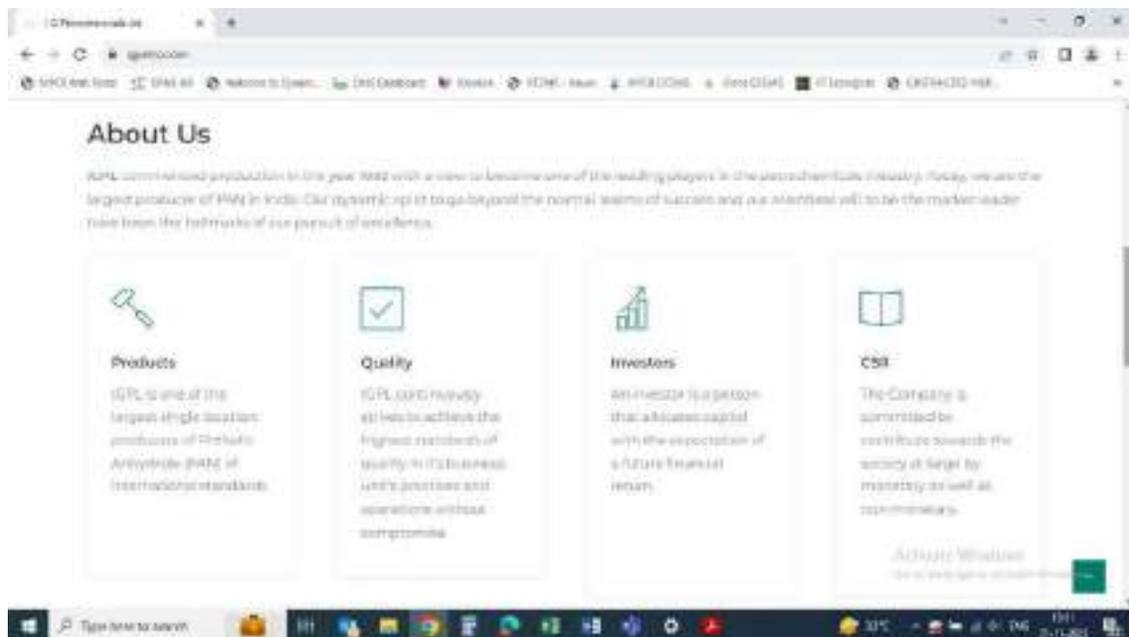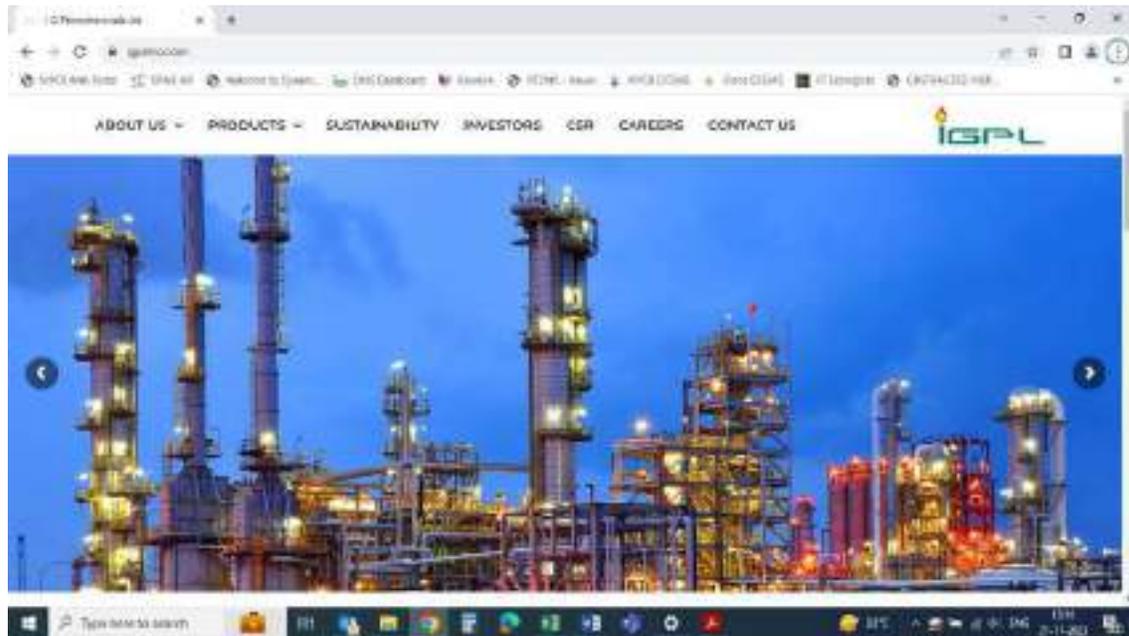

Quality Management Systems

The primary goal of IQPS is to achieve the highest standards of quality in our business units practices and operations without compromise. Quality performance is one of the cornerstones of our Company's culture and is considered a personal responsibility of all employees. IQPS is an ISO accredited Company in respect of the following standards:-

ISO 9001:2015 - Quality Management Systems

ISO 14001:2015 - Environmental Management System

ISO 45001:2018 - Occupational Health and Safety Management System

Ensuring that we fully identify and conform to the needs of our customers. To fulfil and exceed customer needs and expectations by delivering a quality product in a consistent and timely manner. Continuous improvement in our process. IQPS management is fully committed to the Quality Policy through active participation in quality improvement activities.

Activate Windows
Go to Settings to activate Windows.

Quality Management Systems

The primary goal of IQPS is to achieve the highest standards of quality in our business units practices and operations without compromise. Quality performance is one of the cornerstones of our Company's culture and is considered a personal responsibility of all employees. IQPS is an ISO accredited Company in respect of the following standards:-

ISO 9001:2015 - Quality Management Systems

ISO 14001:2015 - Environmental Management System

ISO 45001:2018 - Occupational Health and Safety Management System

Ensuring that we fully identify and conform to the needs of our customers. To fulfil and exceed customer needs and expectations by delivering a quality product in a consistent and timely manner. Continuous improvement in our process. IQPS management is fully committed to the Quality Policy through active participation in quality improvement activities.

Activate Windows
Go to Settings to activate Windows.



ANNEXURE-XXIII

2/10/18

IG PETROCHEMICALS LIMITED

Ref : IGPL/JKS/2018

Date : 08.10.2018

Parvel Municipal Corporation,
Parvel,
Dist. Raigad : 410206
Maharashtra

Dear Sir,

We are enclosing herewith copy of Environmental Clearance issued vide F.No.J-11011/73/2016-IA-II (I) dtd. 18.07.2017 by Ministry of Environment, Forest and Climate Change (MoEFCC), Government of India, New Delhi alongwith amendment to the Environmental Clearance issued Ministry of Environment, Forest and Climate Change (MoEFCC), Government of India, New Delhi dtd. 20.02.2018 for your kind information and records.

Please acknowledge having received the same.

Thanking you,

Yours faithfully,
For I G PETROCHEMICALS LIMITED

(JK SABOO)
EXECUTIVE DIRECTOR

Encl : As above

2/10/18
लेखनिक
भावक-जावक
पनवेल शहर महानगरपालिका
पनवेल - रायगड.

ANNEXURE-XXIV

PHOTOS OF PA – IV AND DEP PLANT

HEATER



DISTILLATION



STORAGE TANKS



DEP PLANT



ANNEXURE - XXV

MEE PLANT-



ETP MCC PANEL ROOM-



TRICKLING FILTER-



MGF AND ACF-



UF-



RO-1-



RO- 2-



TRICKLING FILTER MCC



UF AND RO BUILDING-



ANNEXURE - XXVI

TREE SURVIVAL REPORT PLANTED AT NITLAS & GHOT CAMP-












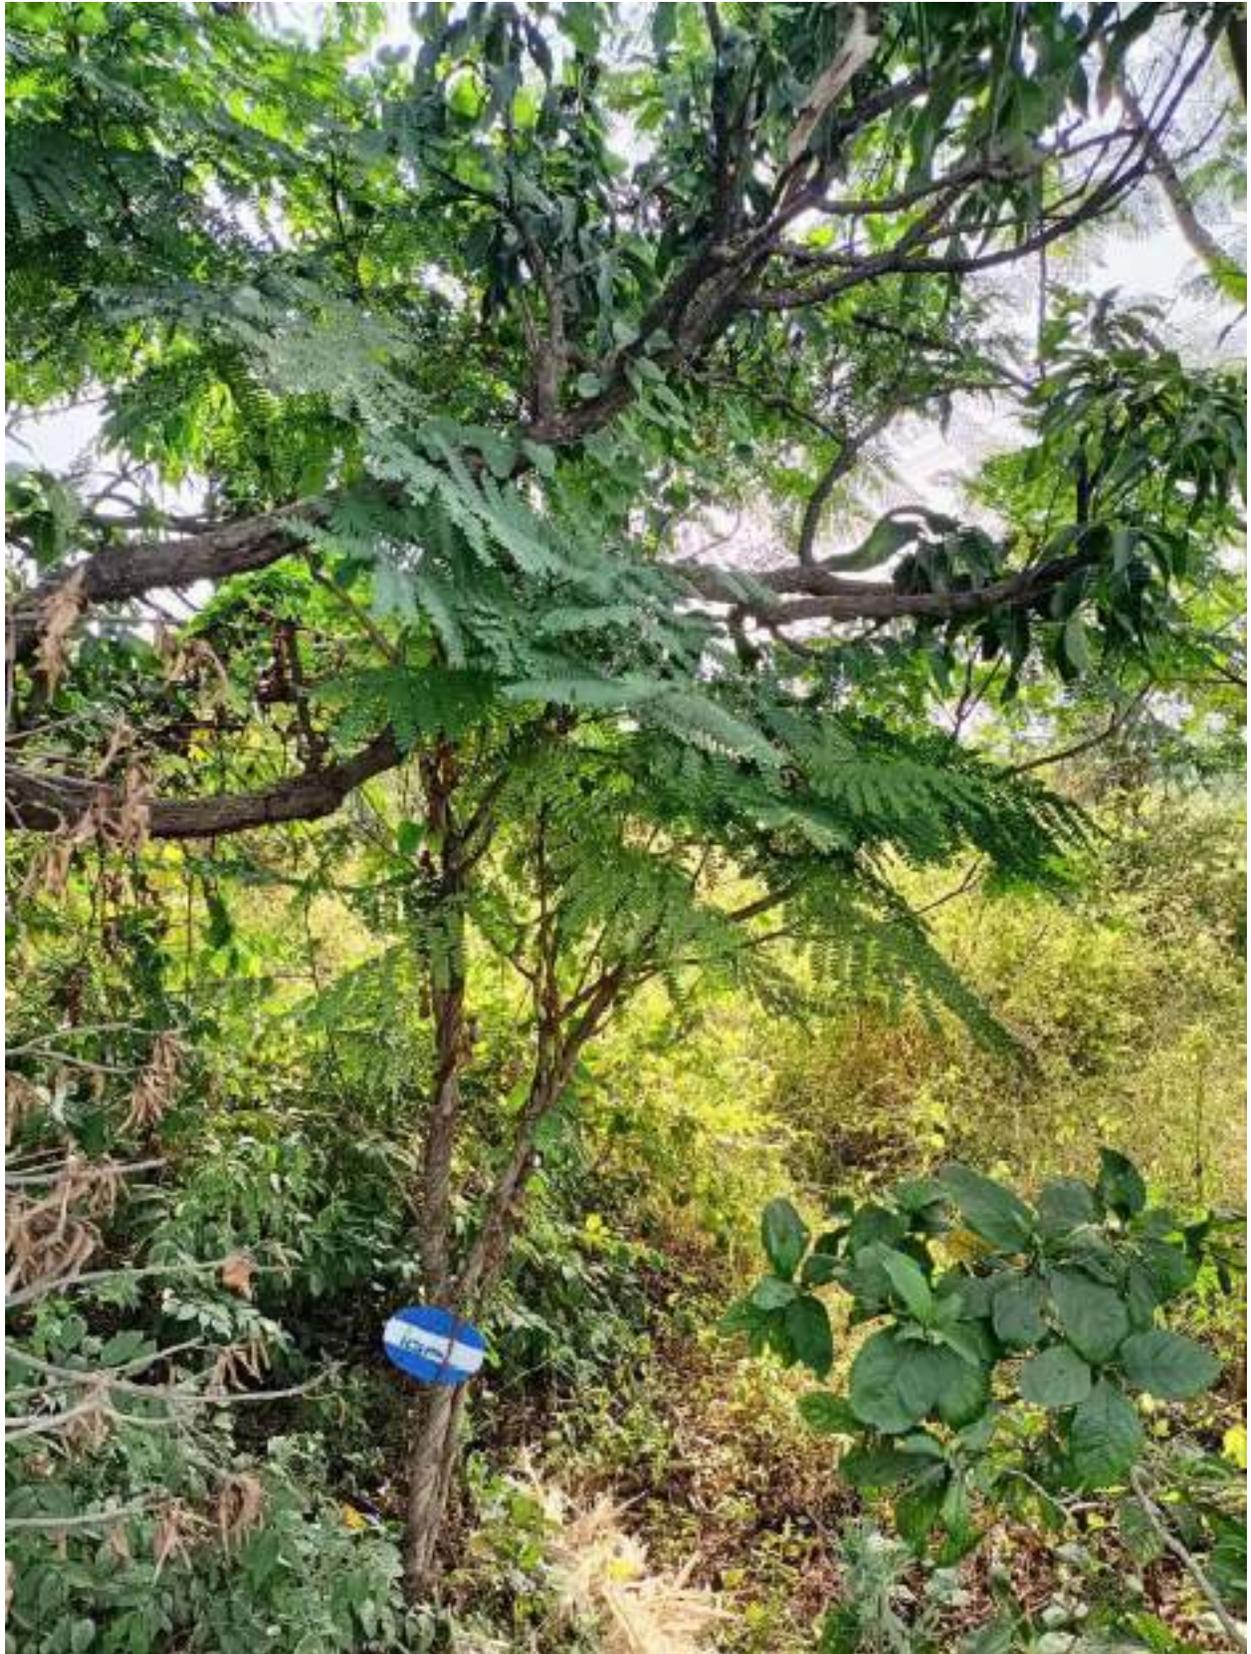



CIDCO / RAMKY ROAD













MIYAWAKI FOREST –





